

WORK INTERGRATED LEARNING

Web Vortex and Mr Auto&Turbo

BUSINESS DETAILS

Mr. Motlokoa Tsotesi, Manager & Mechanic - Mister Auto & Turbo

Group members

224099468 LE LETSIE
223013773 NM NETSHITUKA
219002738 LTBG PULE
222066543 RG MADI
215135458 LE LIPALI

PHASE 1: Planning, Requirements Analysis, Feasibility and Risk Analysis

Project Introduction

In research , we recognized that there was a need for websites that had all the necessary information for car services. Even much larger companies did not have a system that allowed you to track the progress of your car until collection and it generally made it difficult for people to be informed and understand costs where some felt like services were overpriced and there was a lack of communication. This made people feel anxious and often unsure if they were truly getting what they were paying for and for people that looked for car services, they could not compare properly, as so many did not have social media presence or web based information especially for those without insurance because they cannot afford it. Our aim was to start a trend that would support local businesses in a more digital manner and create an environment of transparency between the business and client.

3. Problem Statement

Current situation: Mister Auto & Turbo currently manages customer intake, job cards, quotations and repair tracking using largely manual, paper-based methods, and has no online presence beyond wordof-mouth referrals.

Problem: Customers have no way to check a vehicle's repair progress without phoning the workshop directly, there is no fixed or published pricing for common services, and there is no clear breakdown of cost differences when a customer supplies their own part instead of the business sourcing it. This leads to repeated interruptions, pricing disputes and difficulty attracting new customers without an online presence.

Affected users: Customers experience poor visibility into repair progress and pricing uncertainty; reception and mechanics are repeatedly interrupted by status-check calls and price negotiations; the manager/owner lacks a way to reach new customers online and lacks centralised business records.

Consequences: Frequent phone interruptions during active repair work, recurring disputes over pricing and discounts, missed opportunities to attract new customers, and no centralised repair history for returning customers.

Need for improvement: A digital system is needed to give customers visibility into repair status without phoning in, present clear itemised pricing (including customer-supplied part discounts), and centralise vehicle and customer records.

4. Project Process Aim and Objectives

Aim: To design and develop an integrated Vehicle Service Management System that digitises the vehicle servicing lifecycle for Mister Auto & Turbo, improving record-keeping, communication and operational visibility.

Objectives:

- Replace paper-based job cards with a digital job card and status-tracking system.
- Provide customers with visibility of their vehicle's status via a mobile application.
- Provide reception, mechanics and management with role-appropriate dashboards for their tasks.
- Centralise customer, vehicle, quotation and payment records in a shared backend.
- Deliver a working prototype that has been validated against the stakeholder's actual process by the end of Phase

5. Project Scope

STAKEHOLDER COOPERATION & INFORMATION USE AGREEMENT

Academic Student Project - Central University of Technology, Free State

This Agreement is entered into between the parties named below for the purpose of an academic student project conducted as part of the module ITC327W (Work-Integrated Learning), Diploma in Information Technology, Central University of Technology.

1. The Parties

Stakeholder / Business Representative

Name:
Motlokoa Tsoetsi

Business name:
Mister Auto and Turbo

Position:
Managing Director

Contact details (phone number):
073 002 4579

Email address:
csolotsi.motloton@yahoo.com

Student Group Representative initials and student numbers

224099468 LE LETSIE
215135458 LE LIPALI
219002738 LTBG PULE
223013773 NM NETSHITUKA
222066543 RG MADI

---

2. Purpose of the Project

The student group is developing, as part of their academic assessment, a proposed Vehicle Service Management System intended to support the Stakeholder's day-to-day vehicle servicing operations (customer intake, job cards, quotations, repair tracking, payments, and vehicle collection). The purpose of this Agreement is to confirm what information the Stakeholder voluntarily participates and to set out, in writing, what information will be collected, how it will be used, and what the student group will provide in return.

---

3. What the Students Will Collect

With the Stakeholder's cooperation, the student group may collect the following, strictly for the purposes of this academic project:

• A description of the Stakeholder's current business process and workflow.
• Information about the roles of staff involved in that process (e.g. reception, mechanics, management).
• The Stakeholder's requirements and preferences for a proposed digital system.
• Feedback on draft requirements, mock-ups, or prototypes.
• General, non-identifying examples of the type of data the business handles (e.g. what fields a job card typically contains), rather than actual customer records where avoidable.

---

4. What the Students Will NOT Do

• The students will not request or record sensitive personal information about the Stakeholder's customers or staff beyond what is reasonably necessary to understand the business process.
• The students will not publish any confidential business information, pricing, customer data, or credentials in any public location.
• The students will not use any information gathered for any purpose beyond this academic module and its assessment and presentation requirements.

---

5. What the Stakeholder Agrees To

• Making themselves reasonably available for a limited number of meetings, interviews, or written communications during the semester.
• Providing honest and accurate information about their current process to the best of their ability.
• Reviewing and confirming, in writing (email, WhatsApp, or meeting notes signed off), the requirements gathered so the students have documented evidence for their assessment.
• Understanding that participation is voluntary and can be withdrawn at any time by notifying the student group and their module supervisor.

---

6. What the Students Provide in Return

In exchange for the Stakeholder's time and cooperation, the student group will provide the Stakeholder with a working prototype/solution developed during the module, at no cost, for the Stakeholder's own use.

• The solution is developed as a student learning exercise and is provided "as is," without any guarantee of ongoing support, maintenance, hosting, or further development beyond the academic module, unless separately agreed in writing.
• The Stakeholder understands this is a prototype developed for assessment purposes and may not include all features of a full commercial system.
• Any continued use, hosting, or support arrangement after the module ends is a separate matter to be agreed between the parties directly, and is not a requirement of this Agreement.

---

7. Confidentiality & Data Handling

The student group agrees to handle any information shared by the Stakeholder responsibly and in line with their institution's academic integrity requirements. Where actual customer or business data is shared for reference, it will be used only to inform system design (e.g. field names, workflow steps) and will not be reproduced or published without the Stakeholder's consent.

---

8. Acknowledgement

Both parties confirm that they understand and voluntarily agree to the terms set out above. This Agreement is intended to document good-faith cooperation for academic purposes and does not create a commercial contract, employment relationship, or ongoing service obligation between the parties.

Signed:

Stakeholder signature: _____

Date: 25/08/2026

Print name: Motlokoa Tsoetsi

Student representative surnames and signatures:

224099468 LE LETSIE

215135458 LE LIPALI

219002738 LTBG PULE

223013773 NM Netshituka

Date: ___/08/21/2026

Note: This is a plain-language cooperation agreement for academic purposes, not a legal contract drafted by a lawyer. If the Stakeholder wishes to formalise this further, they are welcome to have it reviewed before signing.

6.Deliverables And Acceptance Criteria

-Deliverables

- Customer and vehicle registration.
- Digital job card creation and status tracking.
- Quotation creation and customer approval workflow.
- Repair tracking through to quality check and collection.
- Payment recording.
- Role-based dashboards for customer, reception/admin, mechanic and manager/owner.

-Acceptance Criteria

- A customer can register, view their vehicle's job status, and receive a notification when it is ready.
- A staff member can create a job card, record diagnosis/quotation, and update status through to collection.
- A manager can view a basic report of jobs and payments.

7.Exclusions, Constraints And Assumptions

-Exclusions (Out of Scope for Phase 1)

- Full supplier/parts ordering and stock management integration.
- SMS notifications (in-app and email only for this phase).
- Full accounting/bookkeeping integration.
- A full public marketing website or SEO/social-media management tools — the customer-facing mobile/web login provides the business some online presence as a secondary benefit, but building out marketing reach is not a function of this system.

-Constraints

- Delivery within the academic semester timeframe.
- Group members' current skill level in Flutter, ASP.NET and Supabase.
- No project budget beyond free-tier tools and services.

-Assumptions

- The stakeholder will remain available for periodic engagement throughout the project.
- The stakeholder has basic smartphone/computer access for demonstration and feedback purposes

8. Stakeholders and User Groups

Organisation: Mister Auto & Turbo ,a vehicle repair and turbo servicing business located at

No. 5, 123 Constantia Road, Dagbreek, Welkom, 9459, Free State, South Africa.

Primary stakeholder: Mr. Motlokoa Tsotesi Manager, who also works as a mechanic in the business himself.

8.1 User Groups

- Customers - vehicle owners bringing vehicles in for service or repair.
- Reception/admin staff - handle intake, job cards and customer communication.
- Mechanics - perform inspection, diagnosis and repair work.
- Manager/Owner - oversees operations, pricing and business decisions.
- Developers – override critical system functionality.

8.2 Stakeholder Needs

This section records needs identified directly from stakeholder engagement with Mr. Motlokoa Tsotesi (Manager & Mechanic, Mister Auto & Turbo). Findings below are drawn from stakeholder discussion; formal written confirmation (WhatsApp/meeting notes) is attached as Appendix A.

- SN-01: The stakeholder needs customers to be able to check a vehicle's repair progress without phoning the workshop, since check-in calls interrupt workshop staff during active repair work.
- SN-02: The stakeholder needs a clear, fixed price reference for common services and parts, to reduce on-thespot negotiation and requests for discounts.
- SN-03: The stakeholder needs quotations to clearly show the price difference between the business supplying a part (e.g. a battery) versus the customer supplying their own part, since this is a recurring source of pricing disputes.
- SN-04: The stakeholder relies almost entirely on word-of-mouth referrals and currently has no website, which limits his ability to reach new customers. A customer-facing mobile/web presence would indirectly support this, though a full marketing website is outside the scope of this system (see Section 7.1, Exclusions).

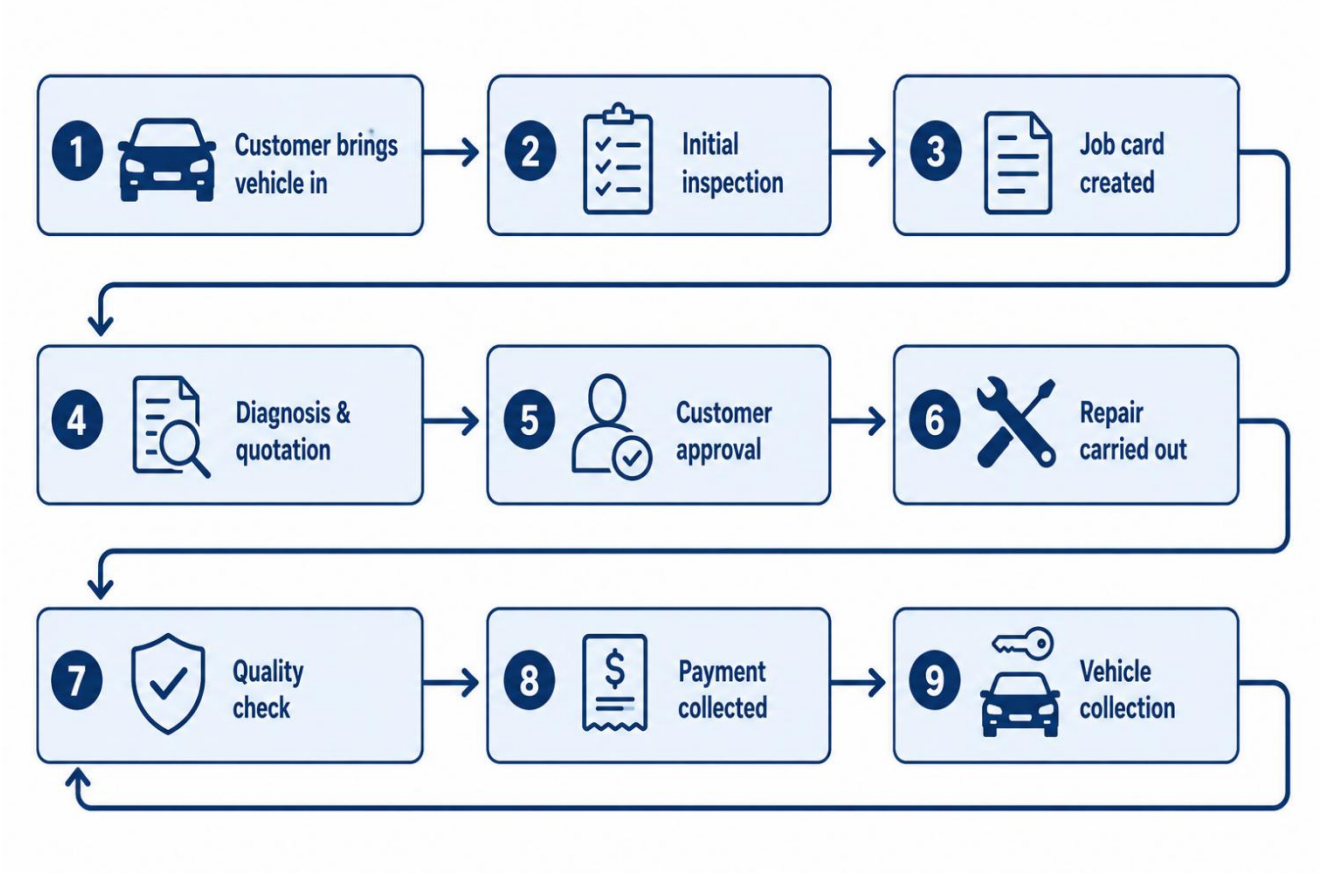
SN-05: The stakeholder needs a record of past repairs per vehicle for reference on repeat customers

9. Current Process and Diagram

Based on stakeholder engagement, the current process typically follows these steps:

- Customer brings the vehicle in, describing the issue or requesting a scheduled service.
- A staff member or mechanic performs an initial inspection.
- A job card is created, usually on paper, recording the vehicle and reported issue.
- The mechanic diagnoses the fault and prepares a quotation for parts and labour.
- The customer is contacted to approve the quotation before work proceeds.
- The repair is carried out.

- A quality check confirms the work is complete and correct.
- Payment is collected.
- The customer collects the vehicle.
- Reviews from Customers



9.1 Problems with the Current Process

- Job cards and records are paper-based and can be lost or misplaced.
- No way for customers to track a vehicle's repair progress remotely customers call in regularly to check status, this interrupts workshop staff.
- No fixed, published price list for common services and parts, which leads to friction with customers negotiating for discounts on the spot.
- No clear breakdown of cost differences when a customer supplies their own part versus the business supplying it (e.g. customer-supplied battery vs. shop-supplied battery), leading to disputes over pricing.
- The business relies almost entirely on word-of-mouth referrals; until recently it had no social media presence and still has no website, making it difficult to reach new customers.
- Repair history is not centrally stored, making it hard to reference past work on a vehicle.

10. Product Perspective

The **Vehicle Service Management System (VSMS)** is a new standalone software solution developed for **Mister Auto & Turbo** to digitise and streamline the vehicle servicing process. The system is intended to replace the current paper-based methods used for job cards, repair tracking, quotations, and customer communication.

The product will provide a centralized platform for managing customer, vehicle, repair, quotation, and payment information. It will serve as a bridge between customers and workshop staff by improving transparency and communication throughout the repair lifecycle.

Unlike the current process, where customers must contact the workshop directly for updates, the proposed system will allow customers to track the status of their vehicles in real time through a mobile or web application. Staff members will be able to update repair progress digitally, while management will be able to monitor operations through administrative dashboards and reporting features.

User Role	**Purpose**
Customer	View vehicle status, quotations, notifications and repair history.
Reception/Admin	Register customers and vehicles, create job cards and manage quotations.
Mechanic	Update diagnoses, repair progress and job statuses.
Manager/Owner	View reports, monitor jobs, manage pricing and operations.
Developer	Maintain and manage critical system functionality.

11. Main Flutter, ASP.NET And Supabase

The system will consist of multiple application components that work together to provide services to customers and workshop staff.

The main components of the system will include:

- A **Flutter customer application**, consisting of a user interface and Flutter application logic for customer-related functionality.
- An **ASP.NET MVC staff application**, consisting of a user interface and MVC application logic for mechanics and other authorised workshop staff.

- An **ASP.NET Web API**, responsible for providing API services and managing communication with the Supabase cloud services where required.
- **Supabase**, responsible for cloud database services, authentication, real-time functionality, and cloud storage.

The customer and staff applications will access the appropriate system services and communicate with Supabase according to the system architecture and authorised access rules.

11.1 Flutter Customer Application

Flutter will be used to develop the customer-facing application across supported mobile and web platforms.

The Flutter application will provide the customer user interface and application functionality required for customers to interact with the vehicle service and repair management system.

Customer Registration and Authentication

The system shall allow customers to:

- Register a new customer account.
- Log into their account.
- Recover or reset their password.
- Securely access authorised customer functionality.

Customer Profile Management

The system shall allow customers to:

- View their personal profile information.
- Update permitted personal information.
- View their registered vehicles.

Vehicle Management

The system shall allow customers to:

- Register vehicles.
- View registered vehicle information.
- View vehicle service and repair status.
- View vehicle repair history.

Job and Repair Tracking

The system shall allow customers to:

- View the current status of their vehicle service or repair.
- Track the progress of active repairs.
- Receive updated information when the status of a repair changes.

Quotations and Approvals

The system shall allow customers to:

- View quotations generated for their vehicles.
- View requests requiring customer approval.
- Approve or reject quotations where authorised.
- View quotation approval status.

Payment Information

The system shall allow customers to:

- View payment information.
- View payment history.
- Submit or upload proof of payment where required.

Notifications

The system shall allow customers to receive notifications regarding:

- Changes to vehicle repair status.
- Quotation requests.
- Approval requests.
- Vehicle collection availability.
- Other relevant service updates.

11.2 ASP.NET MVC Staff Application

ASP.NET MVC will be used to develop the workshop staff-facing application.

The ASP.NET MVC application will provide both the user interface and MVC application logic required by mechanics, reception staff, administrators, and managers.

Access to functionality shall be controlled according to the user's authorised role.

Reception and Administration Functions

The system shall allow authorised reception and administration staff to:

- Register customers.
- Register customer vehicles.
- Create and manage digital job cards.
- Record customer complaints.
- Record vehicle service and repair requests.
- Generate quotations.
- Record customer quotation approvals.
- Record payments.
- Manage vehicle collection records.

Mechanic Functions

The system shall allow mechanics to:

- View assigned jobs.
- View job card information.
- Record vehicle inspection details.
- Record diagnosis details.
- Update repair progress.
- Update the status of assigned jobs.
- Add notes regarding inspections and repairs.

The system shall support the following job statuses:

- Inspection
- Quotation
- In Progress
- Quality Check
- Ready for Collection
- Collected

Manager Functions

The system shall allow authorised managers to:

- View active jobs.
- View completed jobs.
- Monitor workshop performance.
- View payment records.
- Generate basic reports.
- Manage pricing information.
- View customer records.
- View vehicle records.
- Monitor job progress across the workshop.

11.3 Flutter Application Services

The Flutter application shall contain the application logic required to support customer-facing functionality.

These services may include functionality for:

Customer Account Services

- Managing customer registration processes.
- Managing customer login sessions.
- Managing customer profile information.
- Handling password recovery processes.

Vehicle Services

- Managing vehicle registration.
- Retrieving customer vehicle information.

- Retrieving vehicle service and repair history.

Job Tracking Services

- Retrieving vehicle job information.
- Retrieving repair progress.
- Processing customer-facing job status information.
- Providing current vehicle service information.

Quotation and Approval Services

- Retrieving customer quotations.
- Displaying approval requests.
- Processing authorised customer approval decisions.
- Retrieving quotation status information.

Notification Services

- Receiving customer notifications.
- Processing vehicle status updates.
- Displaying relevant service notifications.

11.4 ASP.NET MVC Application Services

The ASP.NET MVC application shall contain the server-side and application logic required to support workshop staff operations.

Authentication and Authorisation

The system shall:

- Validate authorised staff access.
- Apply role-based access control.
- Restrict access to functionality based on user roles.
- Manage authorised user sessions.

Job Card Management

The system shall:

- Create job cards.
- Update job card information.
- Retrieve job details.
- Assign jobs to authorised staff where required.
- Maintain repair history records.

Inspection and Repair Management

The system shall:

- Store inspection information.
- Store vehicle diagnosis information.
- Record repair progress.
- Update vehicle job status.
- Store mechanic notes.

Quotation Management

The system shall:

- Create quotations.
- Calculate labour costs.
- Calculate parts costs.
- Calculate quotation totals.
- Calculate differences when customers provide their own parts.
- Maintain quotation approval status.

Payment Management

The system shall:

- Record payments.
- Store proof of payment information.
- Maintain payment history.

Reporting Services

The system shall:

- Generate job reports.
- Generate payment summaries.
- Generate customer activity reports.
- Provide workshop performance information.

11.5 ASP.NET Web API

The ASP.NET Web API shall provide API functionality and services for communication between the system applications and Supabase.

The API shall expose authorised endpoints for system operations where API-based communication is required.

API Services

The ASP.NET Web API shall provide services for:

- Retrieving authorised system data.
- Processing authorised data requests.
- Managing business operations.
- Validating requests.
- Managing communication with Supabase services.
- Providing structured responses to authorised application components.

Authentication and Security

The API shall:

- Validate authorised requests.
- Enforce appropriate access controls.
- Prevent unauthorised access to protected resources.
- Secure communication between application components.

Business Logic

The API shall handle business operations that require centralised processing, including:

- Job-related operations.
- Quotation calculations.
- Payment processing.
- Reporting operations.
- Notification-related operations.

11.6 Supabase Cloud Services

Supabase will provide the cloud services required for data persistence, authentication, real-time functionality, and file storage.

The Flutter customer application and the ASP.NET MVC staff application shall communicate with Supabase services according to the approved system architecture and security requirements.

The ASP.NET Web API shall also communicate with Supabase when API-based data access or centralised business processing is required.

12.Functional Requirements

Requirements are typed and prioritised per module convention:

Functional (FR); priority Must Have.

• FR-01 Customer registration

The system shall allow customers to register an account with their name, contact details and vehicle information.

• FR-02 Vehicle registration

The system shall allow staff to register a vehicle against a customer record.

• FR-03 Digital job cards

The system shall allow staff to create a digital job card capturing the reported issue and inspection notes.

• FR-04 Diagnosis and quotation generation
The system shall allow a mechanic to record a diagnosis and generate a quotation.

• FR-05 Customer approval workflow
The system shall require customer approval of a quotation before repair work is marked as started.

• FR-06 Repair status tracking
The system shall allow a mechanic to update repair status through defined stages (e.g. In Progress, Quality Check, Ready for Collection), so customers can check progress without phoning the workshop.

• FR-07 Payment recording
The system shall allow staff to record a payment against a job card.

• FR-8 Notifications
The system shall send an in-app and/or email notification to the customer when their vehicle's status changes to "Ready for Collection", reducing status-check phone calls.

• FR-9 Itemised quotations
The system shall display an itemised quotation that separates labour cost from parts cost.

• FR-10 Customer-supplied part comparison
The system shall allow a quotation to show a reduced price where a customer supplies their own part instead of the business supplying it, with both amounts visible for comparison.

13.Non-Functional Requirements

NFR-01: Performance

- The system shall respond to user requests within **3 seconds** under normal operating conditions.
- Customer registration, vehicle registration, job card creation, quotation generation, and payment recording shall be completed without noticeable delay.
- Vehicle status updates shall be available to customers within **5 seconds** of a mechanic updating the status.

NFR-02: Availability

- The system shall be available **99% of operating hours** excluding planned maintenance.
- Customers shall be able to access vehicle progress information at any time when internet connectivity is available.
- Notification services shall be operational whenever the system is available.

NFR-03: Security

- All users shall authenticate before accessing protected system features.
- Customer, vehicle, quotation, and payment information shall only be accessible to authorized users.
- Passwords shall be encrypted before storage.
- Communication between Flutter, ASP.NET, and Supabase shall use secure HTTPS connections.

NFR-04: Usability

- The system shall provide a simple and intuitive interface requiring minimal training.
- Customers shall be able to locate vehicle status information within three navigation steps.
- System screens shall maintain a consistent design throughout the application.

NFR-05: Reliability

- The system shall accurately store and retrieve all job cards, quotations, and payment records.
- No customer, vehicle, or repair information shall be lost during normal system operation.
- Data shall remain consistent across all user roles.

NFR-06: Maintainability

- The application shall be developed using a modular architecture to simplify future enhancements.
- Code shall be documented to support future maintenance and upgrades.
- Errors and exceptions shall be logged for troubleshooting purposes.

NFR-07: Scalability

- The system shall support growth in the number of customers, vehicles, job cards, and quotations without requiring significant redesign.
- The database shall allow future expansion to support additional workshop branches.

NFR-08: Compatibility

- The customer application shall run on Android devices.
- The web version shall support Google Chrome, Microsoft Edge, and Mozilla Firefox.
- The system shall function correctly across different screen sizes.

NFR-09: Notification Delivery

- Email and in-app notifications shall be delivered within **one minute** of a vehicle status changing to "Ready for Collection".
- Notification failures shall be recorded in system logs for administrative review.

NFR-10: Data Accuracy and Transparency

- Quotations shall display labour and parts costs clearly and accurately.
- Any discount resulting from customer-supplied parts shall be calculated automatically.
- Cost calculations shall remain consistent across all quotations.

14. System Requirements

14.1 Hardware Requirements

-Client Devices

- Android smartphone or tablet.
- Desktop or laptop computer.
- Stable internet connection.

-Server Requirements

Since the project uses cloud-hosted services:

- Cloud-hosted ASP.NET backend.
- Supabase cloud database.
- Internet connectivity for all users.

14.2 Software Requirements

Development Environment

- Flutter SDK
- Visual Studio 2022
- .NET 8 or later
- Supabase Account
- GitHub Version Control

Client Software

- Android Operating System
- Web Browser (Chrome, Edge, Firefox)

15. Integration Requirements

The Vehicle Service Management System consists of three primary technology components that must integrate seamlessly.

15.1 Flutter and ASP.NET Integration

Purpose

To allow user interfaces to communicate with business logic and application services.

Integration Requirements

- Flutter shall send API requests to ASP.NET.
- ASP.NET shall return responses in JSON format.
- User authentication requests shall be processed through ASP.NET.
- Job card, quotation, and status update requests shall be transmitted securely.

15.2 ASP.NET and Supabase Integration

Purpose

To connect business logic with cloud-hosted data storage.

Integration Requirements

- ASP.NET shall perform Create, Read, Update, and Delete (CRUD) operations on Supabase.
- ASP.NET shall retrieve customer, vehicle, quotation, repair, and payment information from Supabase.
- ASP.NET shall validate and process data before database storage.
- ASP.NET shall interact with Supabase Authentication services for user management.

15.3 Flutter and ASP.NET Integration

Purpose

To support authentication and real-time updates where required.

Integration Requirements

- Flutter shall receive real-time vehicle status updates from Supabase.
- Flutter shall authenticate users through Supabase authentication services.
- Flutter shall retrieve user-specific information based on access permissions.

15.4 Email Notification Integration

Purpose

To notify customers of important service events.

Integration Requirements

- The system shall send email notifications when:
    - A quotation is ready for approval.
    - A quotation is approved or rejected.
    - Vehicle status changes occur.
    - The vehicle is ready for collection.

16. Requirements Prioritisation

The MoSCoW prioritisation technique was used to rank requirements according to their importance for Phase 1 delivery.

Must Have Requirements

These requirements are essential for the system to operate and meet stakeholder needs.

Requirement ID	**Description**
FR-01	Customer account registration
FR-02	Vehicle registration against customer records
FR-03	Digital job card creation

FR-05	Mechanic diagnosis and quotation generation
FR-06	Customer quotation approval workflow
FR-07	Repair status tracking and updates
FR-09	Payment recording
FR-10	Ready-for-collection notifications
FR-14	Itemised quotations showing labour and parts costs
FR-15	Display of pricing differences for customer-supplied parts

Should Have Requirements

These requirements add significant value but are not critical to the basic operation of the system.

Requirement ID	**Description**
FR-04	Search and retrieval of customer and vehicle records
FR-08	Vehicle repair history viewing
FR-11	Manager dashboard displaying active and completed jobs
FR-12	Basic reporting on jobs and payments
FR-13	User profile management

Could Have Requirements

These requirements would improve user experience but can be implemented in later phases if time permits.

Requirement ID	Description
FR-16	Customer feedback and rating functionality
FR-17	Vehicle image uploads
FR-18	Additional notification preferences and reminders
FR-19	Export reports to PDF or Excel

Won't Have (Phase 1)

The following requirements are intentionally excluded from the first release:

- Full inventory and stock management.
- Supplier ordering integration.
- SMS notifications.
- Accounting software integration.
- Online payment gateway integration.
- Public marketing website.
- Social media management tools.
- Multi-branch workshop support.

Prioritisation Justification

The highest priority requirements focus on solving the stakeholder's main problems:

- Reducing customer status-check phone calls.
- Improving repair progress visibility.
- Eliminating paper-based record keeping.
- Reducing pricing disputes through transparent quotations.
- Centralising customer and vehicle records.

Requirements not directly addressing these issues have been assigned lower priority and reserved for future phases.

17. Appendices Containing Stakeholder Evidence

Appendix A: Stakeholder Information

Business Name: Mister Auto & Turbo

Representative: Mr. Motlokoa Tsoetsi

Position: Managing Director

Business Address: No. 5, 123 Constantia Road, Dagbreek, Welkom, 9459, Free State, South Africa

Contact Number: 073 002 4579

Email Address: csolotsi.motloton@yahoo.com

Appendix B: Stakeholder Cooperation Agreement

Attached to this document is the signed Stakeholder Cooperation and Information Use Agreement confirming:

- Stakeholder participation in requirements gathering.
- Permission to analyse existing business processes.
- Agreement to review project requirements and prototypes.
- Understanding that the developed solution is an academic prototype.
- Confirmation of stakeholder cooperation throughout the project lifecycle.

Evidence Source: Signed Stakeholder Cooperation & Information Use Agreement dated **25/08/2026**.

Appendix C: Stakeholder Interview Findings

The following stakeholder needs were identified during interviews and discussions:

Stakeholder Need ID	**Requirement Identified**
SN-01	Customers should track vehicle progress without phoning the workshop.
SN-02	Fixed and transparent pricing should be available for common services.

SN-03	Quotations should clearly show differences between customer-supplied and business-supplied parts.
SN-04	The business requires a stronger digital presence.
N-05	The business needs repair history records for repeat customers.

Appendix D: Current Process Evidence

Current workflow observed during stakeholder engagement:

1. Customer brings vehicle to workshop.
2. Initial inspection is conducted.
3. Paper-based job card is created.
4. Diagnosis and quotation are prepared.
5. Customer approval is requested.
6. Repairs are performed.
7. Quality inspection is completed.
8. Payment is collected.
9. Customer collects vehicle.

Problems Identified

- Paper records can be misplaced.
- Customers frequently call for status updates.
- Pricing disputes occur regularly.
- No centralised repair history exists.
- Limited online presence restricts customer reach.
- Manual administration increases workload.

Appendix E: Stakeholder Communication Evidence

Evidence may include:

- WhatsApp conversations.
- Email correspondence.
- Meeting minutes.
- Interview notes.
- Screenshots of discussions.
- Requirement validation messages.

.

Appendix F: System Screens and Mockups (If Available)

This appendix may contain:

- Wireframes.
- User interface mockups.
- Dashboard designs.
- Workflow diagrams.
- System architecture diagrams.

These prototypes will be reviewed and validated by the stakeholder before final implementation.

Appendix G: Stakeholder Validation Statement

"The requirements documented in this Software Requirements Specification accurately reflect the current business processes and needs of Mister Auto & Turbo as discussed during stakeholder engagement."

Stakeholder Name: Motlokoa Tsoetsi
Position: Managing Director

STAKEHOLDER COOPERATION & INFORMATION USE AGREEMENT

Academic Student Project - Central University of Technology, Free State

This Agreement is entered into between the parties named below for the purpose of an academic student project conducted as part of the module ITC327W (Work-Integrated Learning), Diploma in Information Technology, Central University of Technology.

1.The Parties

Stakeholder / Business Representative:

Name:

MOTLOKA TSOTETSI

Business name:

MISTER AUTO AND TURBO

Position:

MANAGING DIRECTOR

Contact details (phone number):

073 002 4599

Email address

tsotetsimotloka@yahoo.com

Student Group Representative initials and student numbers

224099468 LE LETSIE
215135458 LE LIPALI
219002738 LTBG PULE
223013773 NM NETSHITUKA
222066543 RG MADI

2. Purpose of the Project

The student group is developing, as part of their academic assessment, a proposed Vehicle Service Management System intended to support the Stakeholder's day-to-day vehicle servicing operations (customer intake, job cards, quotations, repair tracking, payments, and vehicle collection). The purpose of this Agreement is to confirm the Stakeholder's voluntary participation and to set out, in writing, what information will be collected, how it will be used, and what the student group will provide in return.

3. What the Students Will Collect

With the Stakeholder's cooperation, the student group may collect the following, strictly for the purposes of this academic project:

- A description of the Stakeholder's current business process and workflow.
- Information about the roles of staff involved in that process (e.g. reception, mechanics, management).
- The Stakeholder's requirements and preferences for a proposed digital system.
- Feedback on draft requirements, mock-ups, or prototypes.
- General, non-identifying examples of the type of data the business handles (e.g. what fields a job card typically contains), rather than actual customer records where avoidable.

4. What the Students Will NOT Do

- The students will not request or record sensitive personal information about the Stakeholder's customers or staff beyond what is reasonably necessary to understand the business process.
- The students will not publish any confidential business information, pricing, customer data, or credentials in any public location..
- The students will not use any information gathered for any purpose beyond this academic module and its assessment and presentation requirements.

5. What the Stakeholder Agrees To

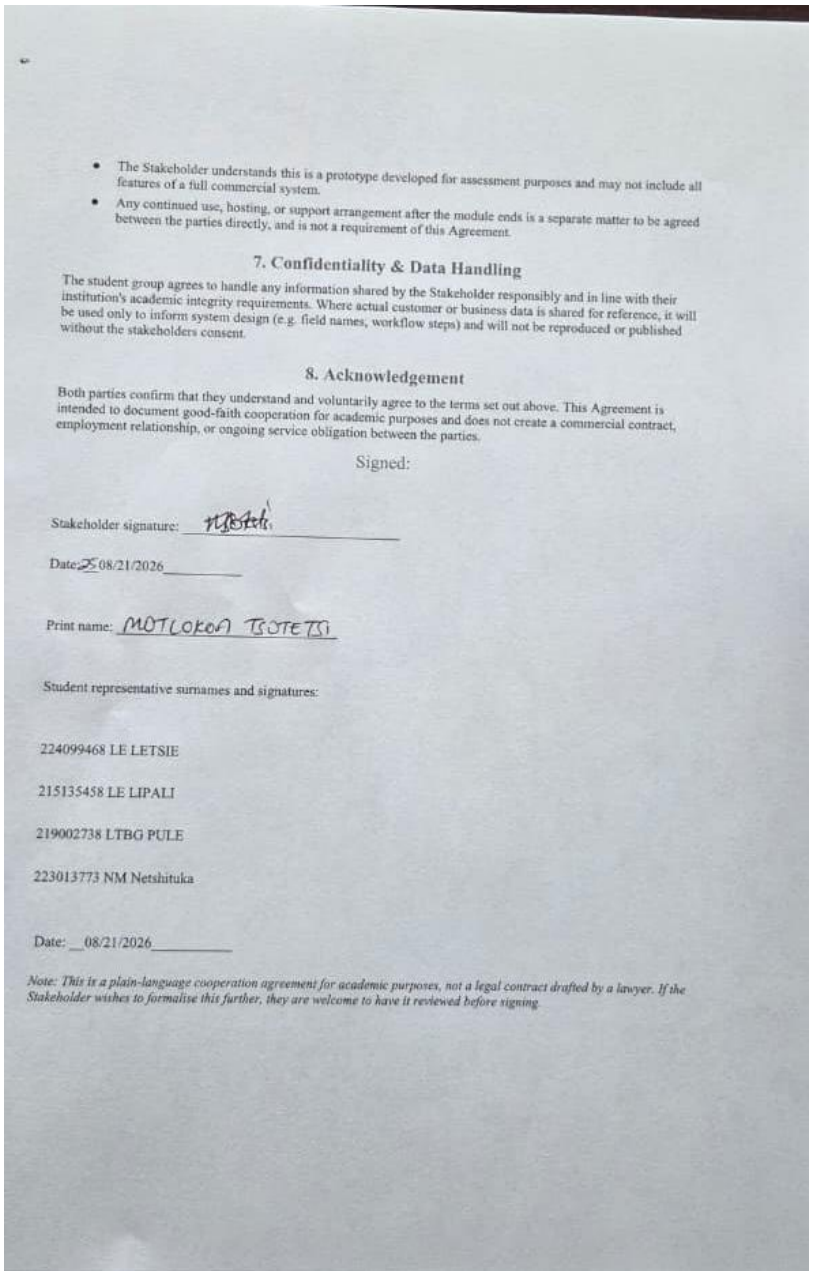
- Making themselves reasonably available for a limited number of meetings, interviews, or written communications during the semester.
- Providing honest and accurate information about their current process to the best of their ability.
- Reviewing and confirming, in writing (email, WhatsApp, or meeting notes signed off), the requirements gathered so the students have documented evidence for their assessment.
- Understanding that participation is voluntary and can be withdrawn at any time by notifying the student group and their module supervisor.

6. What the Students Provide in Return

In exchange for the Stakeholder's time and cooperation, the student group will provide the Stakeholder with a working prototype/solution developed during the module, at no cost, for the Stakeholder's own use.

- The solution is developed as a student learning exercise and is provided "as is," without any guarantee of ongoing support, maintenance, hosting, or further development beyond the academic module, unless separately agreed in writing.

L.M



- The Stakeholder understands this is a prototype developed for assessment purposes and may not include all features of a full commercial system.
- Any continued use, hosting, or support arrangement after the module ends is a separate matter to be agreed between the parties directly, and is not a requirement of this Agreement.

7. Confidentiality & Data Handling

The student group agrees to handle any information shared by the Stakeholder responsibly and in line with their institution's academic integrity requirements. Where actual customer or business data is shared for reference, it will be used only to inform system design (e.g. field names, workflow steps) and will not be reproduced or published without the stakeholders consent.

8. Acknowledgement

Both parties confirm that they understand and voluntarily agree to the terms set out above. This Agreement is intended to document good-faith cooperation for academic purposes and does not create a commercial contract, employment relationship, or ongoing service obligation between the parties.

Signed:

Stakeholder signature: _____

Date: 25 08/21/2026

Print name: MOTLOKOA TSOTETSI

Student representative surnames and signatures:

224099468 LE LETSIE

215135458 LE LIPALI

219002738 LTBG PULE

223013773 NM Netshituka

Date: 08/21/2026

Note: This is a plain-language cooperation agreement for academic purposes, not a legal contract drafted by a lawyer. If the Stakeholder wishes to formalise this further, they are welcome to have it reviewed before signing.

GITHUB LINK

https://github.com/Inheritancersa/MisterAutoAndTurbo

PHASE 2: System Architecture and Design

MR AUTO & TURBO

Workshop Management System - Phase 2 System Design

Field	Detail
Module	ITC327W - Work-Integrated Learning
Assessment	Group Assessment 2 - Phase 2: System Architecture and Design
Client / Stakeholder	Motlokoa Tsotesi, Owner - Mr Auto & Turbo
Prepared by	Web Vortex
Date	25/09/26

1. Purpose of This Document

This document supports the System Architecture and Design section of the ITC327W Phase 2 Software Requirements Specification (SRS) for the Mr Auto & Turbo Workshop Management System. It provides:

- Written content the group can adapt and insert into the updated SRS alongside the System Architecture Diagram, Use Case Diagram, Sequence Diagrams, ERD, and interface designs already completed.
- A Design Alignment table linking requirements, use cases, database entities, and interfaces, as required by the rubric.
- A Stakeholder Review and Approval page (Section 8) for the client, Motlokoa Tsotesi, to review and sign - evidence of stakeholder engagement for the SRS appendix.

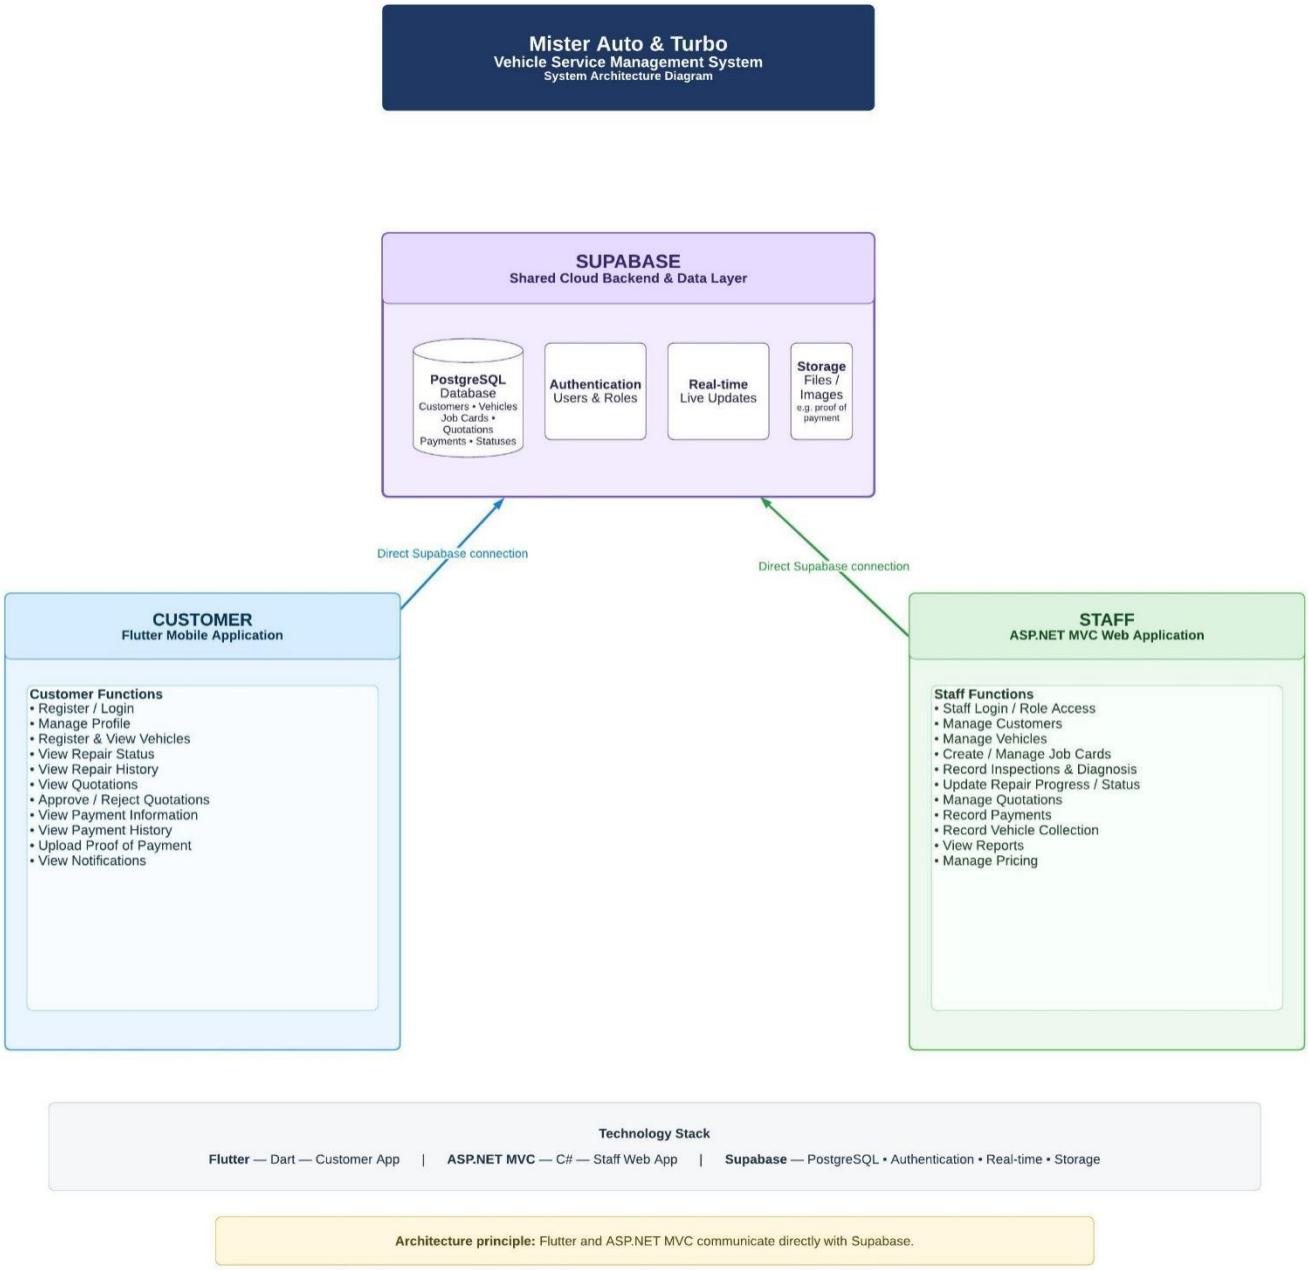
2. System Overview

The Mr Auto & Turbo Workshop Management System is designed as one integrated system built from three connected components: a Flutter mobile application, an ASP.NET web application, and a shared Supabase backend.

The Flutter mobile application serves both customers and workshop staff. Customers use it to track their vehicle's repair status in real time, view notifications, and manage payments. Staff use the same application, under a different role-based view, to check job status on the go and receive job-assignment notifications. Sign-in is handled through a phone-number and OTP (one-time PIN) flow, matching the way the business already communicates with customers over SMS/WhatsApp.

The ASP.NET web application is the primary workstation tool for the business, providing three role-based views: an Administrator/Manager view with full access to all modules including payments and reporting; a Receptionist view scoped to front-desk functions such as customer registration, vehicle check-in, appointments, and collections (with payment processing restricted, since only management handles payments); and a Mechanic view scoped to assigned jobs, inspection checklists, and parts requests.

The Supabase backend provides the shared PostgreSQL database, authentication, and real-time data services that both the Flutter and ASP.NET applications read from and write to. This ensures that a status update made by a mechanic on the web application is reflected immediately in the customer's mobile app, and that a booking made by a receptionist is immediately visible to the assigned mechanic - the three components operate as a single, real-time system rather than separate, disconnected tools.

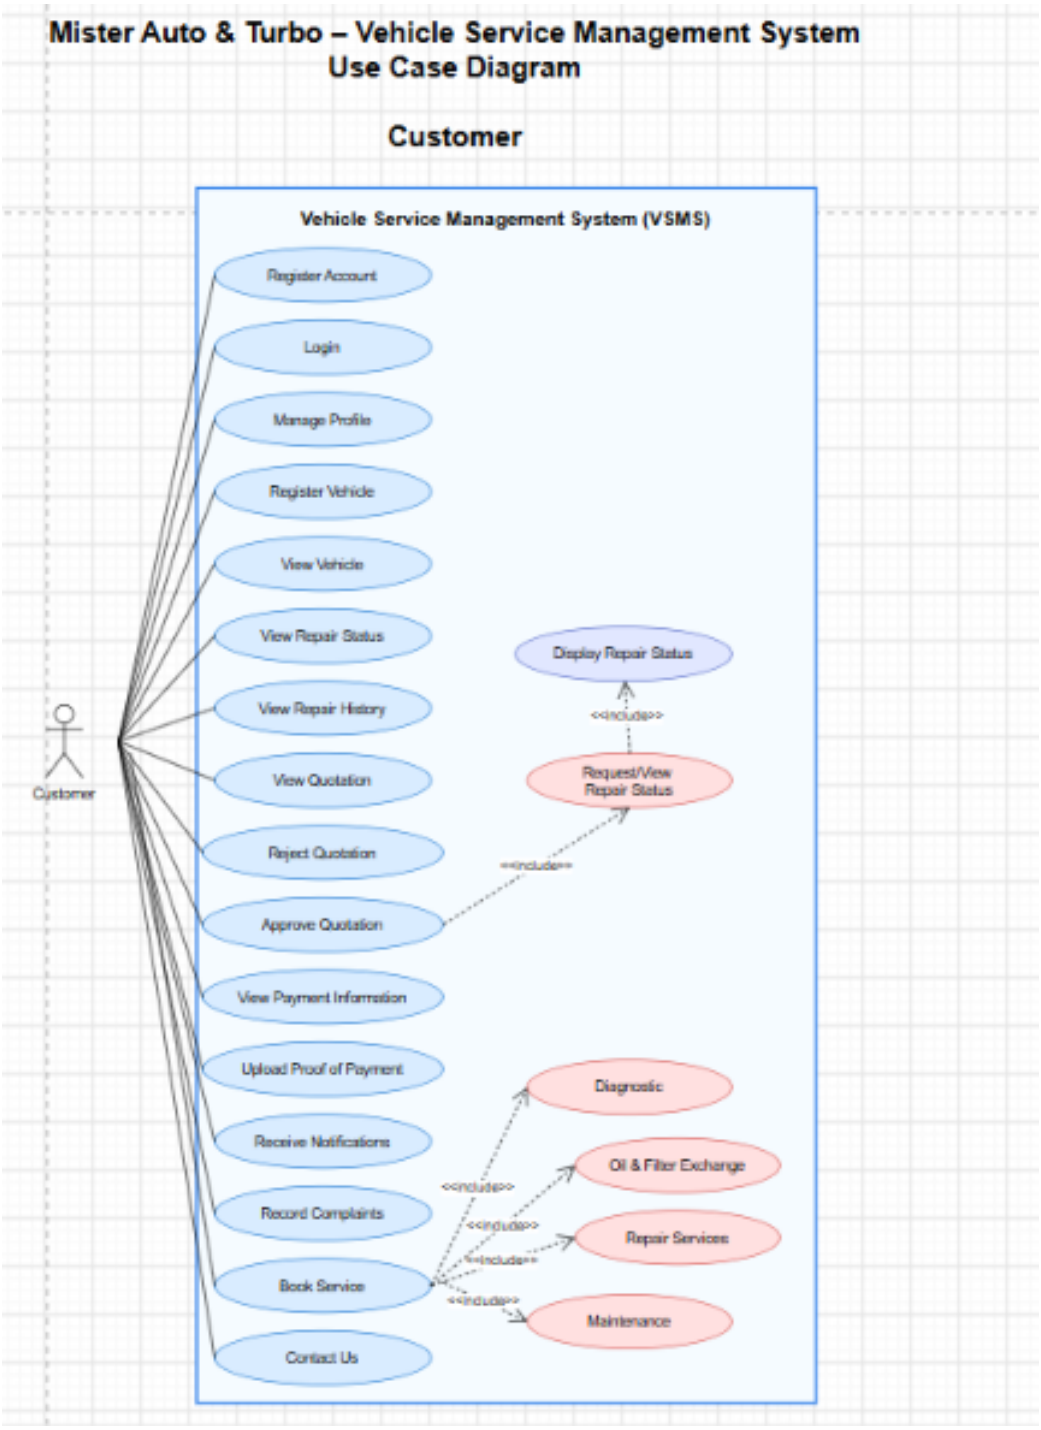


3. User Roles (Actors)

Actor	Description	Primary Interface
Administrator / Manager	Owns or manages the business; has full access to all modules, including payments, staff management, and reporting.	ASP.NET web application
Receptionist	Front-desk staff; manages customers, vehicle check-in, appointments, and collection. No access to payment processing.	ASP.NET web application

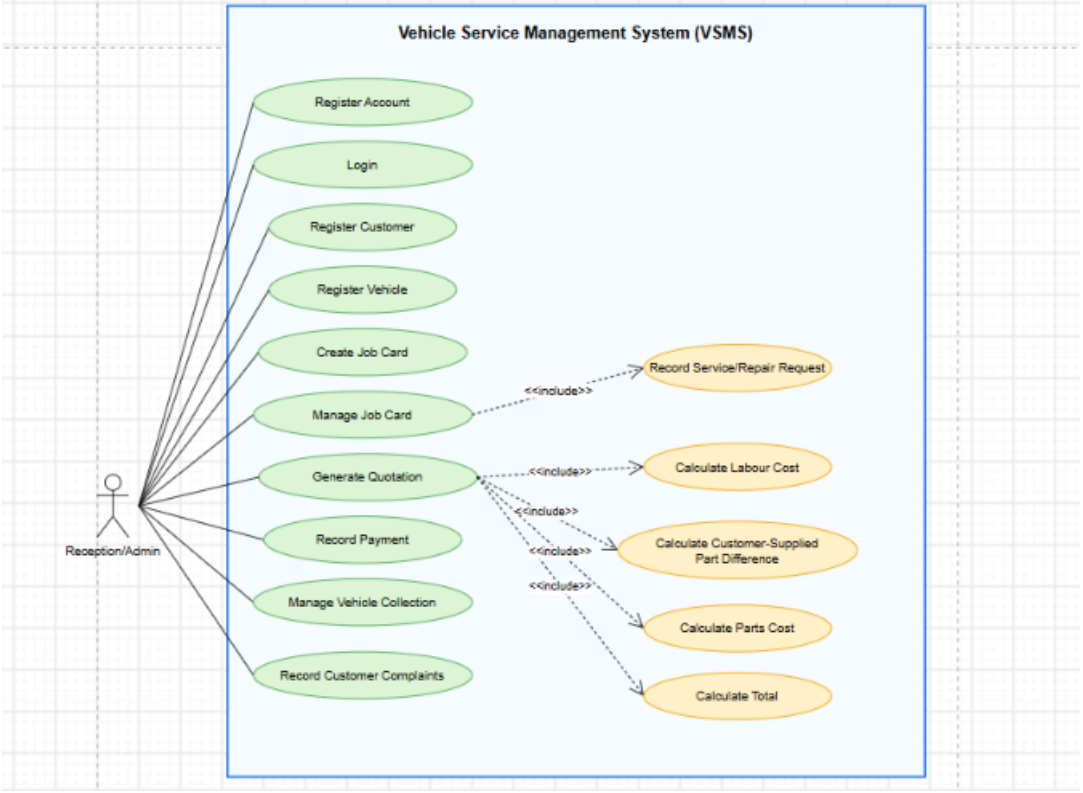
Mechanic	Workshop technician; manages assigned jobs, inspections, status updates, and part requests.	ASP.NET web application + Flutter mobile app
Customer	Vehicle owner; tracks repair status, receives notifications, and pays invoices.	Flutter mobile application

These roles correspond to the actors used in the group's Use Case Diagram.


Mister Auto & Turbo – Vehicle Service Management System
Use Case Diagram
Customer
Vehicle Service Management System (VSMS)
Register Account
Login
Manage Profile
Register Vehicle
View Vehicle
View Repair Status
View Repair History
View Quotation
Reject Quotation
Approve Quotation
View Payment Information
Upload Proof of Payment
Receive Notifications
Record Complaints
Book Service
Contact Us
Display Repair Status
<<include>>
Request/View Repair Status
<<include>>
<<include>>
Diagnostic
<<include>>
Oil & Filter Exchange
<<include>>
Repair Services
<<include>>
Maintenance
Customer

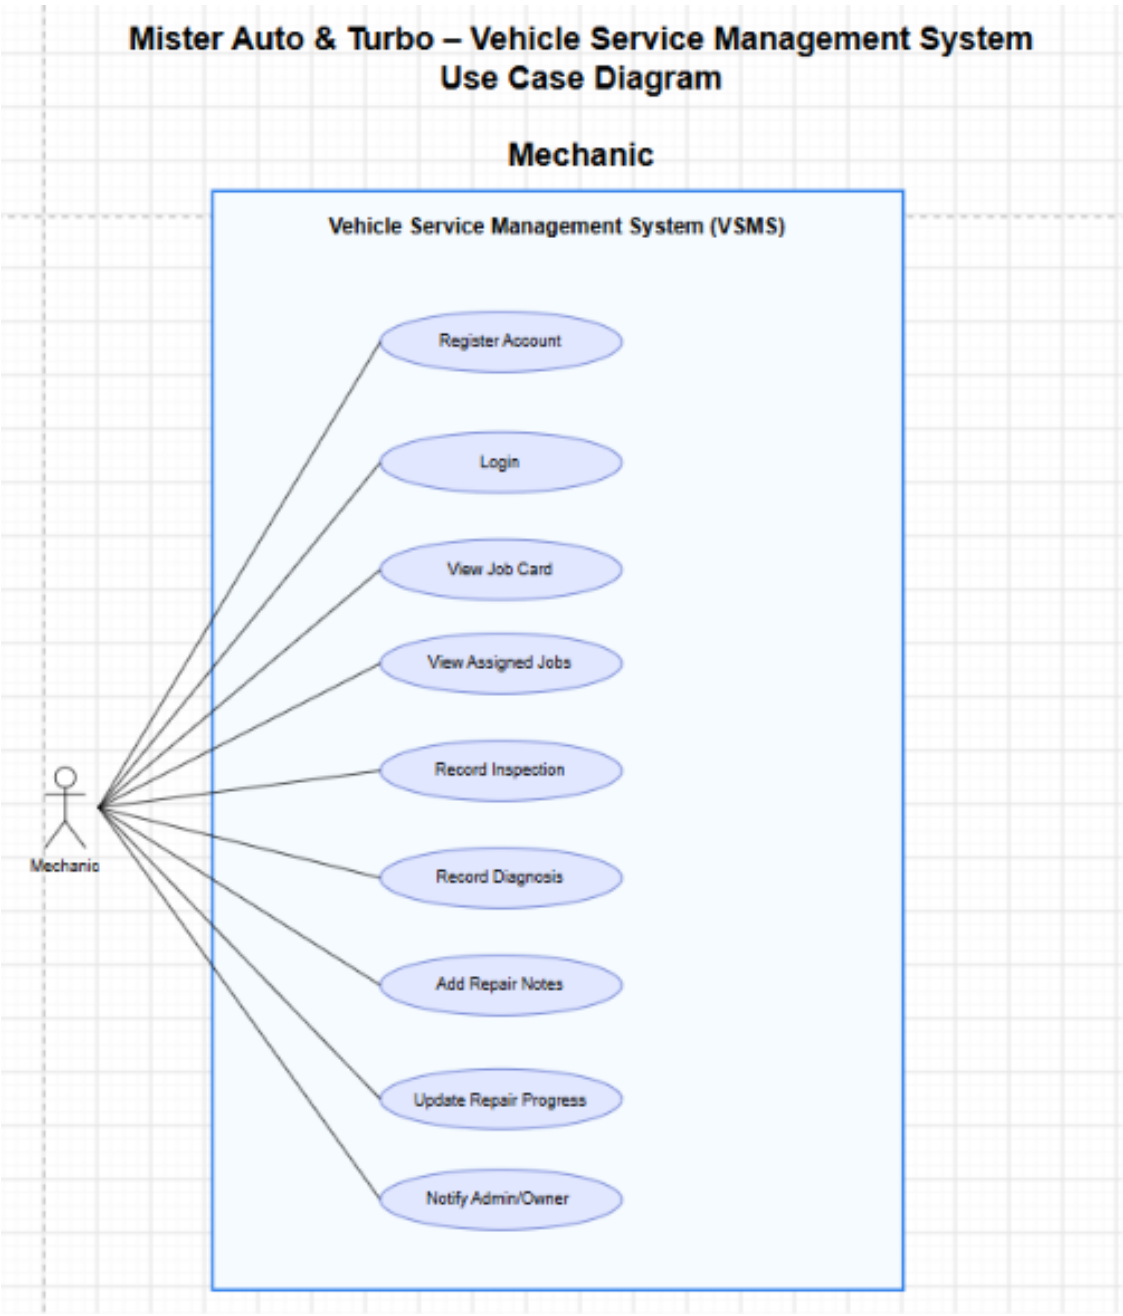
Mister Auto & Turbo – Vehicle Service Management System
Use Case Diagram

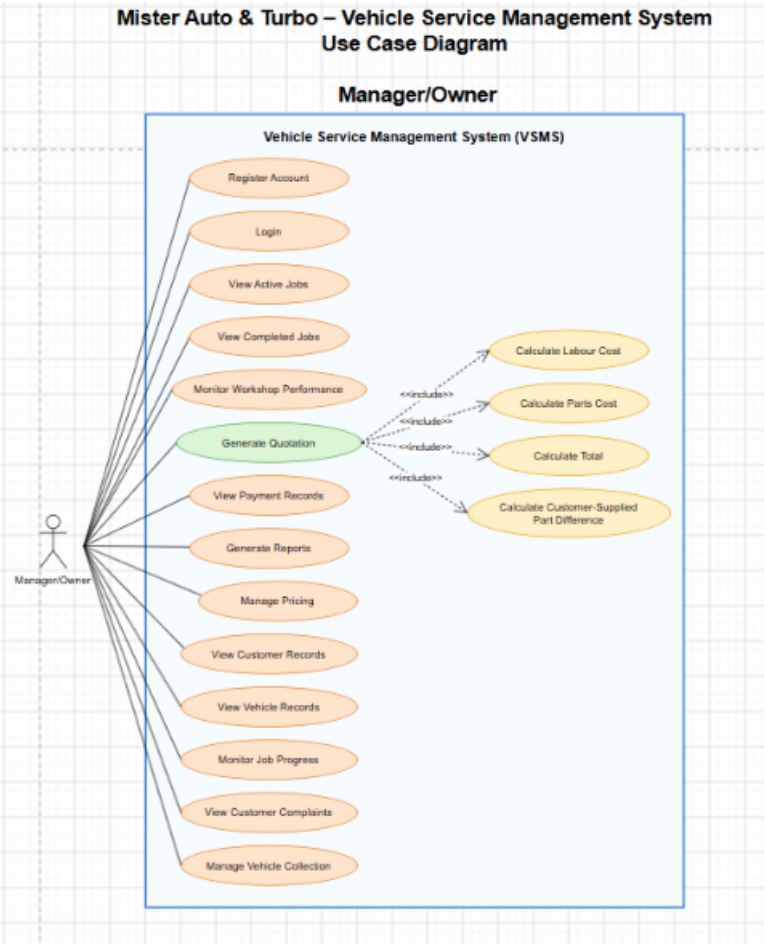
Reception/Admin



Mister Auto & Turbo – Vehicle Service Management System
Use Case Diagram

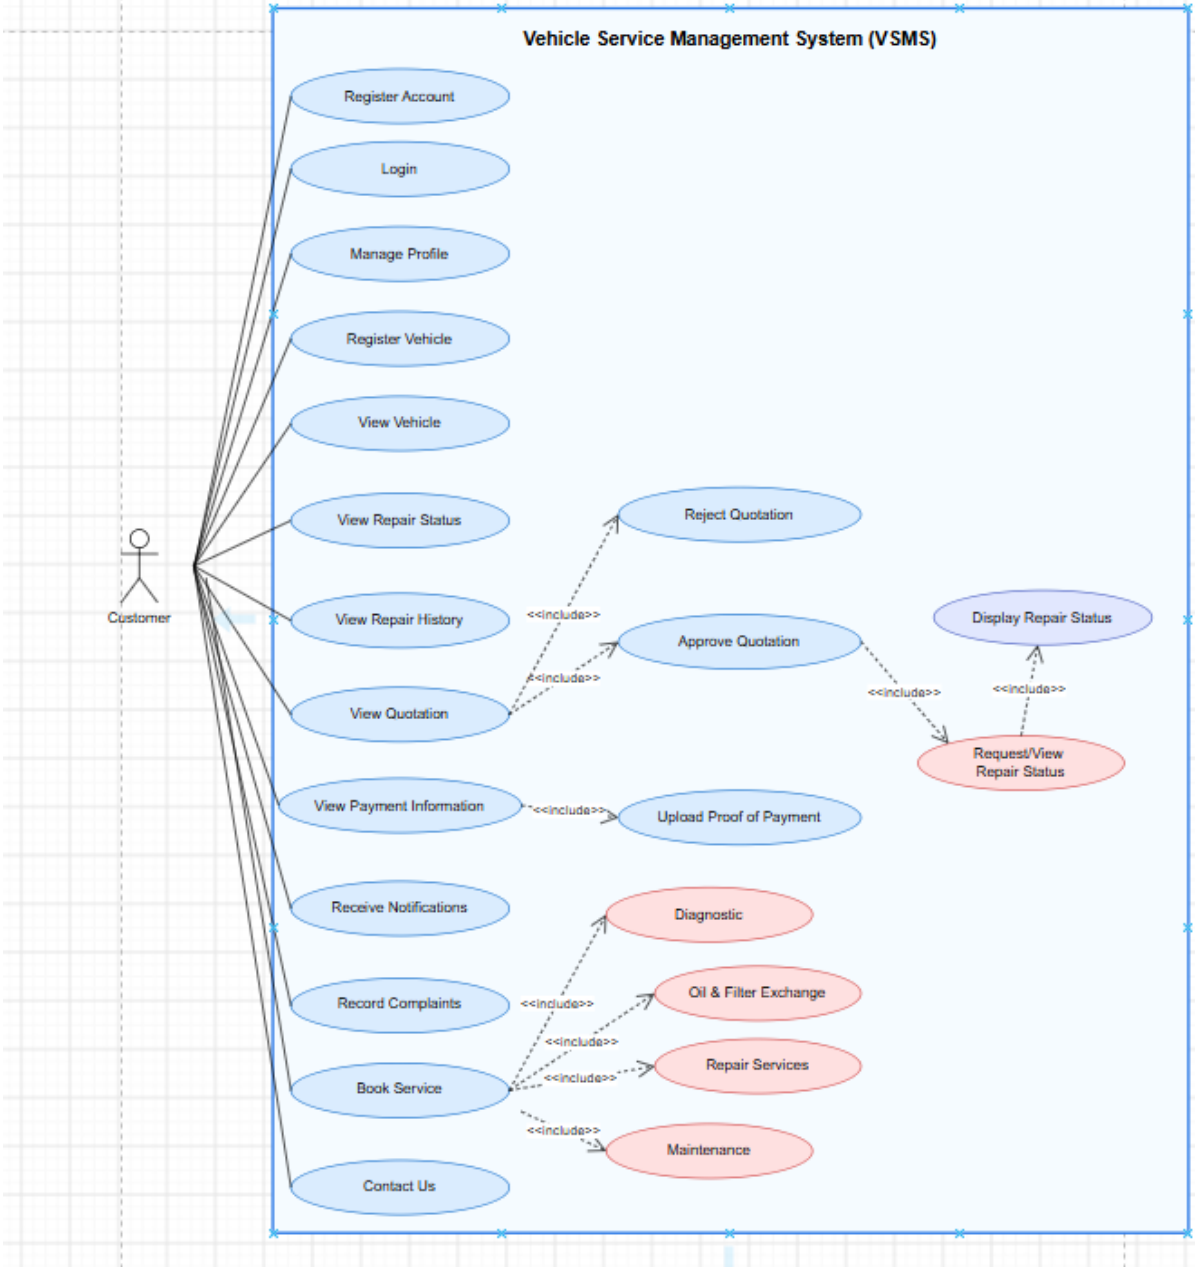
Mechanic

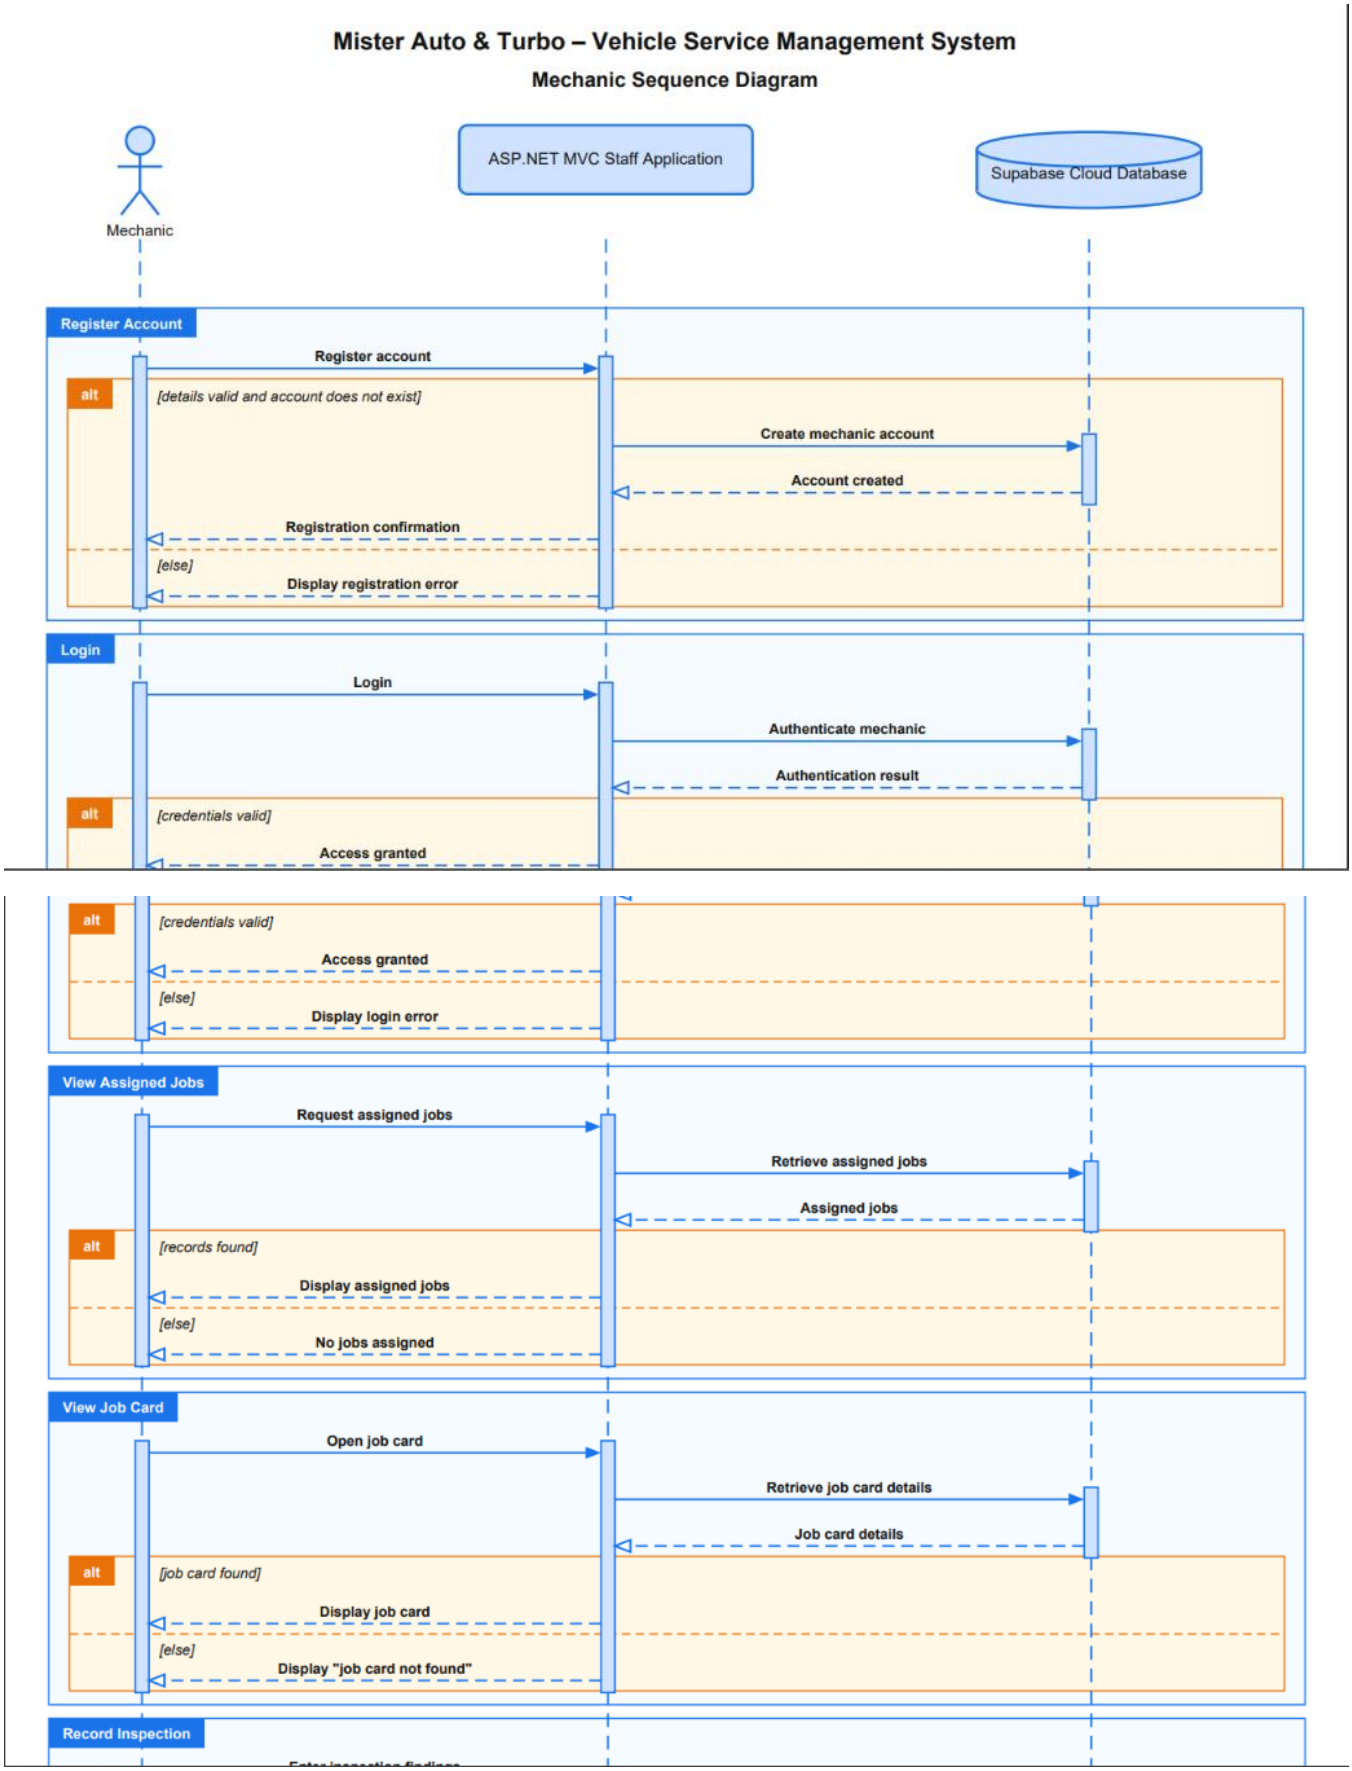


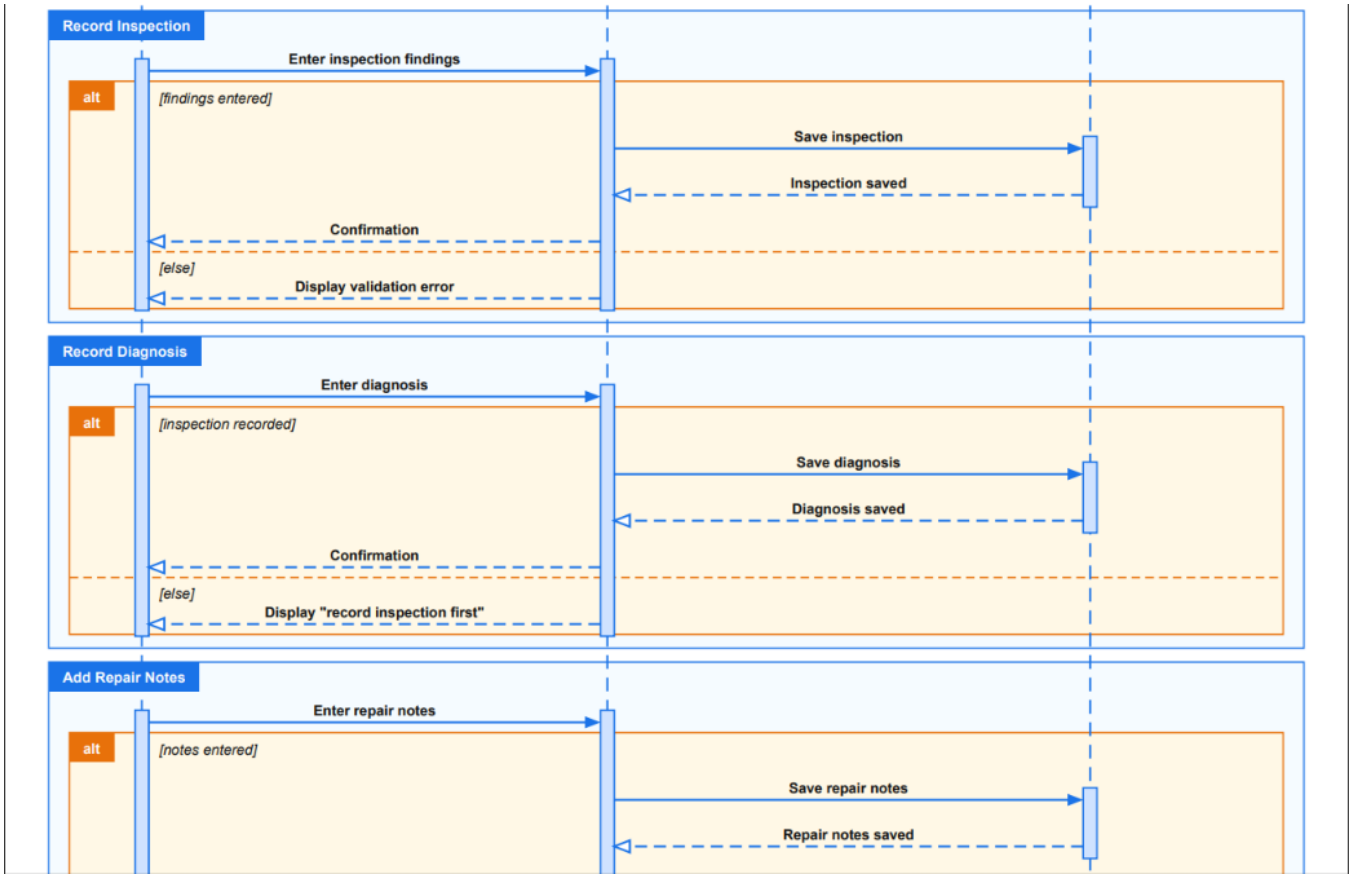

Mister Auto & Turbo – Vehicle Service Management System
Use Case Diagram
Manager/Owner
Vehicle Service Management System (VSMS)
Register Account
Login
View Active Jobs
View Completed Jobs
Monitor Workshop Performance
Generate Quotation
View Payment Records
Generate Reports
Manage Pricing
View Customer Records
View Vehicle Records
Monitor Job Progress
View Customer Complaints
Manage Vehicle Collection
Calculate Labour Cost
Calculate Parts Cost
Calculate Total
Calculate Customer-Supplied Part Difference
<<include>>
<<include>>
<<include>>
<<include>>
Manager/Owner

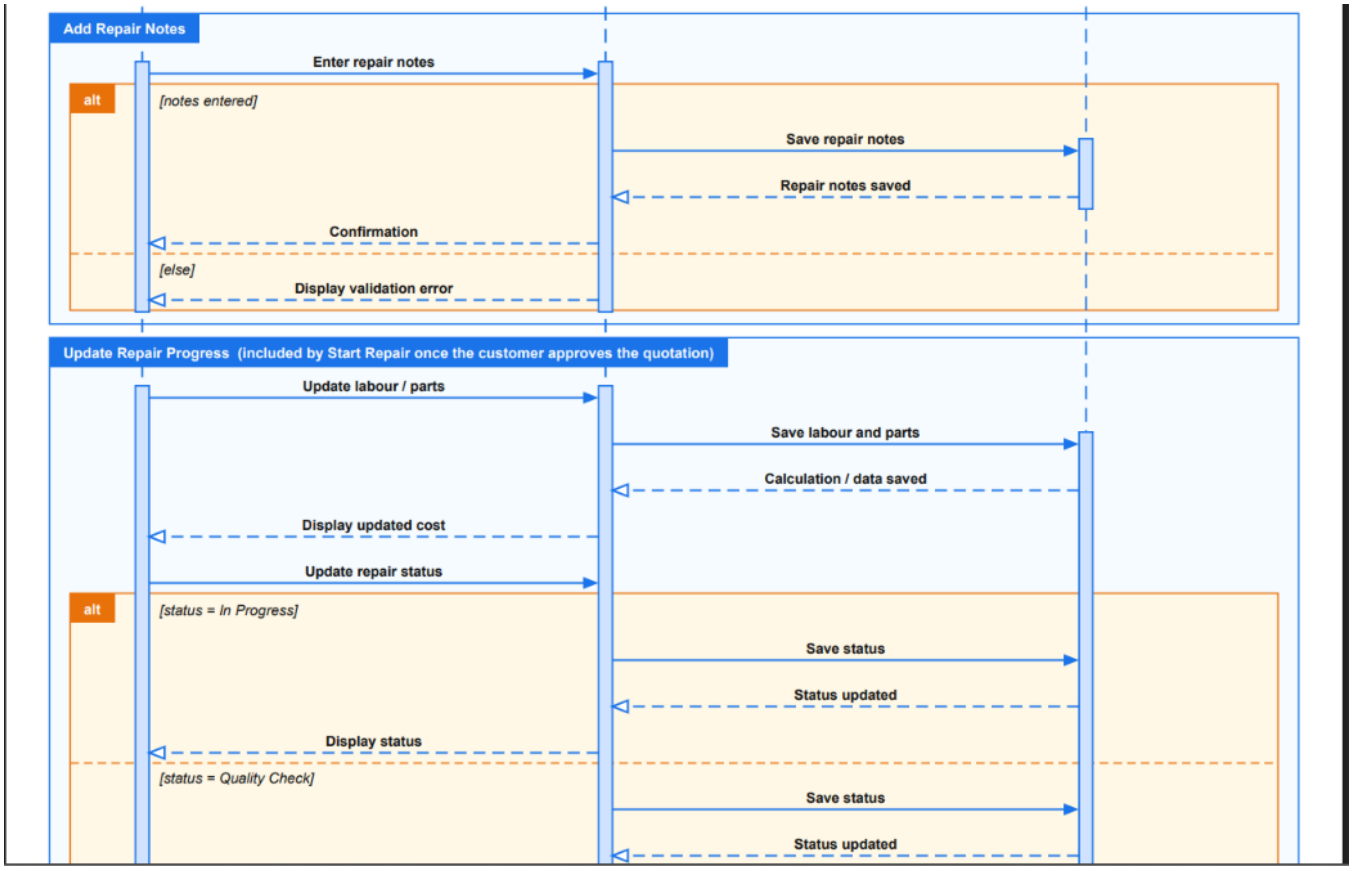
Mister Auto & Turbo – Vehicle Service Management System
Use Case Diagram

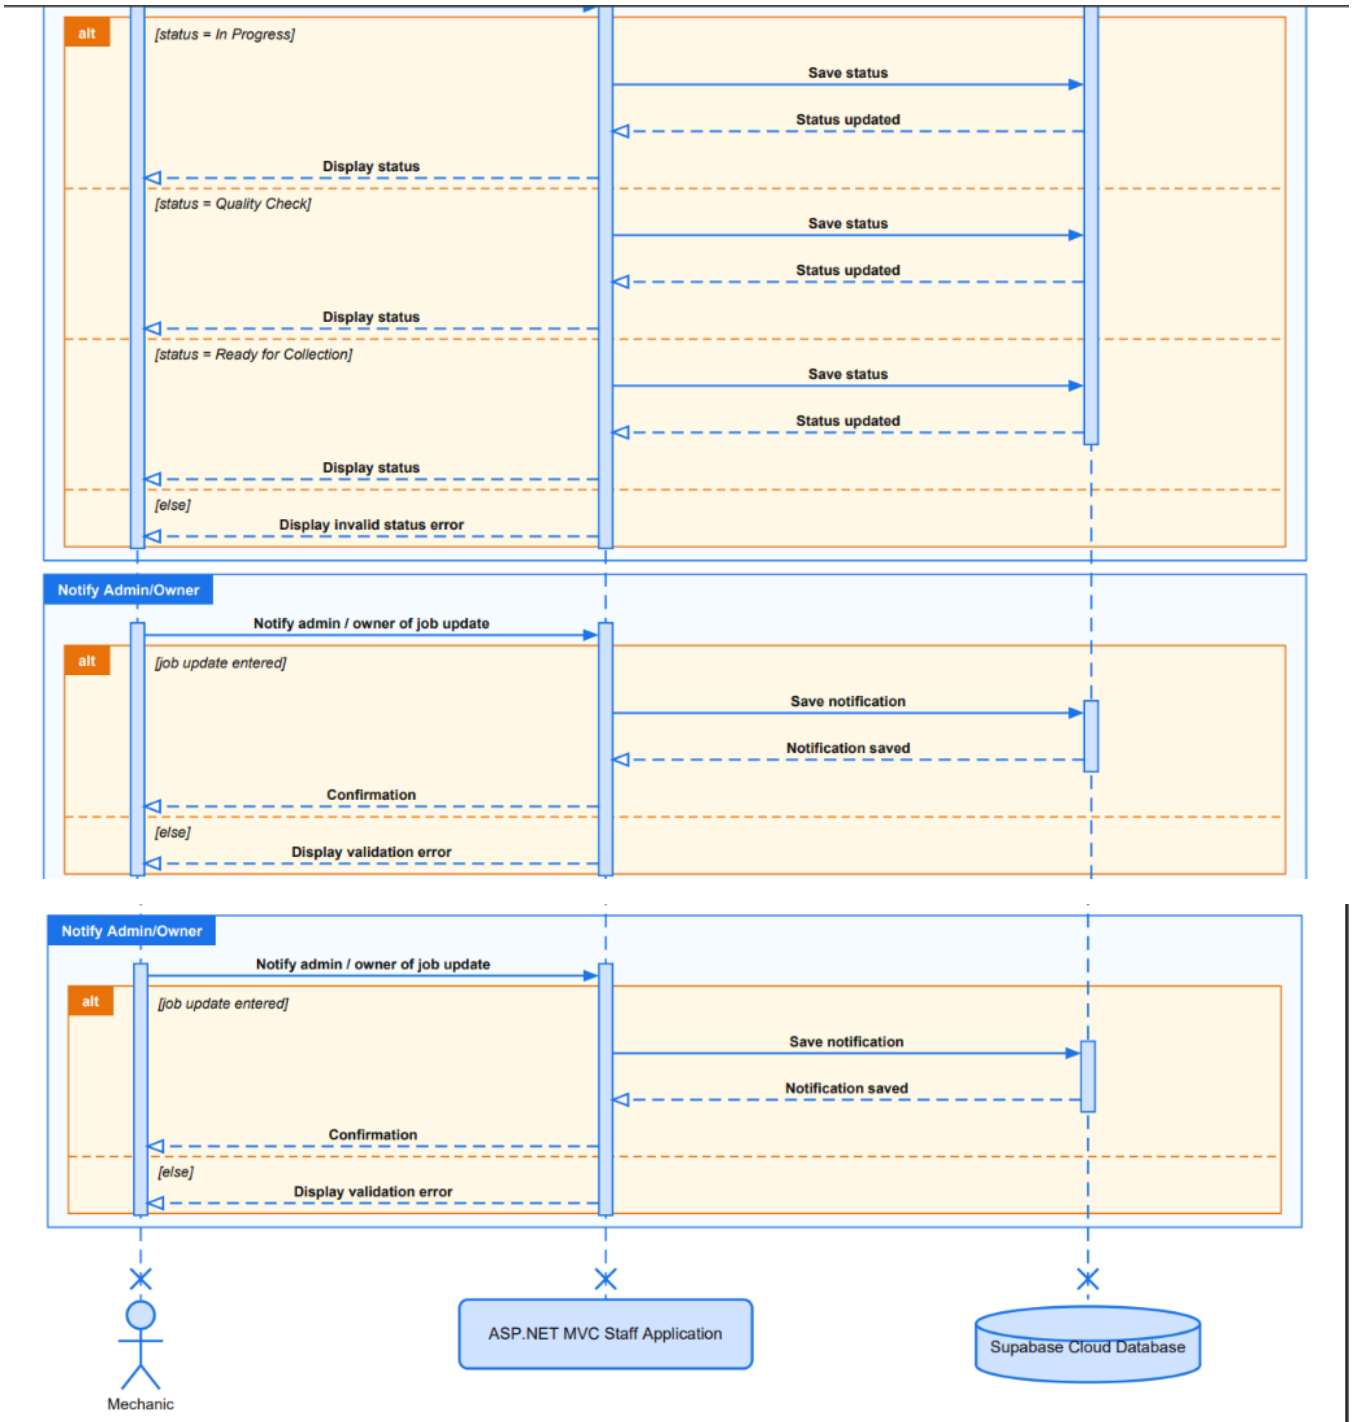
Customer




Mister Auto & Turbo – Vehicle Service Management System
Mechanic Sequence Diagram
Mechanic
ASP.NET MVC Staff Application
Supabase Cloud Database
Register Account
Register account
alt
[details valid and account does not exist]
Create mechanic account
Account created
Registration confirmation
[else]
Display registration error
Login
Login
Authenticate mechanic
Authentication result
alt
[credentials valid]
Access granted
alt
[credentials valid]
Access granted
[else]
Display login error
View Assigned Jobs
Request assigned jobs
Retrieve assigned jobs
Assigned jobs
alt
[records found]
Display assigned jobs
[else]
No jobs assigned
View Job Card
Open job card
Retrieve job card details
Job card details
alt
[job card found]
Display job card
[else]
Display "job card not found"
Record Inspection

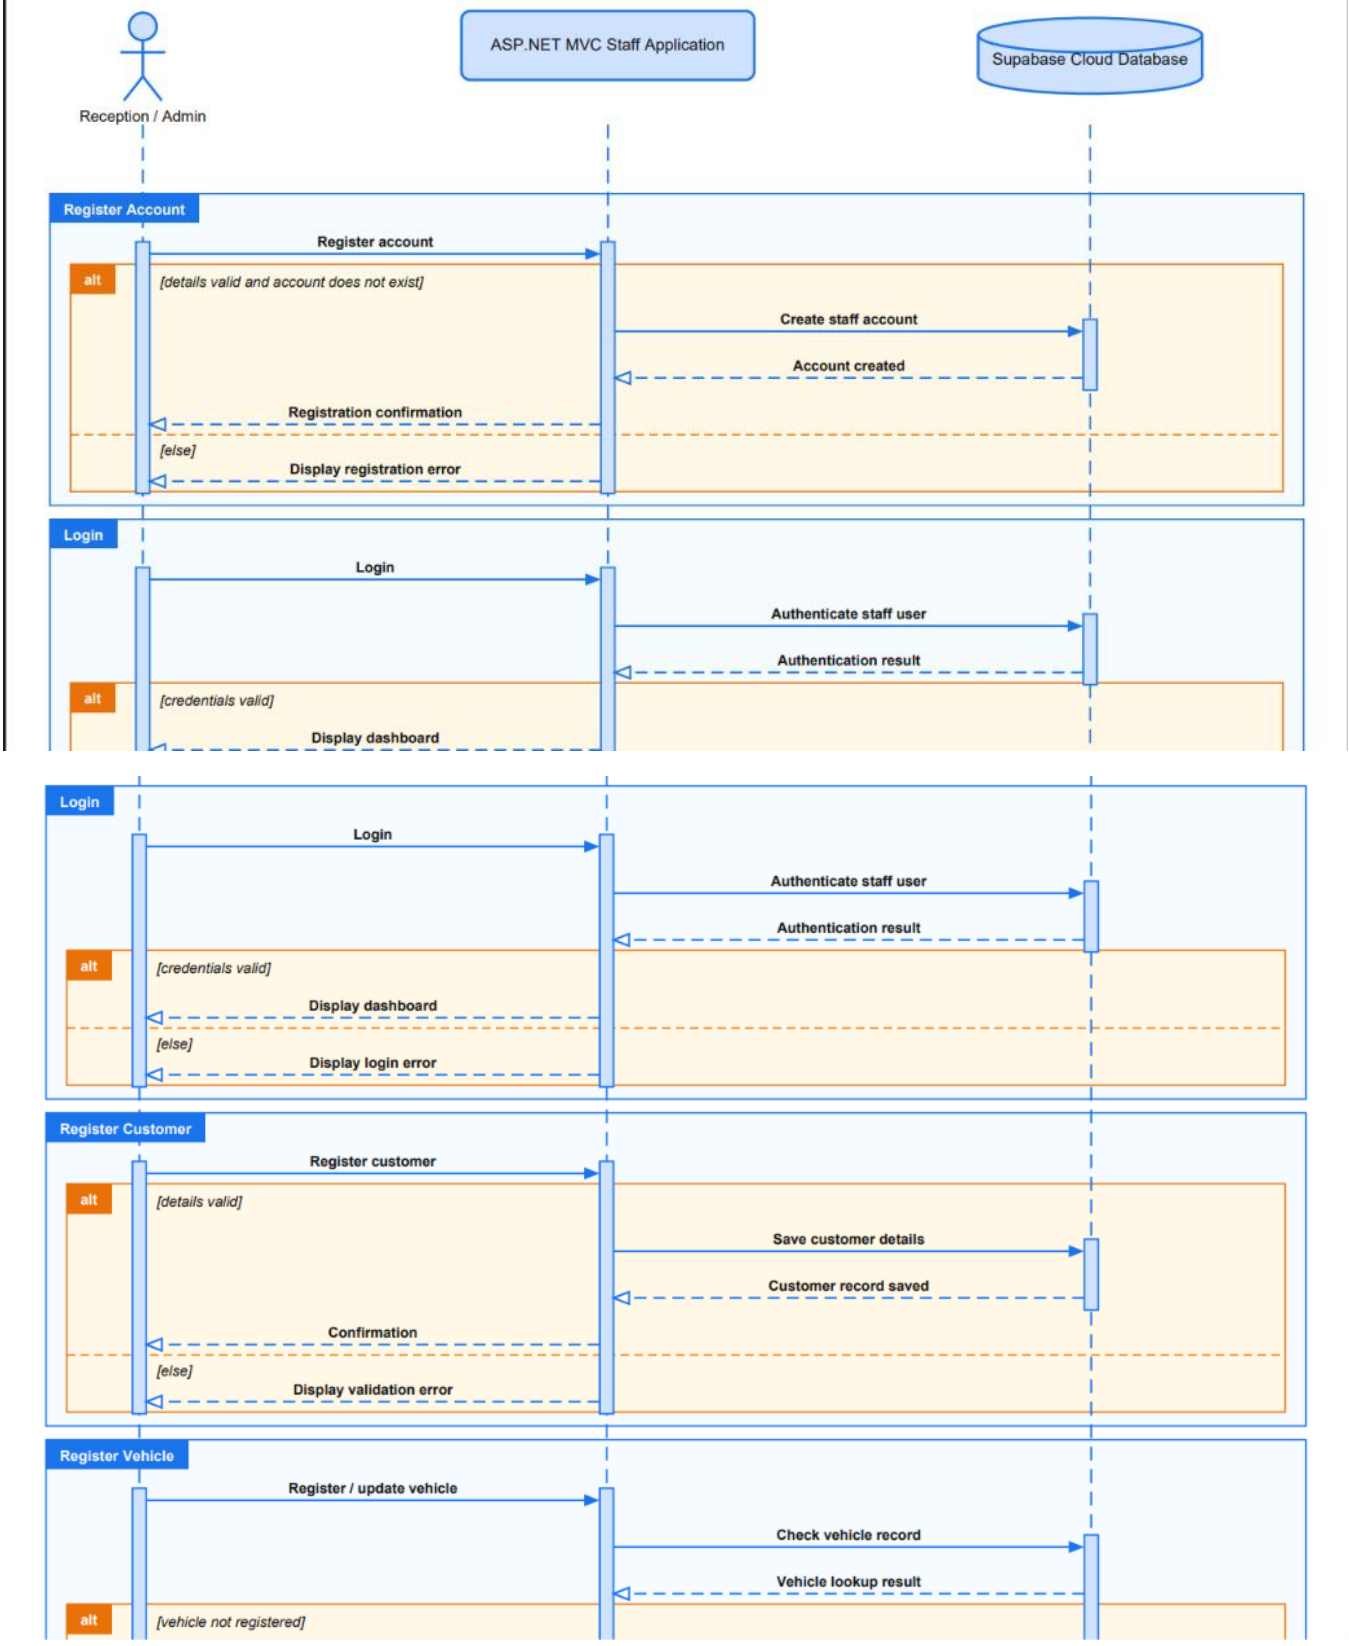

Record Inspection
Enter inspection findings
alt
[findings entered]
Save inspection
Inspection saved
Confirmation
[else]
Display validation error
Record Diagnosis
Enter diagnosis
alt
[inspection recorded]
Save diagnosis
Diagnosis saved
Confirmation
[else]
Display "record inspection first"
Add Repair Notes
Enter repair notes
alt
[notes entered]
Save repair notes
Repair notes saved

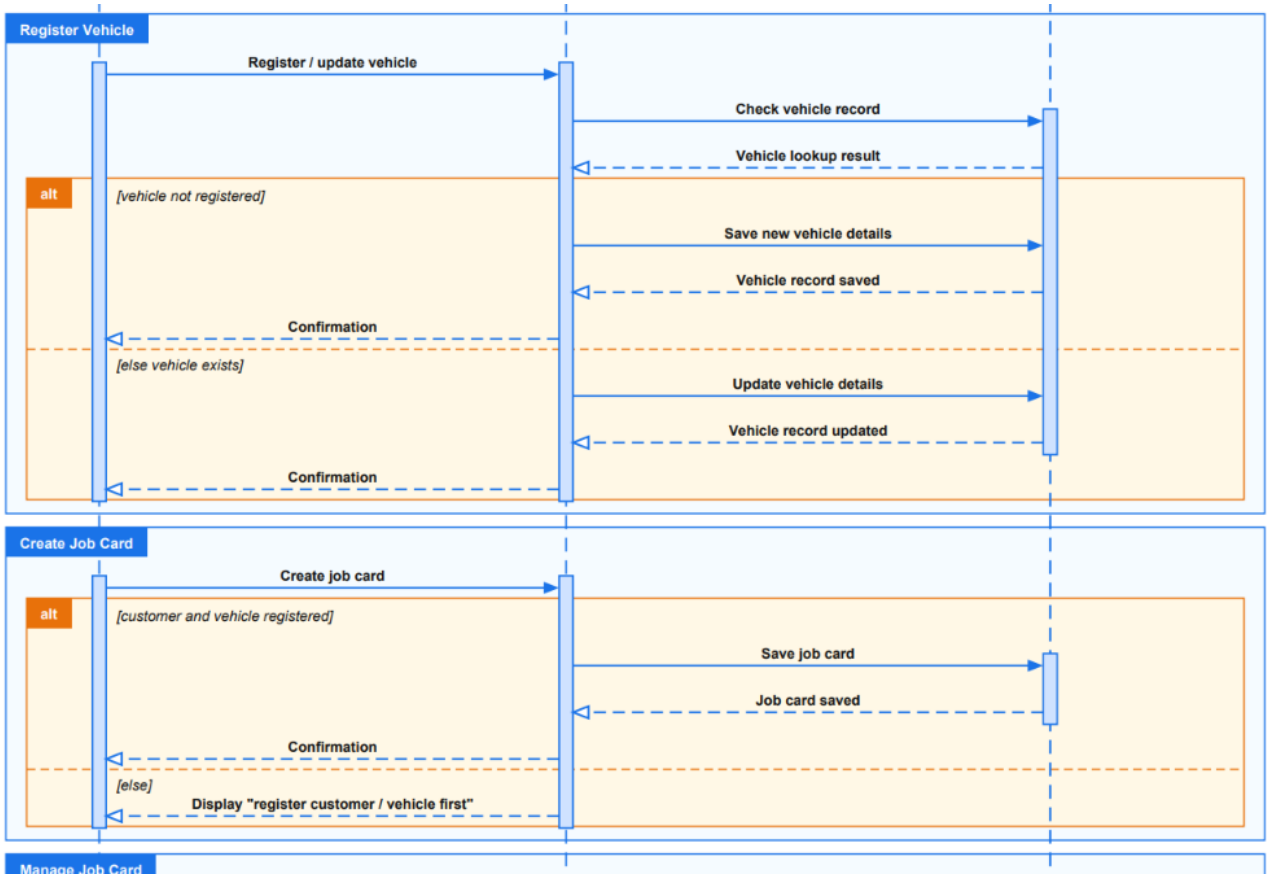

Add Repair Notes
Enter repair notes
alt
[notes entered]
Save repair notes
Repair notes saved
Confirmation
[else]
Display validation error
Update Repair Progress (included by Start Repair once the customer approves the quotation)
Update labour / parts
Save labour and parts
Calculation / data saved
Display updated cost
Update repair status
alt
[status = In Progress]
Save status
Status updated
Display status
[status = Quality Check]
Save status
Status updated

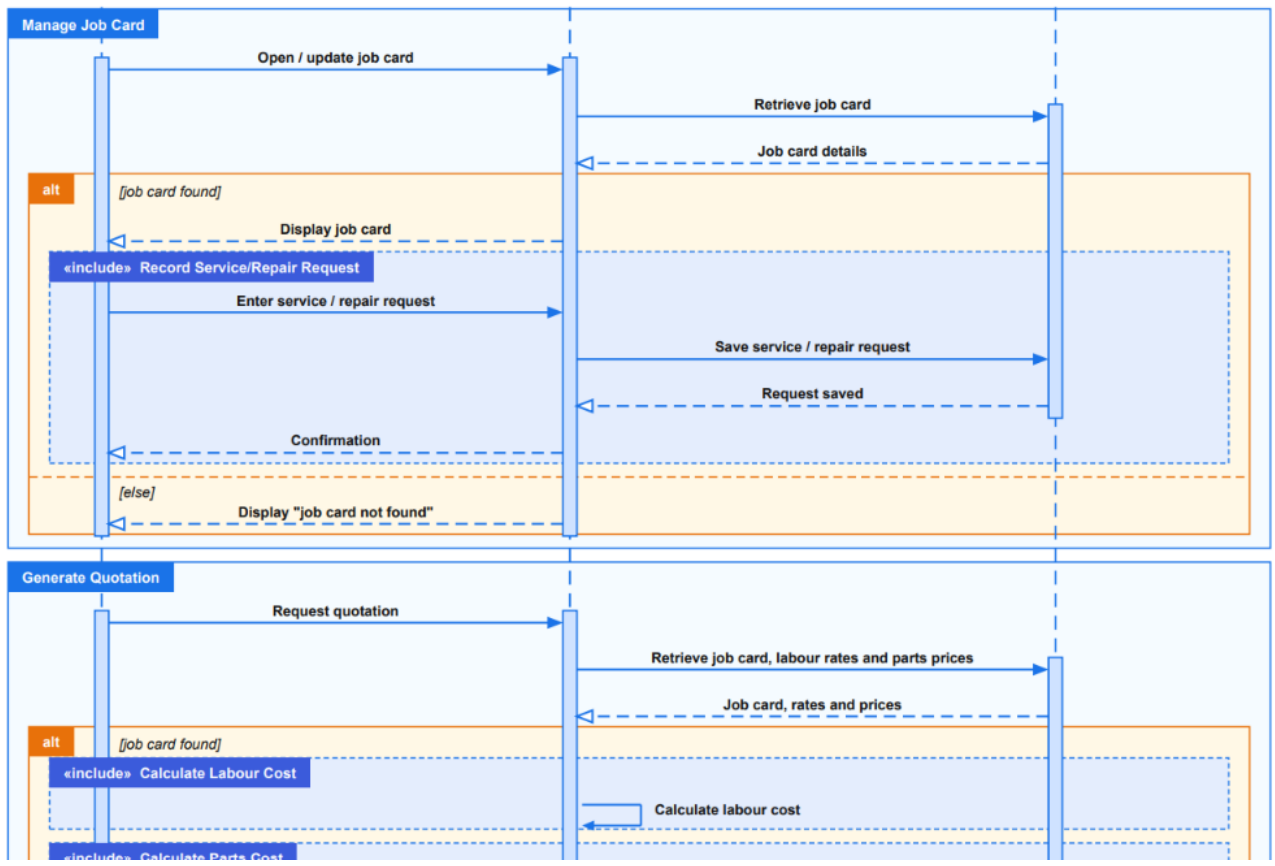

alt
[status = In Progress]
Save status
Status updated
Display status
[status = Quality Check]
Save status
Status updated
Display status
[status = Ready for Collection]
Save status
Status updated
Display status
[else]
Display invalid status error
Notify Admin/Owner
Notify admin / owner of job update
alt
[job update entered]
Save notification
Notification saved
Confirmation
[else]
Display validation error
Notify Admin/Owner
Notify admin / owner of job update
alt
[job update entered]
Save notification
Notification saved
Confirmation
[else]
Display validation error
Mechanic
ASP.NET MVC Staff Application
Supabase Cloud Database

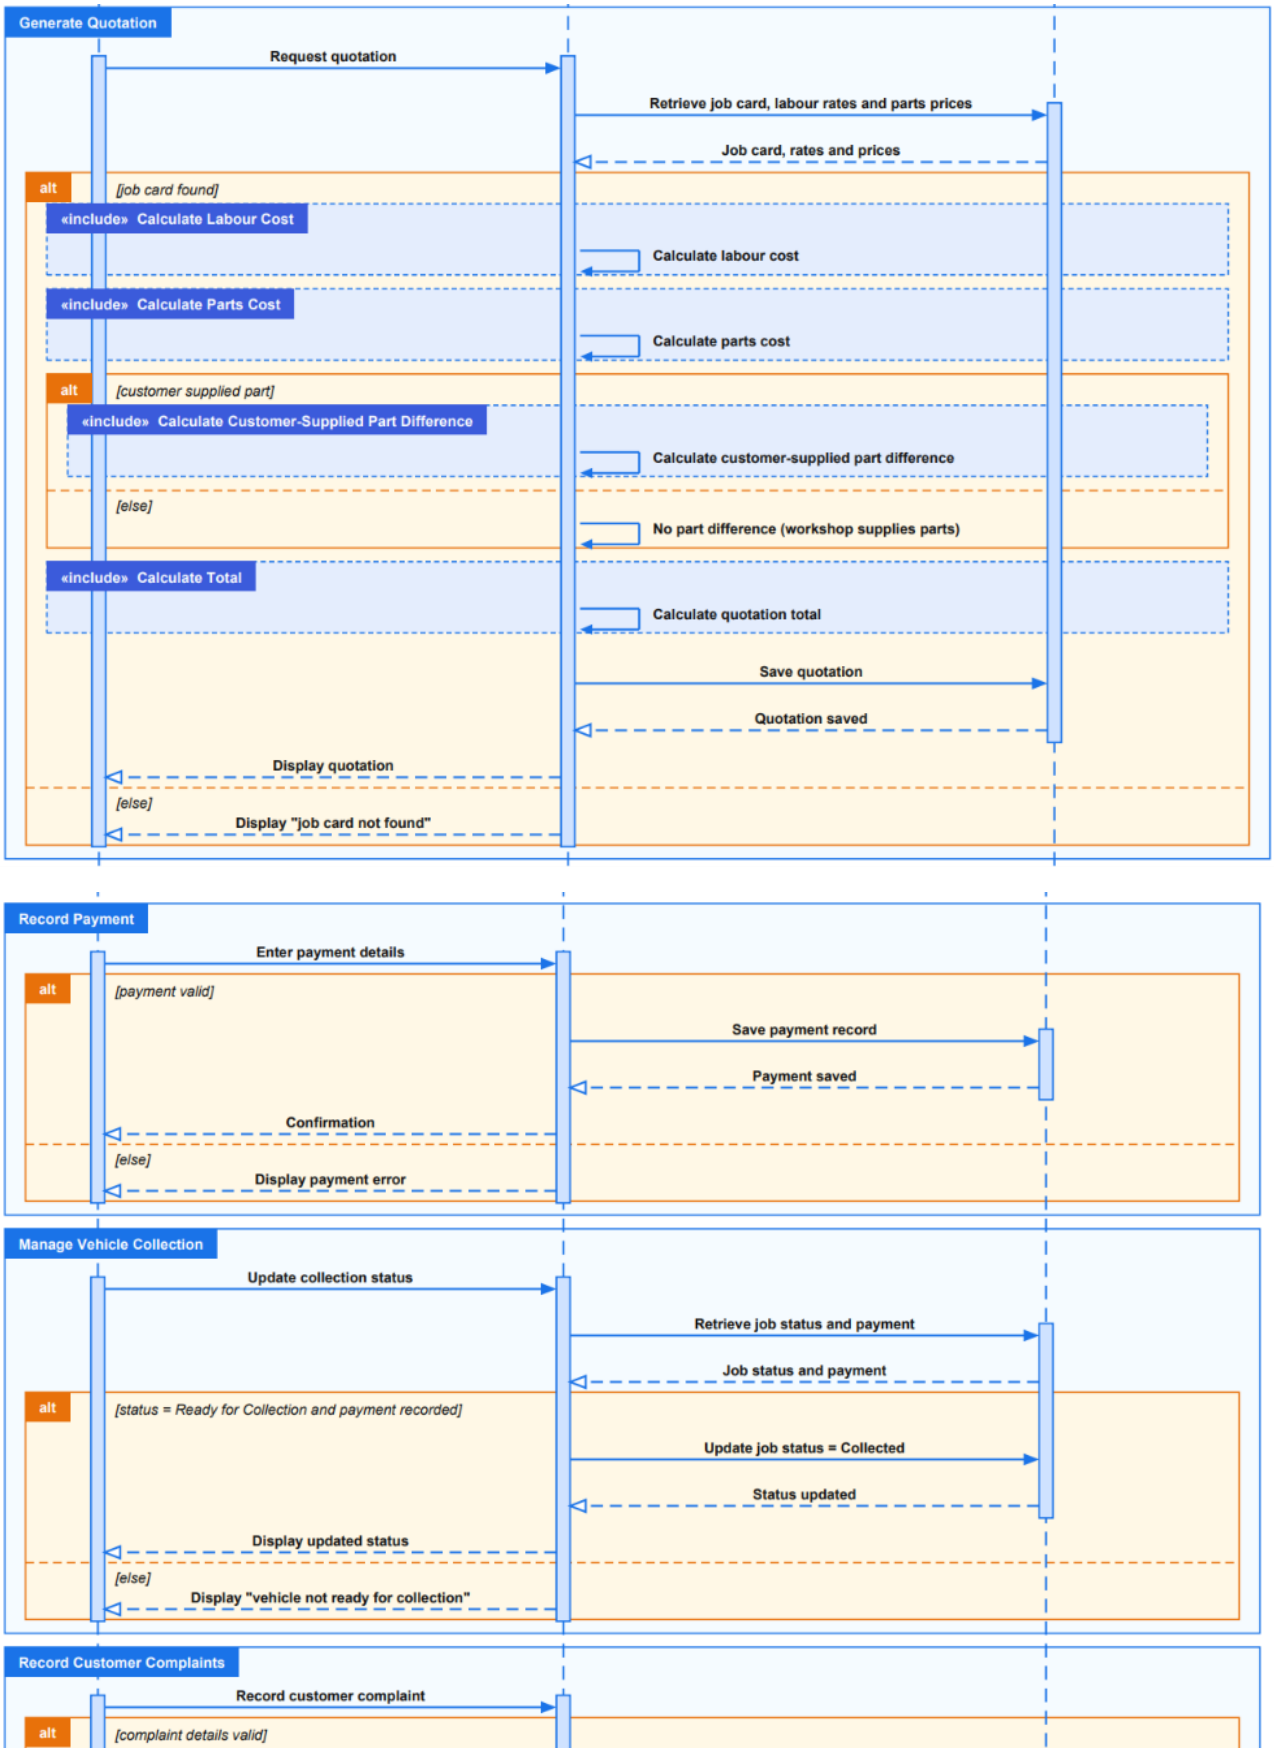
Mister Auto & Turbo – Vehicle Service Management System

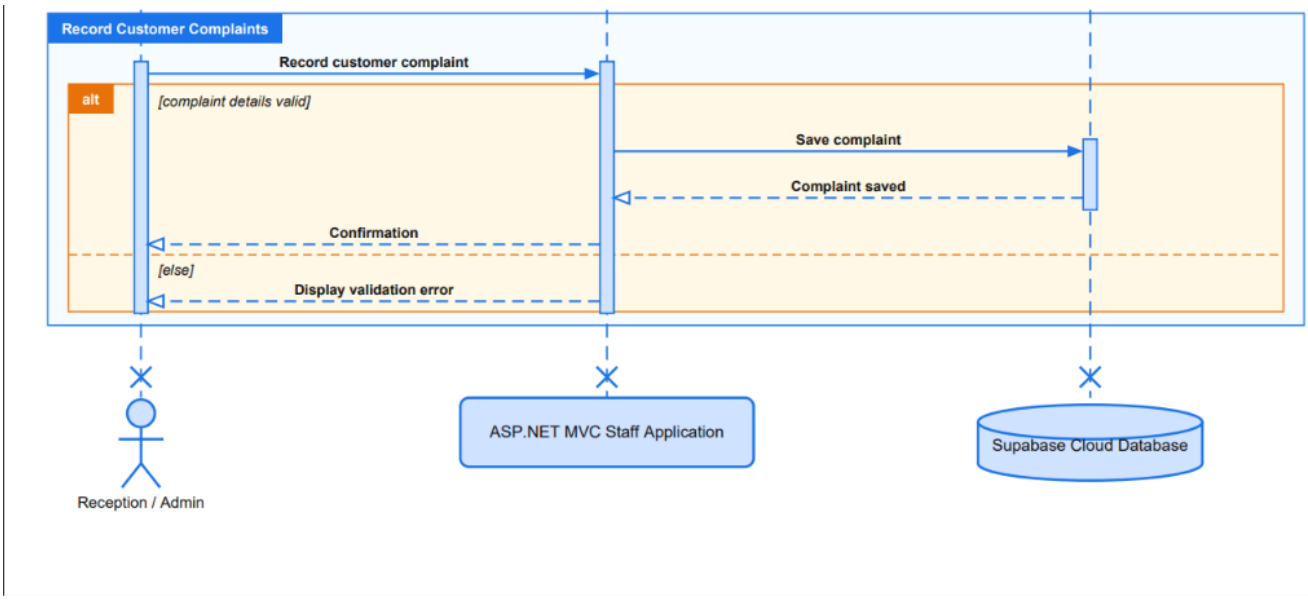
Receptionist / Admin Sequence Diagram

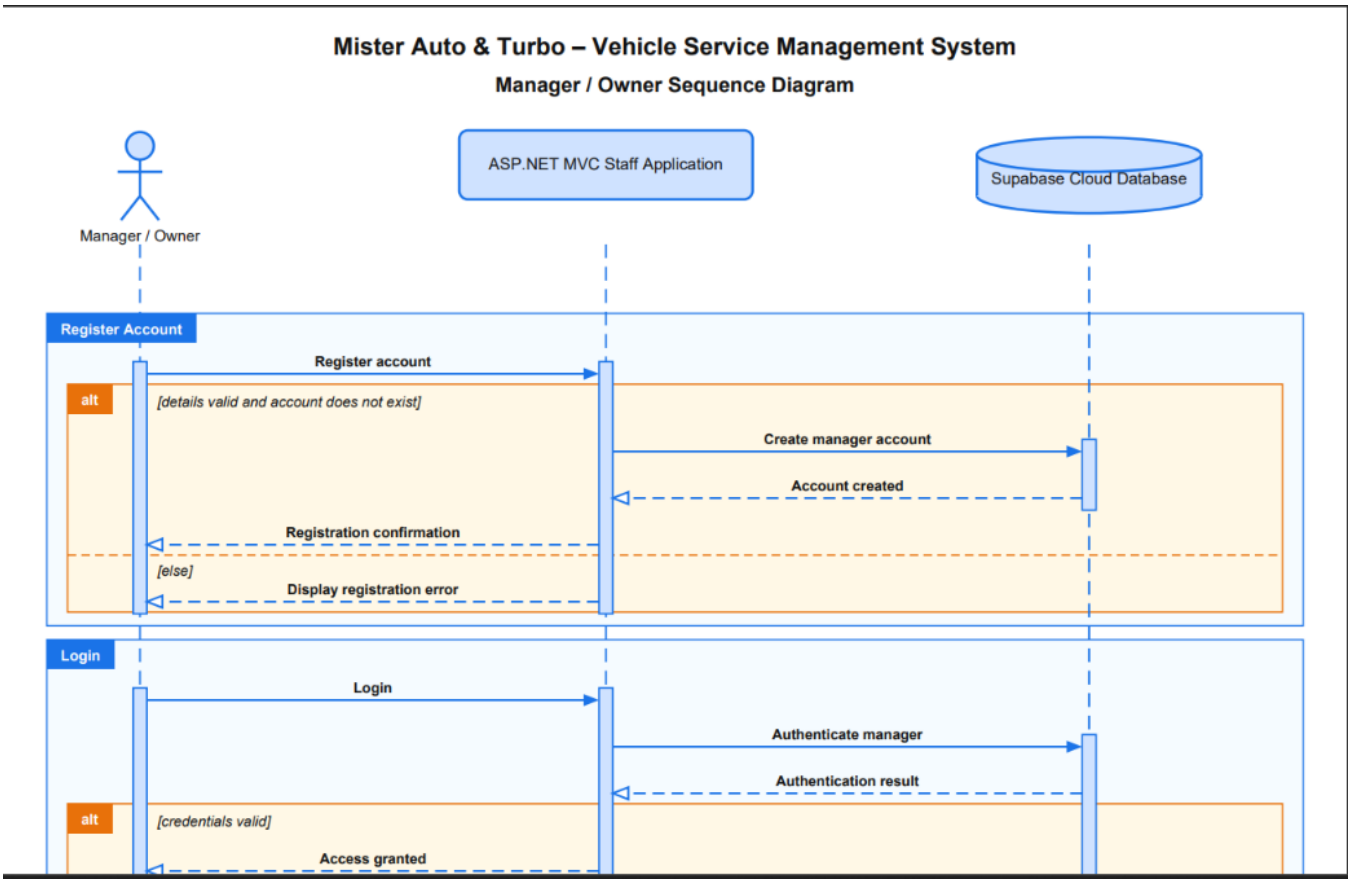


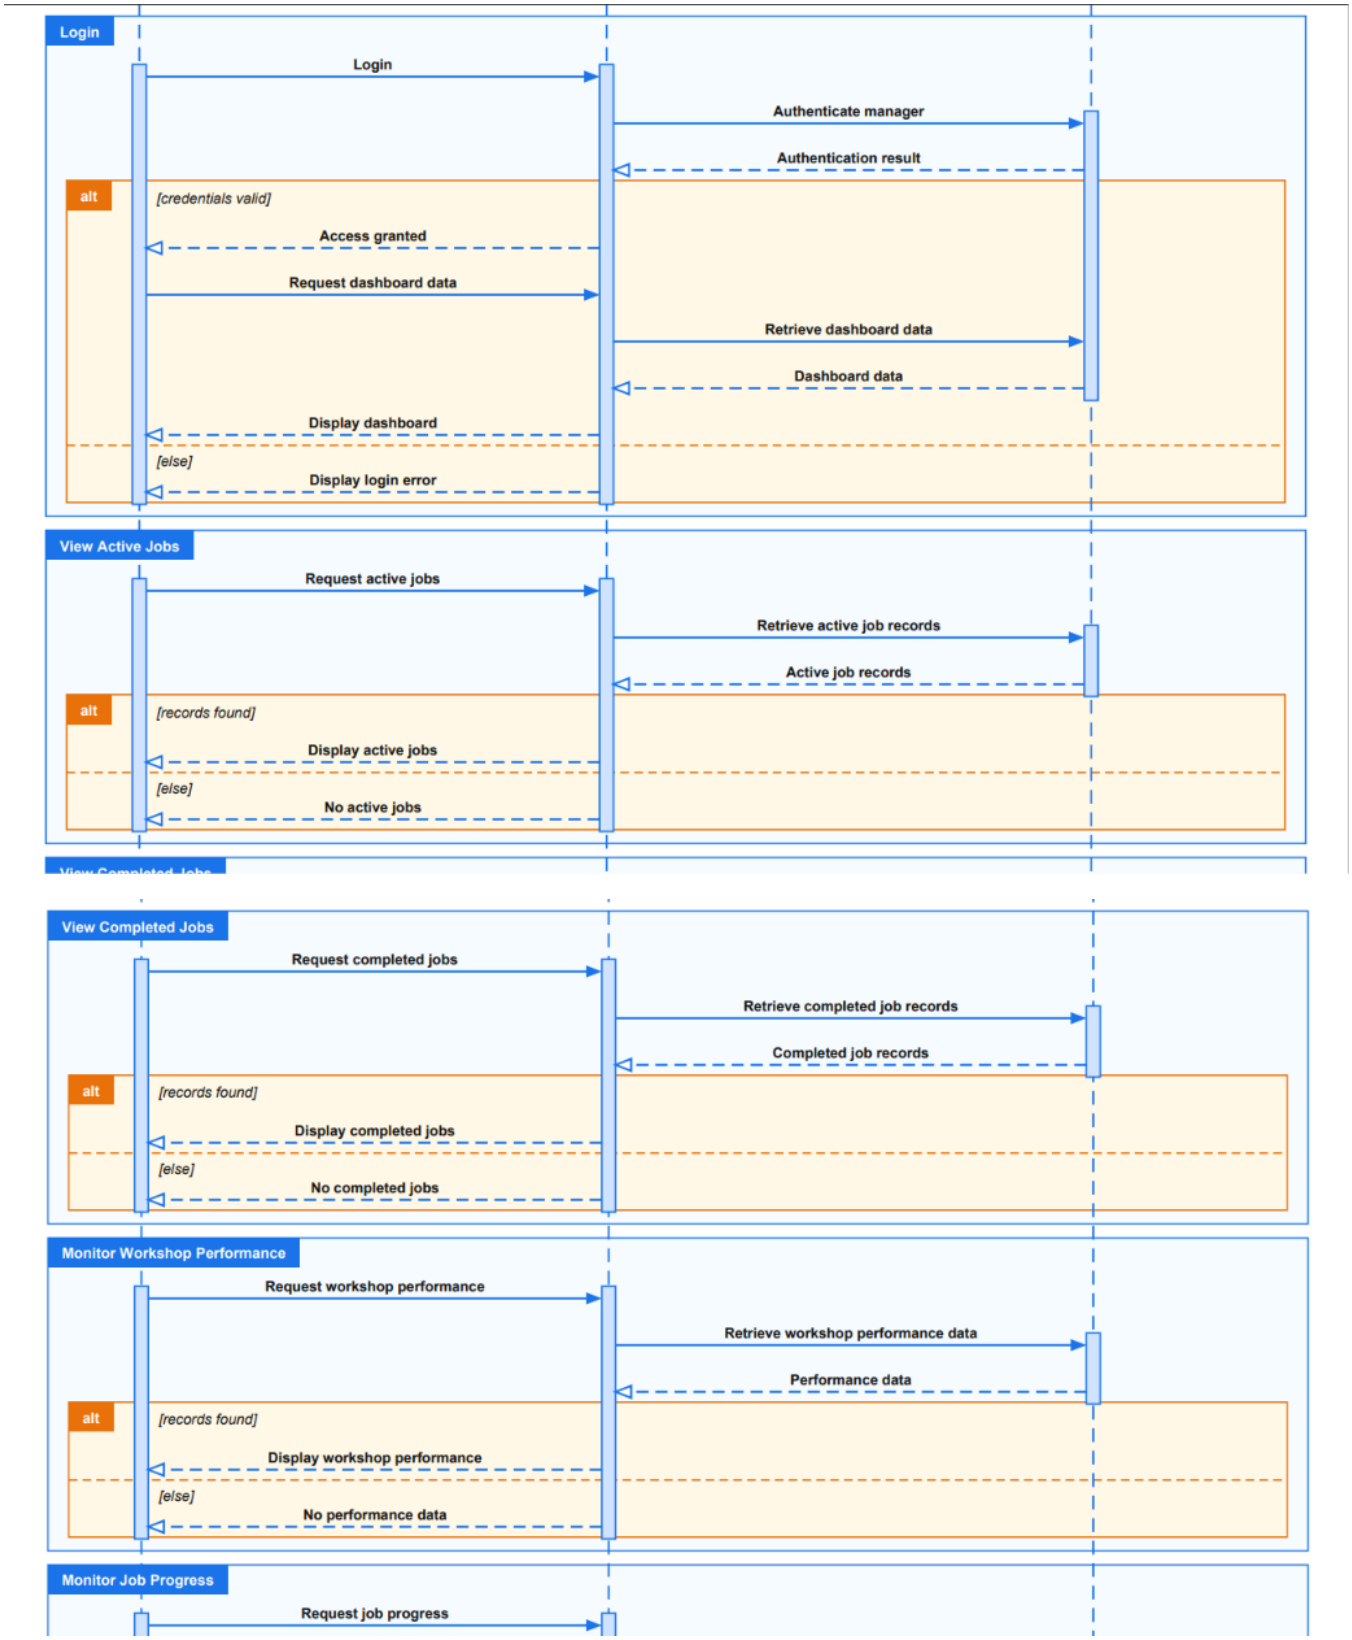

Register Vehicle
Register / update vehicle
Check vehicle record
Vehicle lookup result
alt
[vehicle not registered]
Save new vehicle details
Vehicle record saved
Confirmation
[else vehicle exists]
Update vehicle details
Vehicle record updated
Confirmation
Create Job Card
Create job card
alt
[customer and vehicle registered]
Save job card
Job card saved
Confirmation
[else]
Display "register customer / vehicle first"

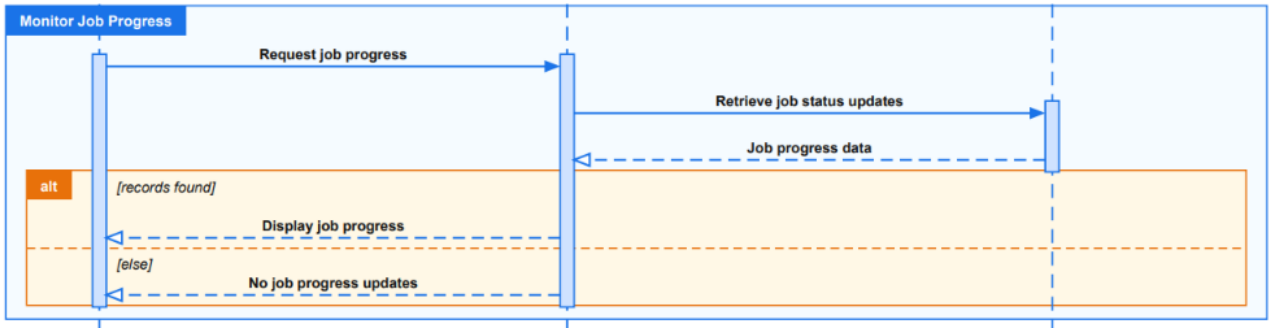

Manage Job Card
Open / update job card
Retrieve job card
Job card details
alt
[job card found]
Display job card
«include» Record Service/Repair Request
Enter service / repair request
Save service / repair request
Request saved
Confirmation
[else]
Display "job card not found"
Generate Quotation
Request quotation
Retrieve job card, labour rates and parts prices
Job card, rates and prices
alt
[job card found]
«include» Calculate Labour Cost
Calculate labour cost

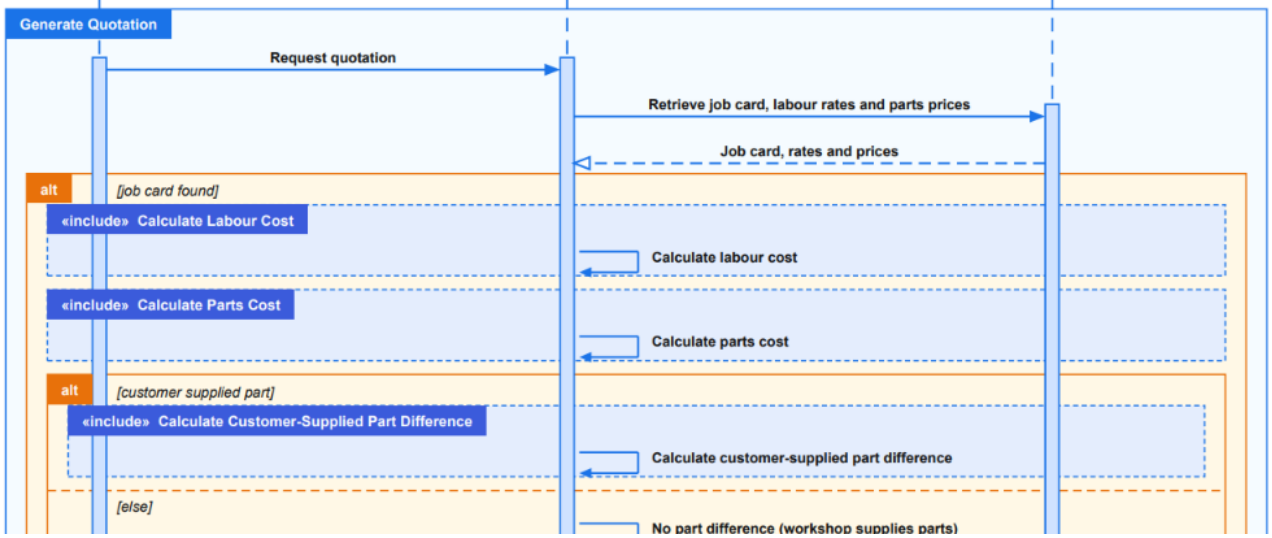

Generate Quotation
Request quotation
Retrieve job card, labour rates and parts prices
Job card, rates and prices
alt
[job card found]
«include» Calculate Labour Cost
Calculate labour cost
«include» Calculate Parts Cost
Calculate parts cost
alt
[customer supplied part]
«include» Calculate Customer-Supplied Part Difference
Calculate customer-supplied part difference
[else]
No part difference (workshop supplies parts)
«include» Calculate Total
Calculate quotation total
Save quotation
Quotation saved
Display quotation
[else]
Display "job card not found"
Record Payment
Enter payment details
alt
[payment valid]
Save payment record
Payment saved
Confirmation
[else]
Display payment error
Manage Vehicle Collection
Update collection status
Retrieve job status and payment
Job status and payment
alt
[status = Ready for Collection and payment recorded]
Update job status = Collected
Status updated
Display updated status
[else]
Display "vehicle not ready for collection"
Record Customer Complaints
Record customer complaint
alt
[complaint details valid]

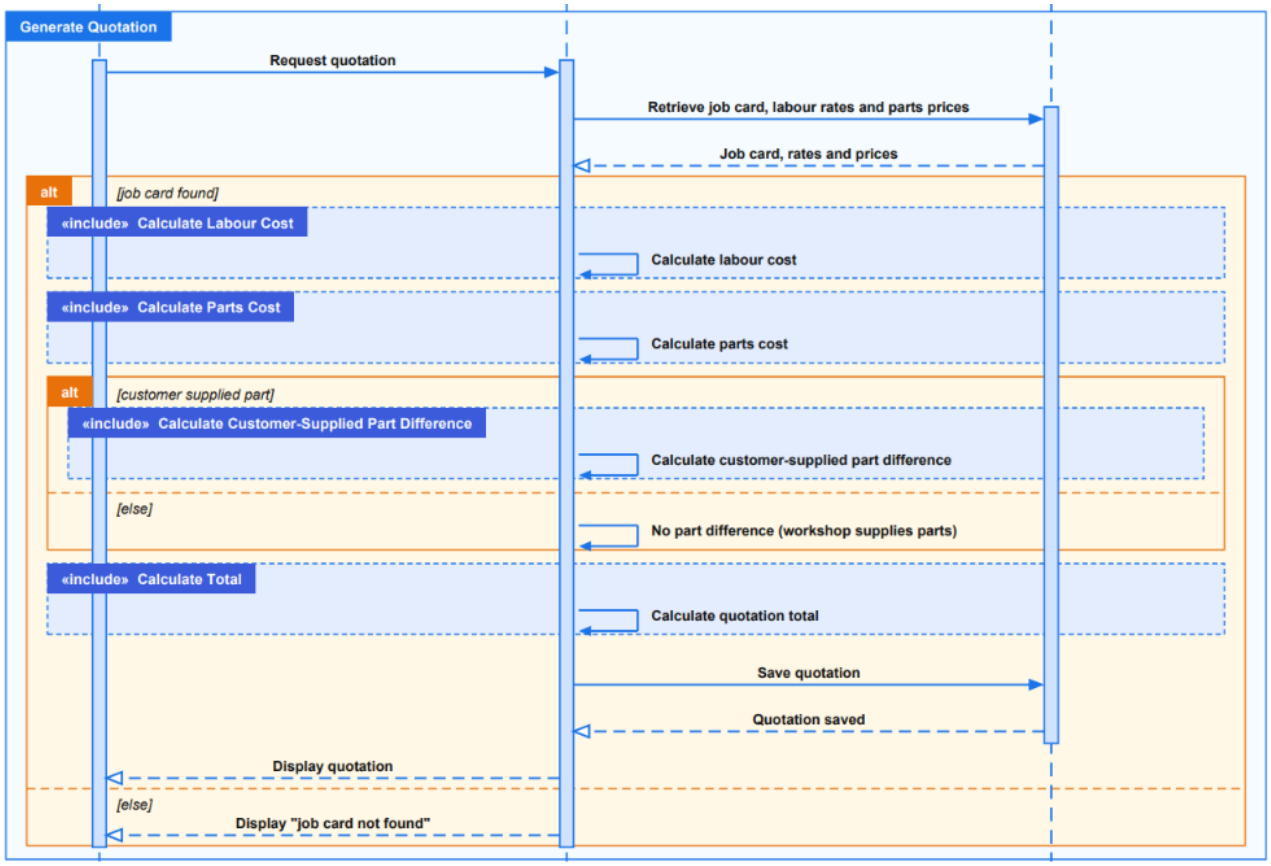

Record Customer Complaints
Record customer complaint
alt
[complaint details valid]
Save complaint
Complaint saved
Confirmation
[else]
Display validation error
Reception / Admin
ASP.NET MVC Staff Application
Supabase Cloud Database

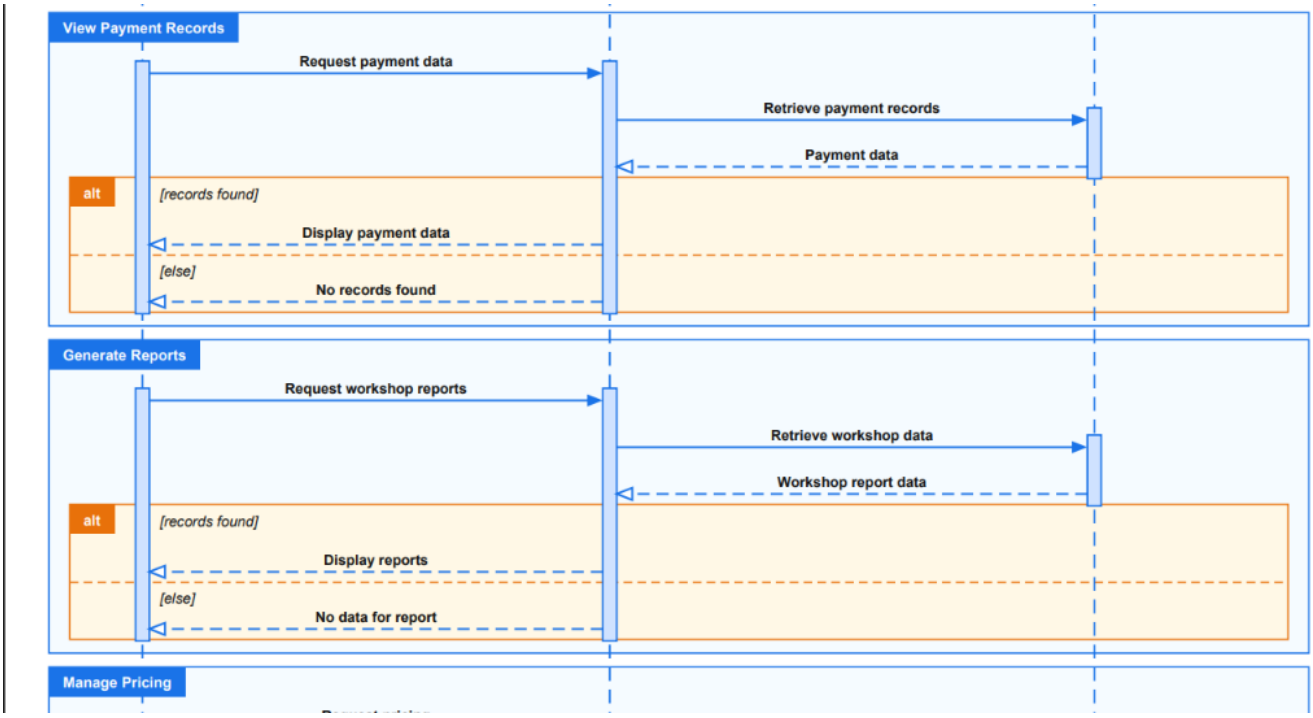

Mister Auto & Turbo – Vehicle Service Management System
Manager / Owner Sequence Diagram
Manager / Owner
ASP.NET MVC Staff Application
Supabase Cloud Database
Register Account
Register account
alt
[details valid and account does not exist]
Create manager account
Account created
Registration confirmation
[else]
Display registration error
Login
Login
Authenticate manager
Authentication result
alt
[credentials valid]
Access granted

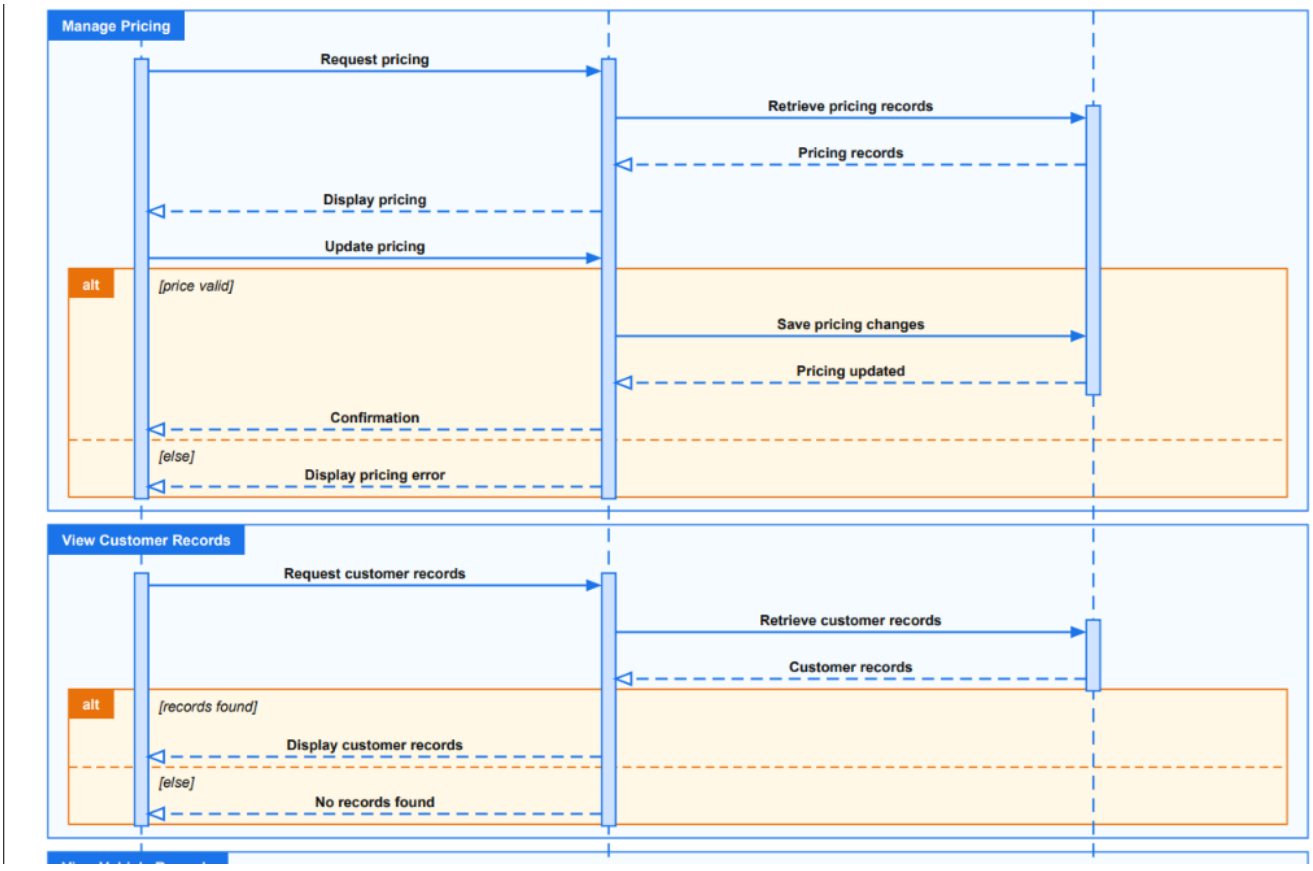

Login
Login
Authenticate manager
Authentication result
alt
[credentials valid]
Access granted
Request dashboard data
Retrieve dashboard data
Dashboard data
Display dashboard
[else]
Display login error
View Active Jobs
Request active jobs
Retrieve active job records
Active job records
alt
[records found]
Display active jobs
[else]
No active jobs
View Completed Jobs
Request completed jobs
Retrieve completed job records
Completed job records
alt
[records found]
Display completed jobs
[else]
No completed jobs
Monitor Workshop Performance
Request workshop performance
Retrieve workshop performance data
Performance data
alt
[records found]
Display workshop performance
[else]
No performance data
Monitor Job Progress
Request job progress

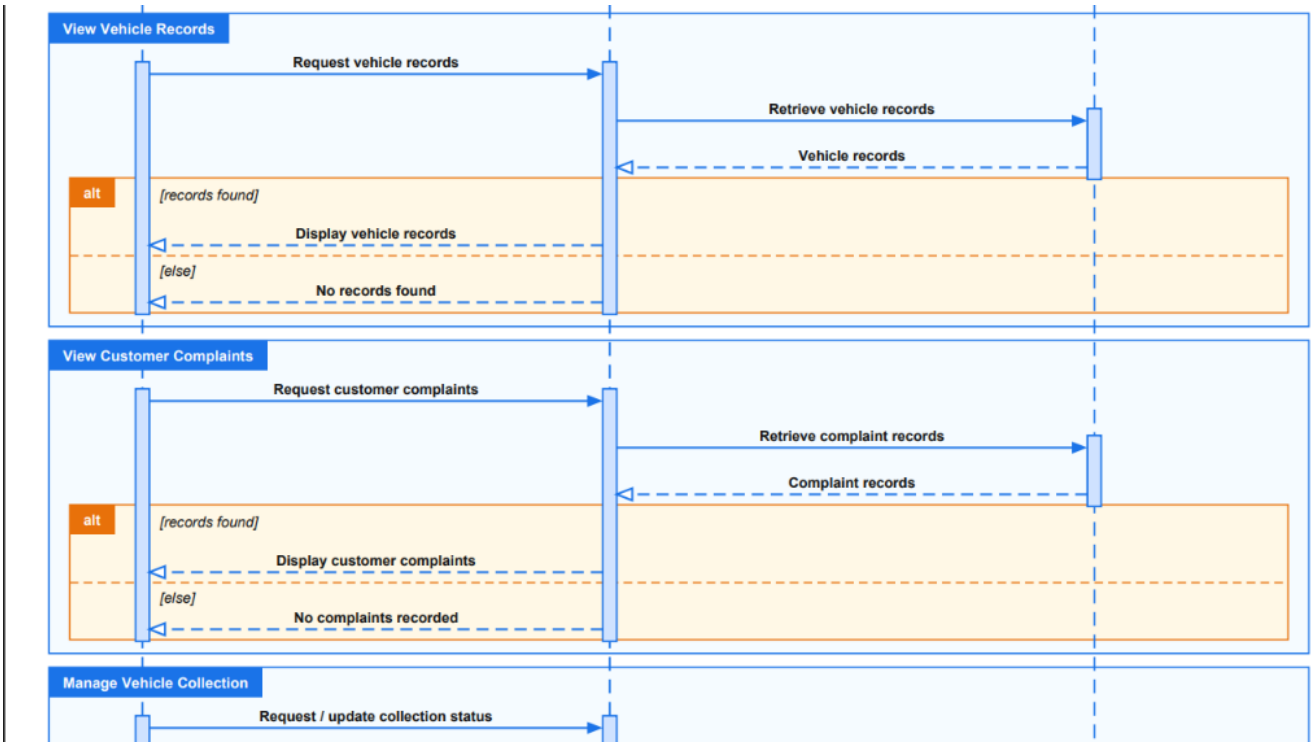

Monitor Job Progress
Request job progress
Retrieve job status updates
Job progress data
alt
[records found]
Display job progress
[else]
No job progress updates

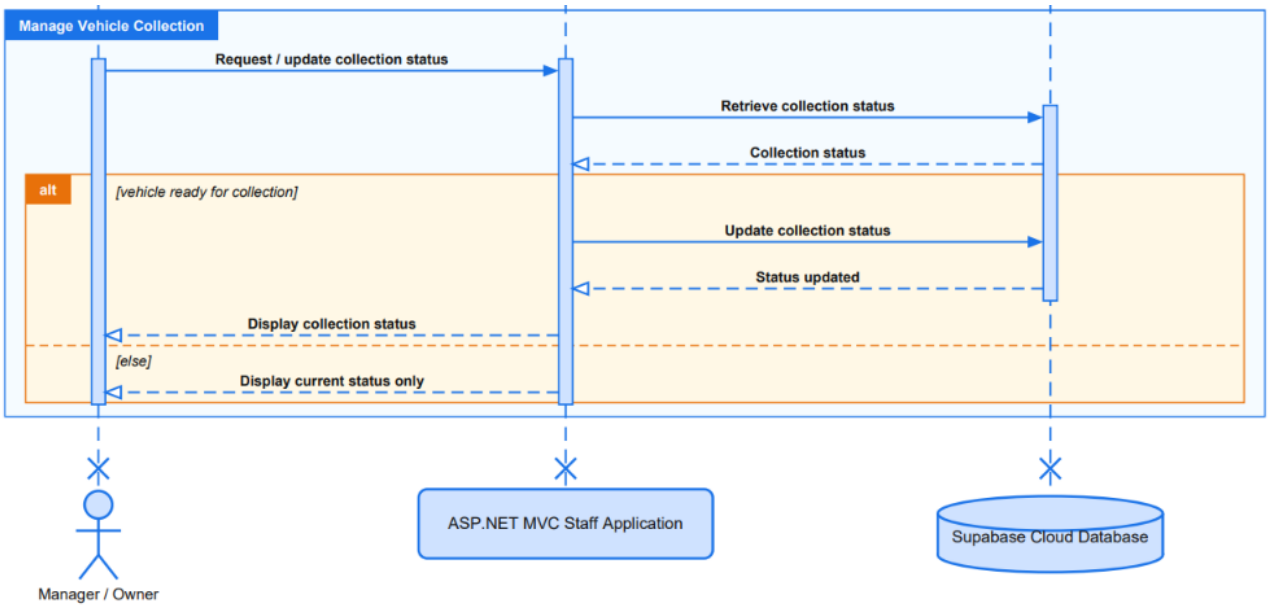

Generate Quotation
Request quotation
Retrieve job card, labour rates and parts prices
Job card, rates and prices
alt
[job card found]
«include» Calculate Labour Cost
Calculate labour cost
«include» Calculate Parts Cost
Calculate parts cost
alt
[customer supplied part]
«include» Calculate Customer-Supplied Part Difference
Calculate customer-supplied part difference
[else]
No part difference (workshop supplies parts)

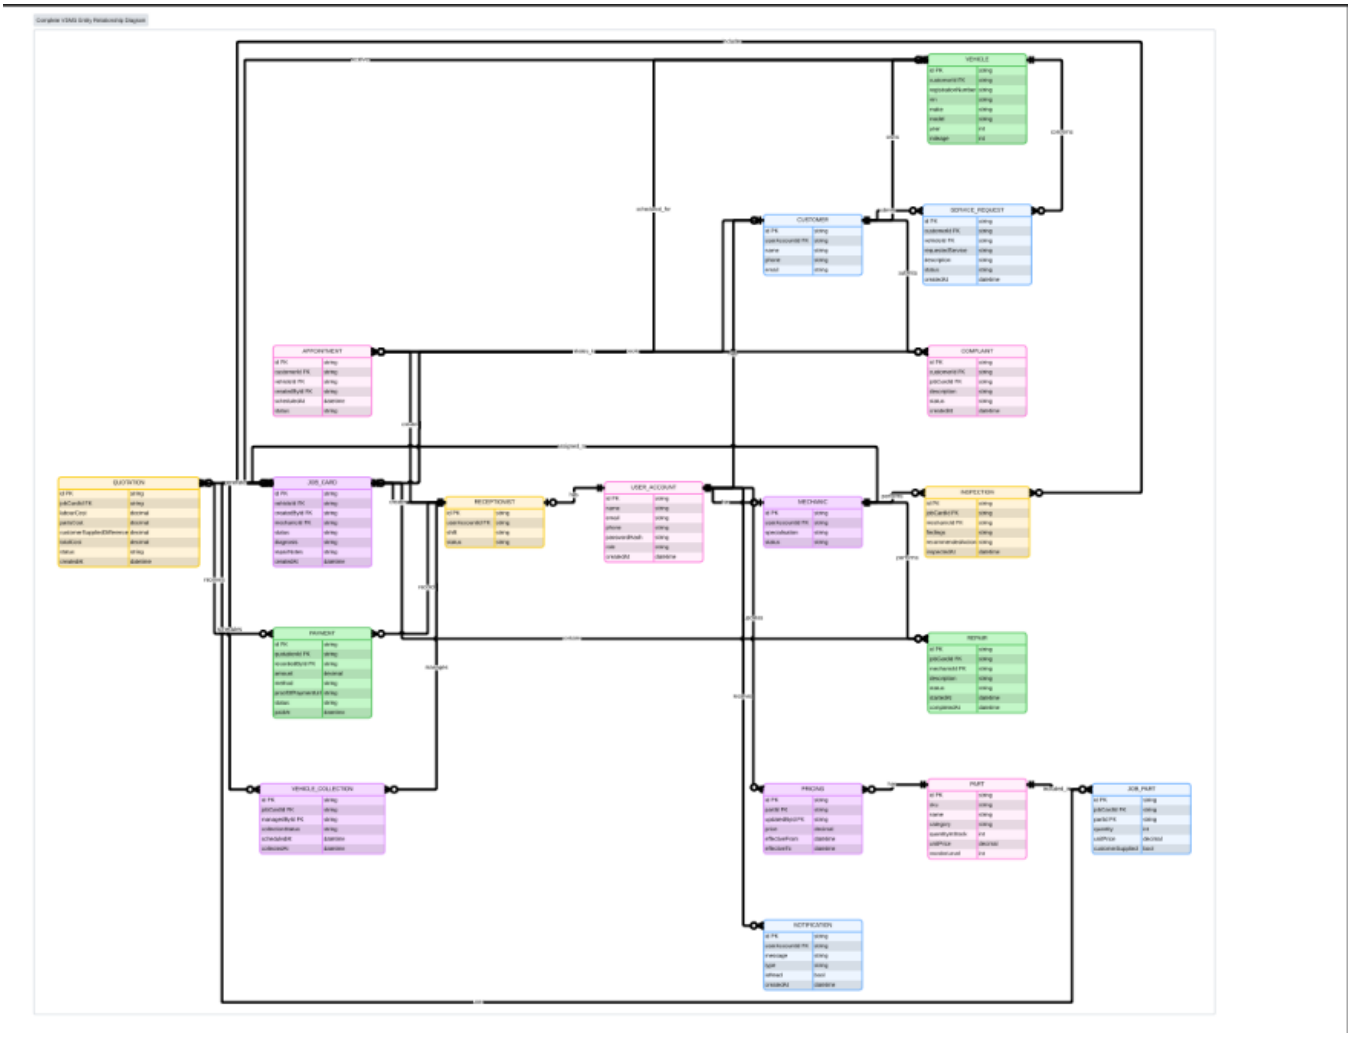

Generate Quotation
Request quotation
Retrieve job card, labour rates and parts prices
Job card, rates and prices
alt
[job card found]
«include» Calculate Labour Cost
Calculate labour cost
«include» Calculate Parts Cost
Calculate parts cost
alt
[customer supplied part]
«include» Calculate Customer-Supplied Part Difference
Calculate customer-supplied part difference
[else]
No part difference (workshop supplies parts)
«include» Calculate Total
Calculate quotation total
Save quotation
Quotation saved
Display quotation
[else]
Display "job card not found"


View Payment Records
Request payment data
Retrieve payment records
Payment data
alt
[records found]
Display payment data
[else]
No records found
Generate Reports
Request workshop reports
Retrieve workshop data
Workshop report data
alt
[records found]
Display reports
[else]
No data for report
Manage Pricing


Manage Pricing
Request pricing
Retrieve pricing records
Pricing records
Display pricing
Update pricing
alt
[price valid]
Save pricing changes
Pricing updated
Confirmation
[else]
Display pricing error
View Customer Records
Request customer records
Retrieve customer records
Customer records
alt
[records found]
Display customer records
[else]
No records found


View Vehicle Records
Request vehicle records
Retrieve vehicle records
Vehicle records
alt
[records found]
Display vehicle records
[else]
No records found
View Customer Complaints
Request customer complaints
Retrieve complaint records
Complaint records
alt
[records found]
Display customer complaints
[else]
No complaints recorded
Manage Vehicle Collection
Request / update collection status


Manage Vehicle Collection
Request / update collection status
Retrieve collection status
Collection status
alt
[vehicle ready for collection]
Update collection status
Status updated
Display collection status
[else]
Display current status only
Manager / Owner
ASP.NET MVC Staff Application
Supabase Cloud Database



4. Use Case Summary

This table summarises the use cases represented in the group's Use Case Diagram, for reference alongside the diagram in the SRS.

Use Case	Primary Actor	Includes / Extends
Sign In (OTP)	All actors	-
Register Customer	Receptionist	-
Register Vehicle / Check-In Vehicle	Receptionist	<<include>> Register Customer (if new)
Book Appointment	Receptionist	-
Create Job Card	Receptionist, Mechanic	<<include>> Register Vehicle
Conduct Inspection	Mechanic	<<extend>> Create Job Card

Use Case	Primary Actor	Includes / Extends
Update Repair Status	Mechanic	-
Request / Manage Parts	Mechanic, Administrator	-
Record Payment	Administrator	-
Confirm Vehicle Collection	Receptionist	<<include>> Record Payment (if outstanding)
Log Customer Complaint	Receptionist	-
Track Vehicle Status	Customer	-
Receive Notifications	Customer, Mechanic	-
Manage Staff / Users	Administrator	-
View Reports	Administrator	-

5. Database Entity Summary

This table summarises the entities represented in the group's ERD, for reference alongside the diagram in the SRS.

Entity	Purpose	Key Relationships
Customer	Stores customer contact and account details.	One customer has many Vehicles; many Complaints; many Payments.
Vehicle	Stores registration, make, model, and condition details.	Belongs to one Customer; has many Jobs.
Job	Represents a repair/service job card and its current status.	Belongs to one Vehicle; linked to one Mechanic (User); has many Parts Used and Labour entries.
Appointment	Stores scheduled workshop visits.	Linked to one Customer and one Vehicle.
Part	Inventory item with stock level and pricing.	Linked to Jobs via a Job Parts junction table (many-to-many).
Payment	Records an amount paid against a Job invoice.	Belongs to one Job.
Complaint	Records a customer complaint or review.	Belongs to one Customer; optionally linked to one Job.
User (Staff)	Administrator, Receptionist, or Mechanic account.	A Mechanic User is linked to many Jobs.

6. Interface Design Summary

This table lists the main screens produced for the Flutter mobile application and ASP.NET web application, linking each to its primary use case.

reception – r...



reception – l...



reception – dashbo...



reception –vehicles



reception –add ve...



reception – Vehicl...



reception – repair/jo...



reception – create ...



Reception compla...



reception – custo...



reception – add cu...



reception – custo...



reception – appoin...



reception – collect...



Forgot password



Login



my jobs today



jobs



vehicles Lookup



appointments



Parts & inventory



add-vehicles



new appointment

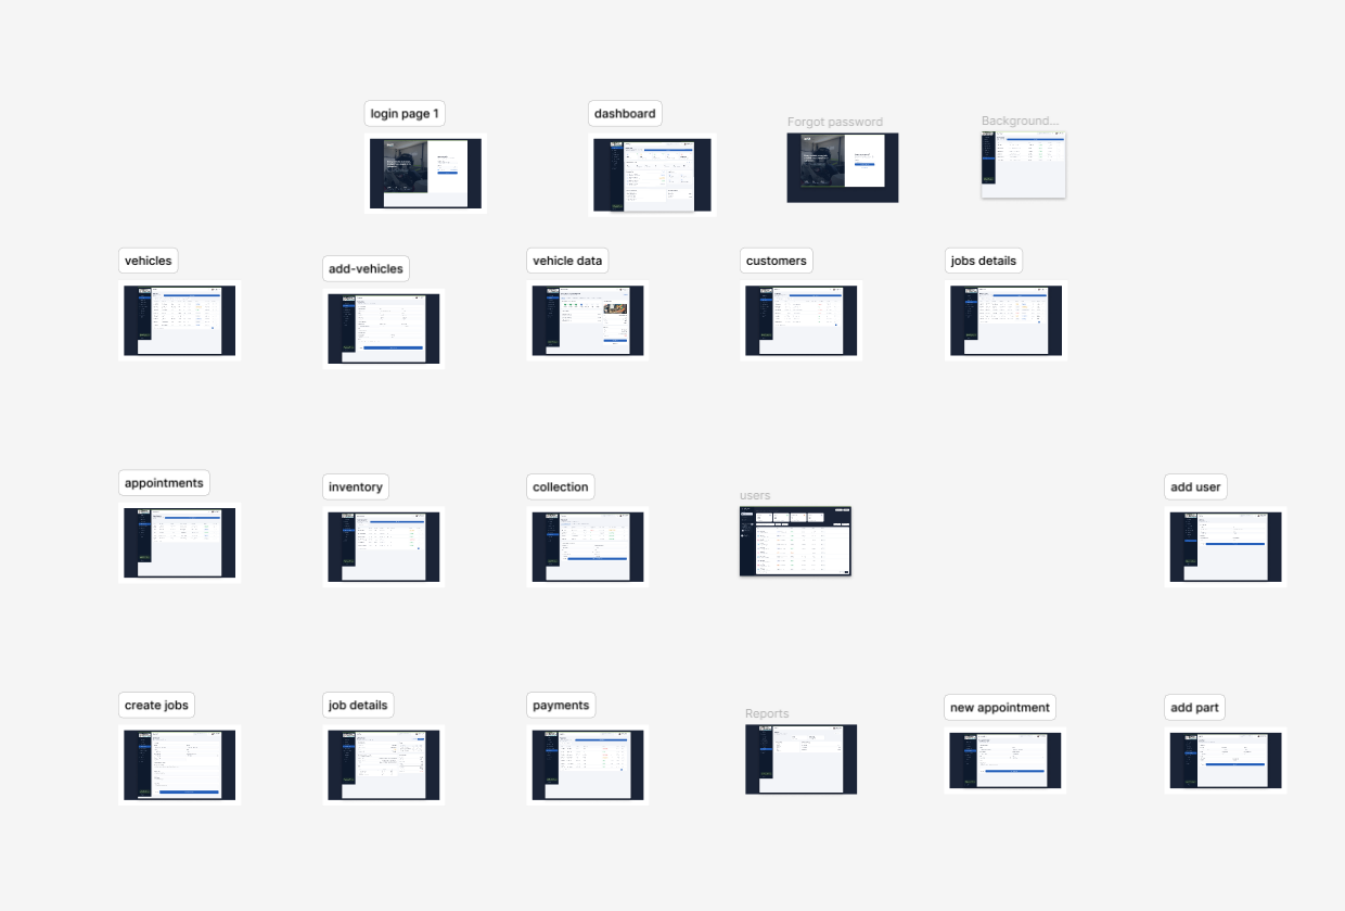


add part



vehicle data





Screen / Page	Platform	Role	Related Use Case
Login + OTP Verification	Flutter	All	Sign In (OTP)
Vehicle Status & Timeline	Flutter	Customer	Track Vehicle Status
Notifications	Flutter	Customer, Mechanic	Receive Notifications
Payments / Invoice	Flutter	Customer	Record Payment (view)
My Jobs / Job Detail	Flutter	Mechanic	Update Repair Status
Dashboard	ASP.NET	Administrator	View Reports
Vehicles / Add Vehicle	ASP.NET	Receptionist	Register Vehicle
Customers / Add Customer / Customer Details	ASP.NET	Receptionist	Register Customer
Appointments / New Appointment	ASP.NET	Receptionist	Book Appointment
Jobs / Create Job / Job Card	ASP.NET	Receptionist, Mechanic	Create Job Card
Job Card - Status Picker & Inspection Checklist	ASP.NET	Mechanic	Conduct Inspection, Update Repair Status

Screen / Page	Platform	Role	Related Use Case
Parts / Inventory / Add Part	ASP.NET	Administrator, Mechanic	Request / Manage Parts
Payments / Record Payment	ASP.NET	Administrator	Record Payment
Collection	ASP.NET	Receptionist	Confirm Vehicle Collection
Customer Complaints	ASP.NET	Receptionist	Log Customer Complaint
Users / Add User	ASP.NET	Administrator	Manage Staff / Users
Reports	ASP.NET	Administrator	View Reports

7. Design Alignment Table

This table demonstrates that the architecture, use cases, database design, and interfaces describe the same, consistent system, as required by the rubric.

Requirement	Use Case	ERD Entity	Interface
Customer can track repair status remotely	Track Vehicle Status	Job, Vehicle	Flutter - Vehicle Status & Timeline
Front desk can register new customers and vehicles	Register Customer, Register Vehicle	Customer, Vehicle	ASP.NET - Add Customer, Add Vehicle
Mechanic can update job status and log inspection findings	Conduct Inspection, Update Repair Status	Job	ASP.NET - Job Card (status picker + checklist)
Only management can process payments	Record Payment	Payment, Job	ASP.NET - Payments (Admin only; hidden from Receptionist)
Customers and staff receive real-time updates	Receive Notifications	Job, User	Flutter - Notifications
Workshop can track and request parts	Request / Manage Parts	Part, Job	ASP.NET - Parts / Inventory
Front desk can log and track customer complaints	Log Customer Complaint	Complaint, Customer	ASP.NET - Customer Complaints

8. Original Design Source Links

Design Artefact	Tool Used	Link / File Location
System Architecture Diagram	LucidChart	File is attached
Use Case Diagram	Draw.io	File is attached
Sequence Diagram 1 (Flutter ↔ Supabase)	LucidChart	File is attached
Sequence Diagram 2 (ASP.NET ↔ Supabase)	LucidChart	File is attached
ERD	LucidChart,	File is attached
Flutter Mobile Interface Design (Every interface combined)	Figma	https://www.figma.com/design/kEyegKqrF78iY3xdtU5Xaq/WebVortex---Mr-Auto-Desktop?t=vk6XPei7YKP2Kxgn-1
ASP.NET Web Interface Design for desktops	Figma	https://www.figma.com/design/IhomVdDBHY9DbSQzEv50WM/Desktop-WebVortex?t=vk6XPei7YKP2Kxgn-1
Flutter Mobile Interface Design	Figma	https://www.figma.com/design/xfaNqX7d1PSMdKE3YC4z9r/customer-proto?node-id=0-1&t=epaBJOw8dWZSNJaq-1

MR AUTO & TURBO

Stakeholder Review & Approval - Phase 2 System Design

This page confirms that the stakeholder listed below has reviewed the Phase 2 system design for the Mr Auto & Turbo Workshop Management System, prepared as part of the ITC327W Work-Integrated Learning module (Central University of Technology, Free State).

Project

Mr Auto & Turbo Workshop Management System - a Flutter mobile application and ASP.NET web application, sharing a Supabase backend, designed to manage customers, vehicles, repair jobs, appointments, parts, payments, and complaints for the workshop.

Artefacts Reviewed

Artefact	Reviewed
System Architecture Diagram	☑Yes ☐ No
Use Case Diagram	☑Yes ☐ No
Sequence Diagrams	☑ Yes ☐ No
Entity Relationship Diagram (ERD)	☑ Yes ☐ No
Flutter Mobile Interface Design	☑Yes ☐ No
ASP.NET Web Interface Design	☑ Yes ☐ No

Stakeholder Statement

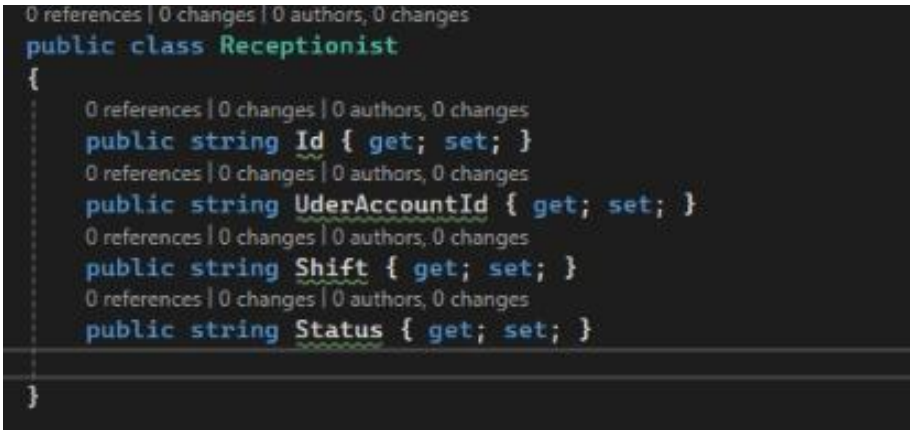
I, the undersigned, confirm that I have reviewed the system design listed above, prepared by the project group for Mr Auto & Turbo. I confirm that the design reflects the business needs and workflow discussed with the group, and I approve the group to proceed to the next phase of development on this basis.

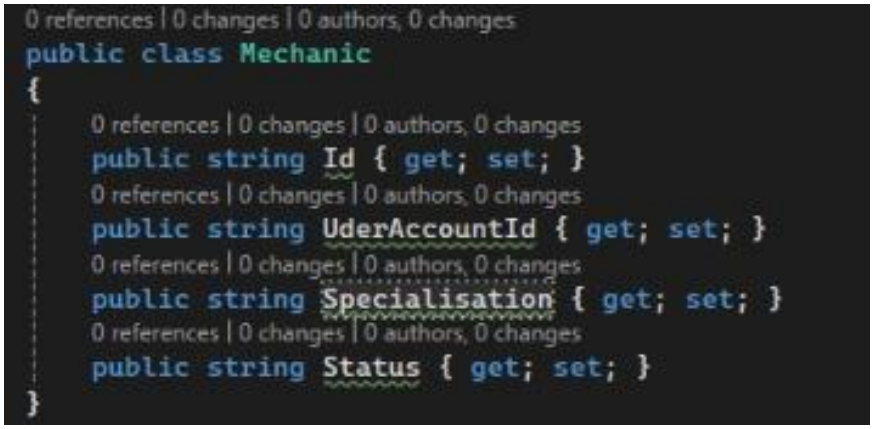
I understand that this design may be refined during development, and that any significant change to scope will be discussed with me before implementation.

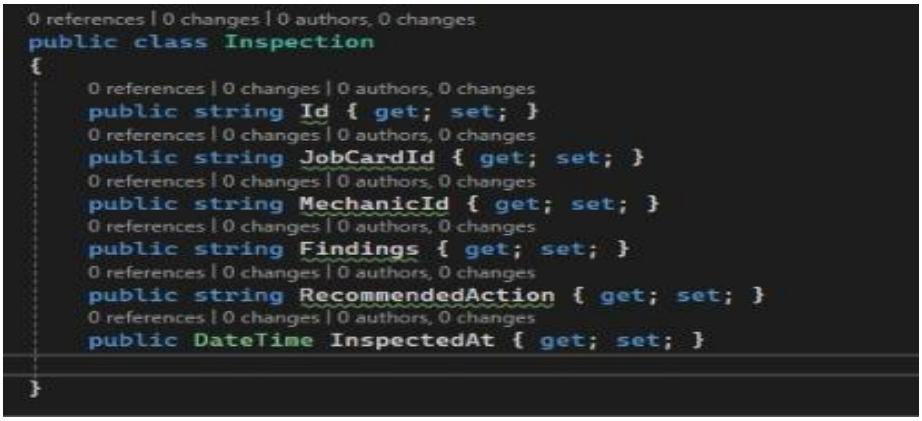
Signatures

	Name	Signature/Student no.	Date
Stakeholder	Motlokoa Tsotesi (Owner, Mr Auto & Turbo)		25/09/26

	Name	Signature/Student no.	Date
Group Member 1	Lefa Lipali	215135458	25/09/26
Group Member 2	Ndivhuwo Netshituka	223013773	25/09/26
Group Member 3	Rotondwa Madi	222066543	25/09/26
Group Member 4	Lehlokoa Pule	219002738	25/09/26
Group Member 5	Lekete Letsie	224099468	25/09/26

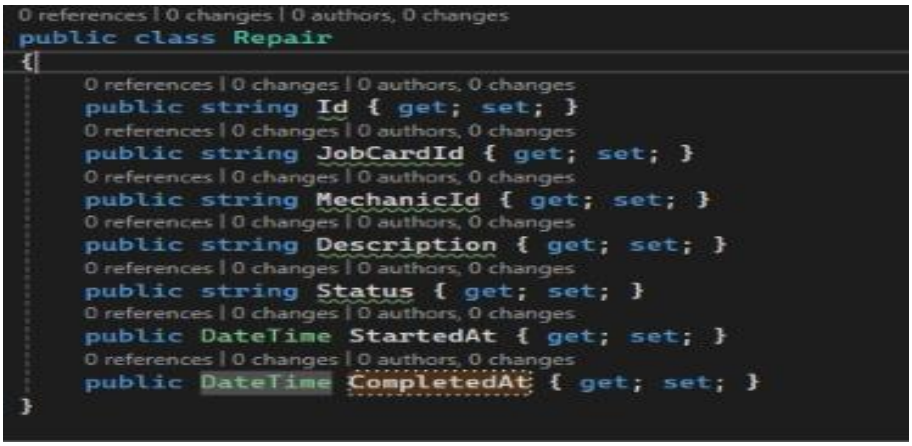







```
0 references | 0 changes | 0 authors, 0 changes
public class Inspection
{
    0 references | 0 changes | 0 authors, 0 changes
    public string Id { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public string JobCardId { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public string MechanicId { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public string Findings { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public string RecommendedAction { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public DateTime InspectedAt { get; set; }

}
```



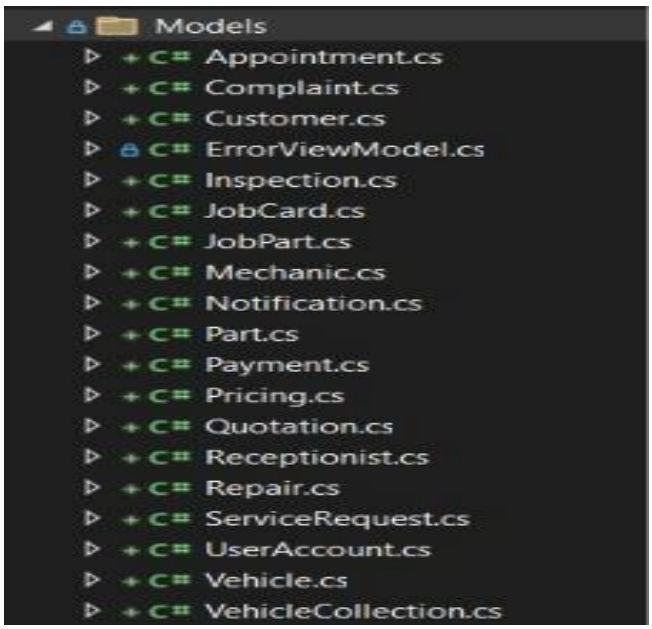
```
0 references | 0 changes | 0 authors, 0 changes
public class Repair
{
    0 references | 0 changes | 0 authors, 0 changes
    public string Id { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public string JobCardId { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public string MechanicId { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public string Description { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public string Status { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public DateTime StartedAt { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public DateTime CompletedAt { get; set; }
}
```



```
0 references | 0 changes | 0 authors, 0 changes
public class VehicleCollection
{
    0 references | 0 changes | 0 authors, 0 changes
    public string Id { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public string JobCardId { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public string ManagedById { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public string CollectionStatus { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public DateTime ScheduledAt { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public DateTime CollectedAt { get; set; }
}
```

```
0 references | 0 changes | 0 authors, 0 changes
public class Part
{
    0 references | 0 changes | 0 authors, 0 changes
    public string Id { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public string StockKeepingUnit { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public string Name { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public string Category { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public int QuantityInStock { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public decimal UnitPrice { get; set; }
    0 references | 0 changes | 0 authors, 0 changes
    public int ReorderLevel { get; set; }

}
```





Progress Tracker

Task Progress Tracker														
Task ID	Reporting Phase	Activity	Task Description	Assigned Student(s)	Start Date	Due Date	Status	% Complete	Evidence / Link	Verified by Group	Lecturer Comment	Progress Flag		
U1-01	Unit 1 / Phase 1	Activity 1.1	Identify and confirm the external stakeholder	LE Letsie	25/08/2026	26/08/2026	Completed	100%	Signed Stakeholder Cooperation & Information Use Agreement (Appendix B) with Mister Auto & Turbo, dated 25/08/2026.	Yes		Completed		
U1-02	Unit 1 / Phase 1	Activity 1.1	Document the current process and problem	RG Madi	25/08/2026	26/08/2026	Completed	100%	SRS Section 3 (Problem Statement), Section 9 (Current Process and Diagram) and Appendix D (Current Process	Yes		Completed		
U1-03	Unit 1 / Phase 1	Activity 1.1	Define the project aim, objectives and scope	NM Netshituka	25/08/2026	26/08/2026	Completed	100%	SRS Section 4 (Aim and Objectives) and Section 5 (Project	Yes		Completed		
U1-04	Unit 1 / Phase 1	Activity 1.2	Prepare stakeholder interview questions	LE Lipali	25/08/2026	26/08/2026	Completed	100%	Stakeholder needs SN-01–SN-05 documented in SRS Section 8.2, drawn from prepared interview/engagement questions.	Yes		Completed		
U1-05	Unit 1 / Phase 1	Activity 1.2	Conduct and document the stakeholder interview	LTBG Pule	25/08/2026	26/08/2026	Completed	100%	SRS Appendix C (Stakeholder Interview Findings) and Section	Yes		Completed		
U1-06	Unit 1 / Phase 1	Activity 1.3	Compile the initial SRS	Group	25/08/2026	26/08/2026	Completed	100%	This Web Vortex WIL document — full initial SRS including scope, functional/non-functional requirements, system requirements, integration requirements and MoSCoW prioritisation.	Yes		Completed		
U1-07	Unit 1 / Phase 1	Activity 1.3	Create the initial Microsoft Project schedule	LE Letsie			Completed	100%		Yes		Completed		
U1-08	Unit 1 / Phase 1	Activity 1.3	Create and configure the GitHub repository	LE Lipali	30/08/2026	30/08/2026	Completed	100%		Yes		Completed		
U1-09	Unit 1 / Phase 1	Activity 1.3	Create the initial Supabase project	LE Lipali	30/08/2026	30/08/2026	Completed	100%		Yes		Completed		
U1-10	Unit 1 / Phase 1	Activity 1.3	Complete the progress report and contribution record	NM Netshituka	27/08/2026	31/08/2026	Completed	100%	This progress tracker workbook, being completed from the SRS.	Yes		Completed		
U1-11	Unit 1 / Phase 1	Activity 1.3	Complete the Unit 1 group reflection	RG Madi	28/08/2026	28/08/2026	Completed	100%		Yes		Completed		
U2-01	Phase 2	Activity 2.1	Design the system architecture	LE Lipali	22/09/2026	22/09/2026	Completed	100%	SRS Phase 2 System Design Section 2 (System Overview) and Section 8 (Original Design Source Links): System Architecture	Yes		Completed		
U2-02	Phase 2	Activity 2.1	Model the system use cases	LTBG Pule	23/09/2026	23/09/2026	Completed	100%	SRS Phase 2 System Design Section 4 (Use Case Summary) and attached Use Case Diagram	Yes		Completed		
U2-03	Phase 2	Activity 2.1	Design the sequence diagrams (Flutter↔Supabase and ASP.NET↔Supabase)	RG Madi	24/09/2026	24/09/2026	Completed	100%	SRS Phase 2 System Design Section 8: Sequence Diagram 1 (Flutter ↔ Supabase) and Sequence Diagram 2 (ASP.NET ↔	Yes		Completed		
U2-04	Phase 2	Activity 2.2	Design the database (Entity Relationship Diagram)	LE Letsie	09/09/2026	09/09/2026	Completed	100%	SRS Phase 2 System Design Section 5 (Database Entity Summary) and attached ERD	Yes		Completed		
U2-05	Phase 2	Activity 2.2	Design the Flutter mobile interface	LE Lipali	21/09/2026	22/09/2026	Completed	100%	SRS Phase 2 System Design	Yes		Completed		

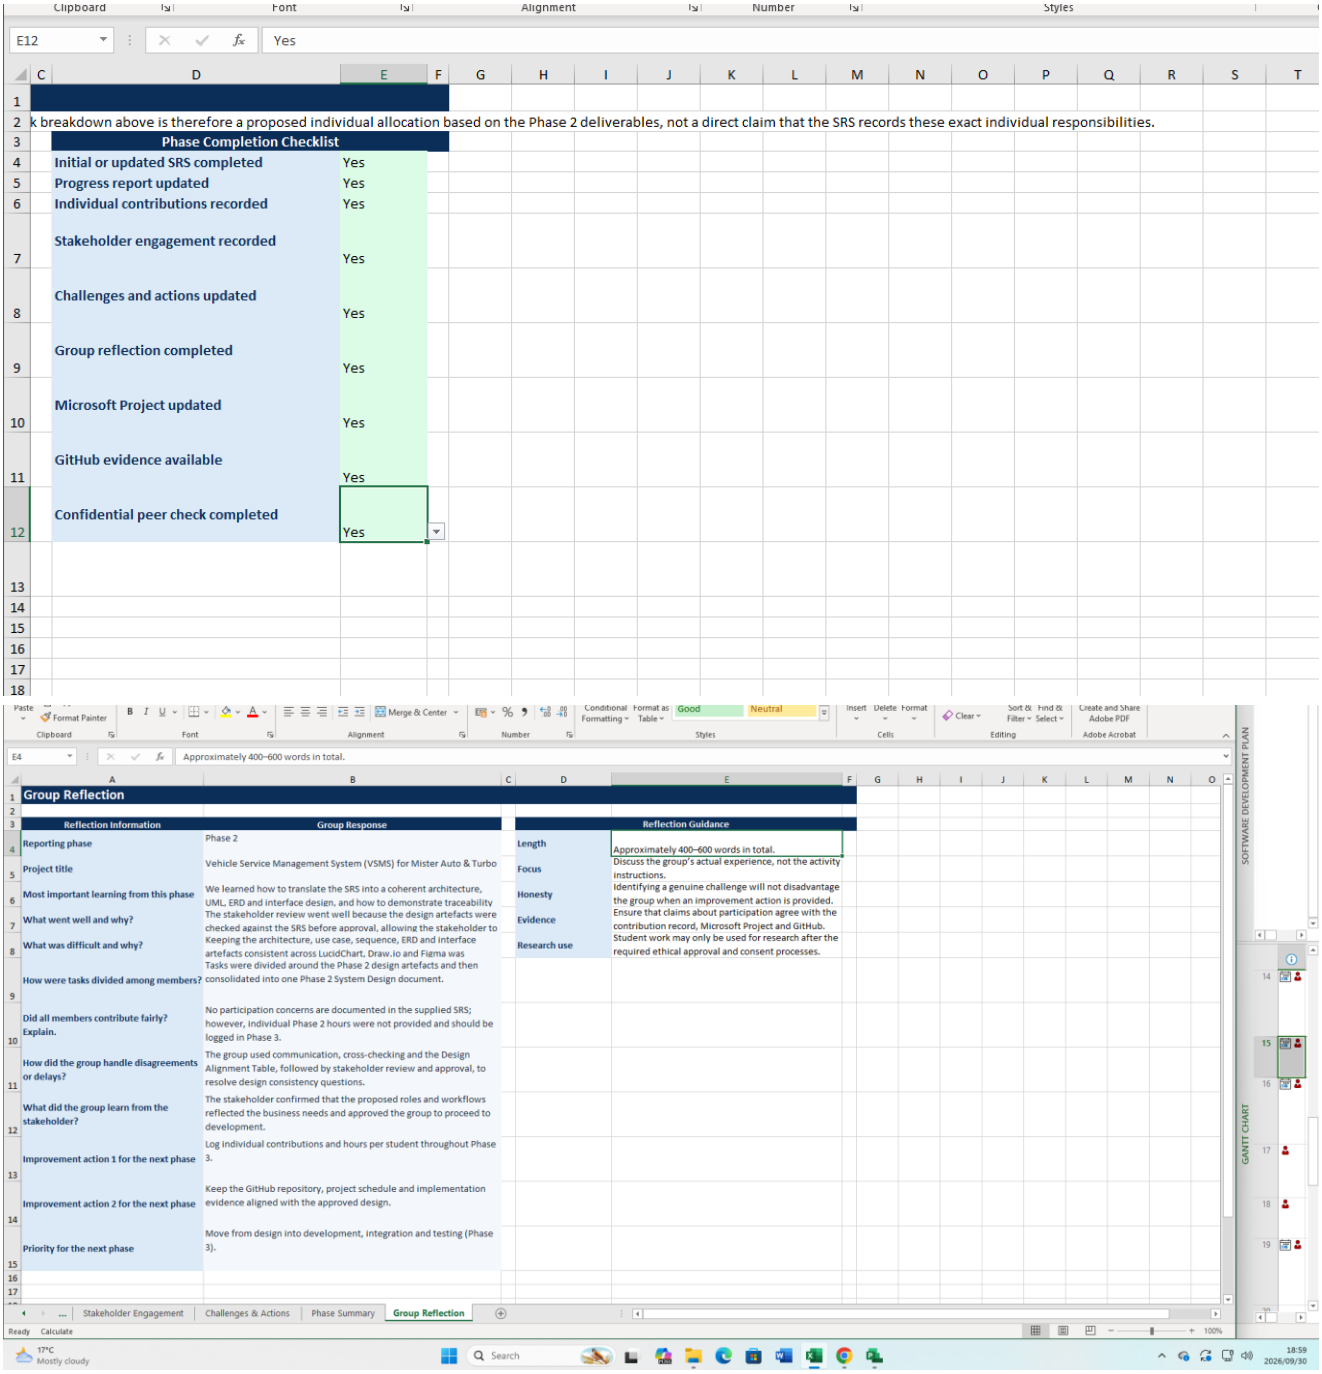
				contribution record						being completed from the SRS.			
U1-11	Unit 1 / Phase 1	Activity 1.3	Complete the Unit 1 group reflection	RG Madi	28/08/2026	28/08/2026	Completed	100%		Yes		Completed	
U2-01	Phase 2	Activity 2.1	Design the system architecture	LE Lipali	22/09/2026	22/09/2026	Completed	100%	SRS Phase 2 System Design Section 2 (System Overview) and Section 8 (Original Design Source Links): System Architecture	Yes		Completed	
U2-02	Phase 2	Activity 2.1	Model the system use cases	LTBG Pule	23/09/2026	23/09/2026	Completed	100%	SRS Phase 2 System Design Section 4 (Use Case Summary) and attached Use Case Diagram	Yes		Completed	
U2-03	Phase 2	Activity 2.1	Design the sequence diagrams (Flutter↔Supabase and ASP.NET↔Supabase)	RG Madi	24/09/2026	24/09/2026	Completed	100%	SRS Phase 2 System Design Section 8: Sequence Diagram 1 (Flutter ↔ Supabase) and Sequence Diagram 2 (ASP.NET ↔	Yes		Completed	
U2-04	Phase 2	Activity 2.2	Design the database (Entity Relationship Diagram)	LE Letsie	09/09/2026	09/09/2026	Completed	100%	SRS Phase 2 System Design Section 5 (Database Entity Summary) and attached ERD	Yes		Completed	
U2-05	Phase 2	Activity 2.2	Design the Flutter mobile interface	LE Lipali	01/09/2026	22/09/2026	Completed	100%	SRS Phase 2 System Design Section 6 (Interface Design Summary) and Section 8: Flutter	Yes		Completed	
U2-06	Phase 2	Activity 2.2	Design the ASP.NET web interface	LE Lipali	01/09/2026	22/09/2026	Completed	100%	SRS Phase 2 System Design Section 6 (Interface Design Summary) and Section 8: ASP.NET	Yes		Completed	
U2-07	Phase 2	Activity 2.3	Compile the Design Alignment Table and Phase 2 System Design document	NM Netshituka	20/09/2026	24/09/2026	Completed	100%	SRS Phase 2 System Design Section 7 (Design Alignment Table), linking requirements, use cases, ERD entities and	Yes		Completed	
U2-08	Phase 2	Activity 2.3	Obtain stakeholder review and sign-off of the Phase 2 design	NM Netshituka	23/09/2026	23/09/2026	Completed	100%	SRS Phase 2 System Design Section 8 / Stakeholder Review & Approval: signed by Motlokoa Teoteo) and group members on	Yes		Completed	
U2-09	Phase 2	Activity 2.3	Update the GitHub repository with Phase 2 design artefacts	RG Madi	23/09/2026	23/09/2026	Completed	100%	SRS page 28: GitHub repository listed with "Phase 2 updates."	Yes		Completed	
U2-10	Phase 2	Activity 2.3	Complete the progress report and contribution record for Phase 2	LE Letsie	25/09/2026	25/09/2026	Completed	100%	Updated progress tracker for Phase 2, based on the completed Phase 2 System Design and	Yes		Completed	

Individual Contribution Record

Student Name	Student Number	Reporting Phase	Activity	Assigned Responsibility	Work Personally Completed	Date Completed	Hours Spent	Evidence / Link	Verified by Group	Verification Date	Notes
LE Letsie	224099468	Unit 1 / Phase 1	System architecture	Coordinate stakeholder engagement	Confirmed stakeholder and agreement	21/08/2026	3	Stakeholder agreement	YES	26/08/2026	
LE Lipali	215135458	Unit 1 / Phase 1	Use case design:	Prepare questions	Created interview questions	21/08/2026	3	Interview notes	YES	26/08/2026	
LTBG Pule	219002738	Unit 1 / Phase 1	ERD/database design:	Collect requirements	Captured stakeholder needs	24/08/2026	3	Stakeholder discussion	YES	26/08/2026	
NM Netshituka	223013773	Unit 1 / Phase 1	Sequence/process design:	Define objectives and scope	Prepared aims and objectives	25/08/2026	3	Project document	YES	26/08/2026	
RG Madi	222066543	Unit 1 / Phase 1	Interface design:	Document current process/problem	Compiled problem statement	26/08/2026	3	WIL document	YES	26/08/2026	
LE Letsie	224099468	Phase 2	System	Design and review the system archite	Reviewed the completed system architectur	22/09/2026		SRS Phase 2 – System Architecture sect	YES	25/09/2026	SRS confirms the member
LE Lipali	215135458	Phase 2	Use case design:	Design and review use cases	Reviewed the use case diagram and descric	23/09/2026		SRS Phase 2 – Use Case section	YES	25/09/2026	SRS confirms the member
LTBG Pule	219002738	Phase 2	ERD/database	Design and review the database/ERD	Reviewed the ERD for correct entities, relati	09/09/2026		SRS Phase 2 – ERD/Database section	YES	25/09/2026	SRS confirms the member
NM Netshituka	223013773	Phase 2	Sequence/proce	Design and review sequence/process	Reviewed the sequence diagrams to confirn	24/09/2026		SRS Phase 2 – Sequence/Process sectio	YES	25/09/2026	SRS confirms the member
RG Madi	222066543	Phase 2	Interface	Design and review the interface	Reviewed the interface designs/wireframes	24/09/2026		SRS Phase 2 – Interface Design section	YES	25/09/2026	SRS confirms the member

Challenges and Corrective Actions

Date Identified	Reporting Phase	Challenge	Effect on Progress	Corrective Action	Responsible Student	Target Date	Status
25/08/2026	Unit 1 / Phase 1	Group members' current skill level in Flutter, ASP.NET and Supabase (documented constraint).	Risk of slower development once the project moves into design and build phases.	Self-study and small practice builds in each technology alongside requirements work.	LE Letsie	26/08/2026	Resolved
25/08/2026	Unit 1 / Phase 1	Stakeholder's business is entirely paper-based with no existing digital or online records.	Made it harder to gather structured requirements and cost/pricing data quickly.	Relied on direct interviews, observation of the manual process and written confirmation (WhatsApp/meeting notes) per the Cooperation Agreement.	LE Lipali	26/08/2026	Resolved
25/08/2026	Unit 1 / Phase 1	Limited time with stakeholder	Delayed requirements clarification	Schedule follow-up session and consolidate questions	LTBG Pule	26/08/2026	Resolved
20/09/2026	Phase 2	Keeping the architecture, use case, sequence, ERD and interface artefacts (built across LucidChart, Draw.io and Figma) consistent with one another.	Risk of the design documents contradicting each other and failing the rubric's consistency requirement.	Built a Design Alignment Table cross-referencing each requirement to its use case, ERD entity and interface, and reviewed it with the stakeholder before sign-off.	Group	24/09/2026	Resolved



k breakdown above is therefore a proposed individual allocation based on the Phase 2 deliverables, not a direct claim that the SRS records these exact individual responsibilities.

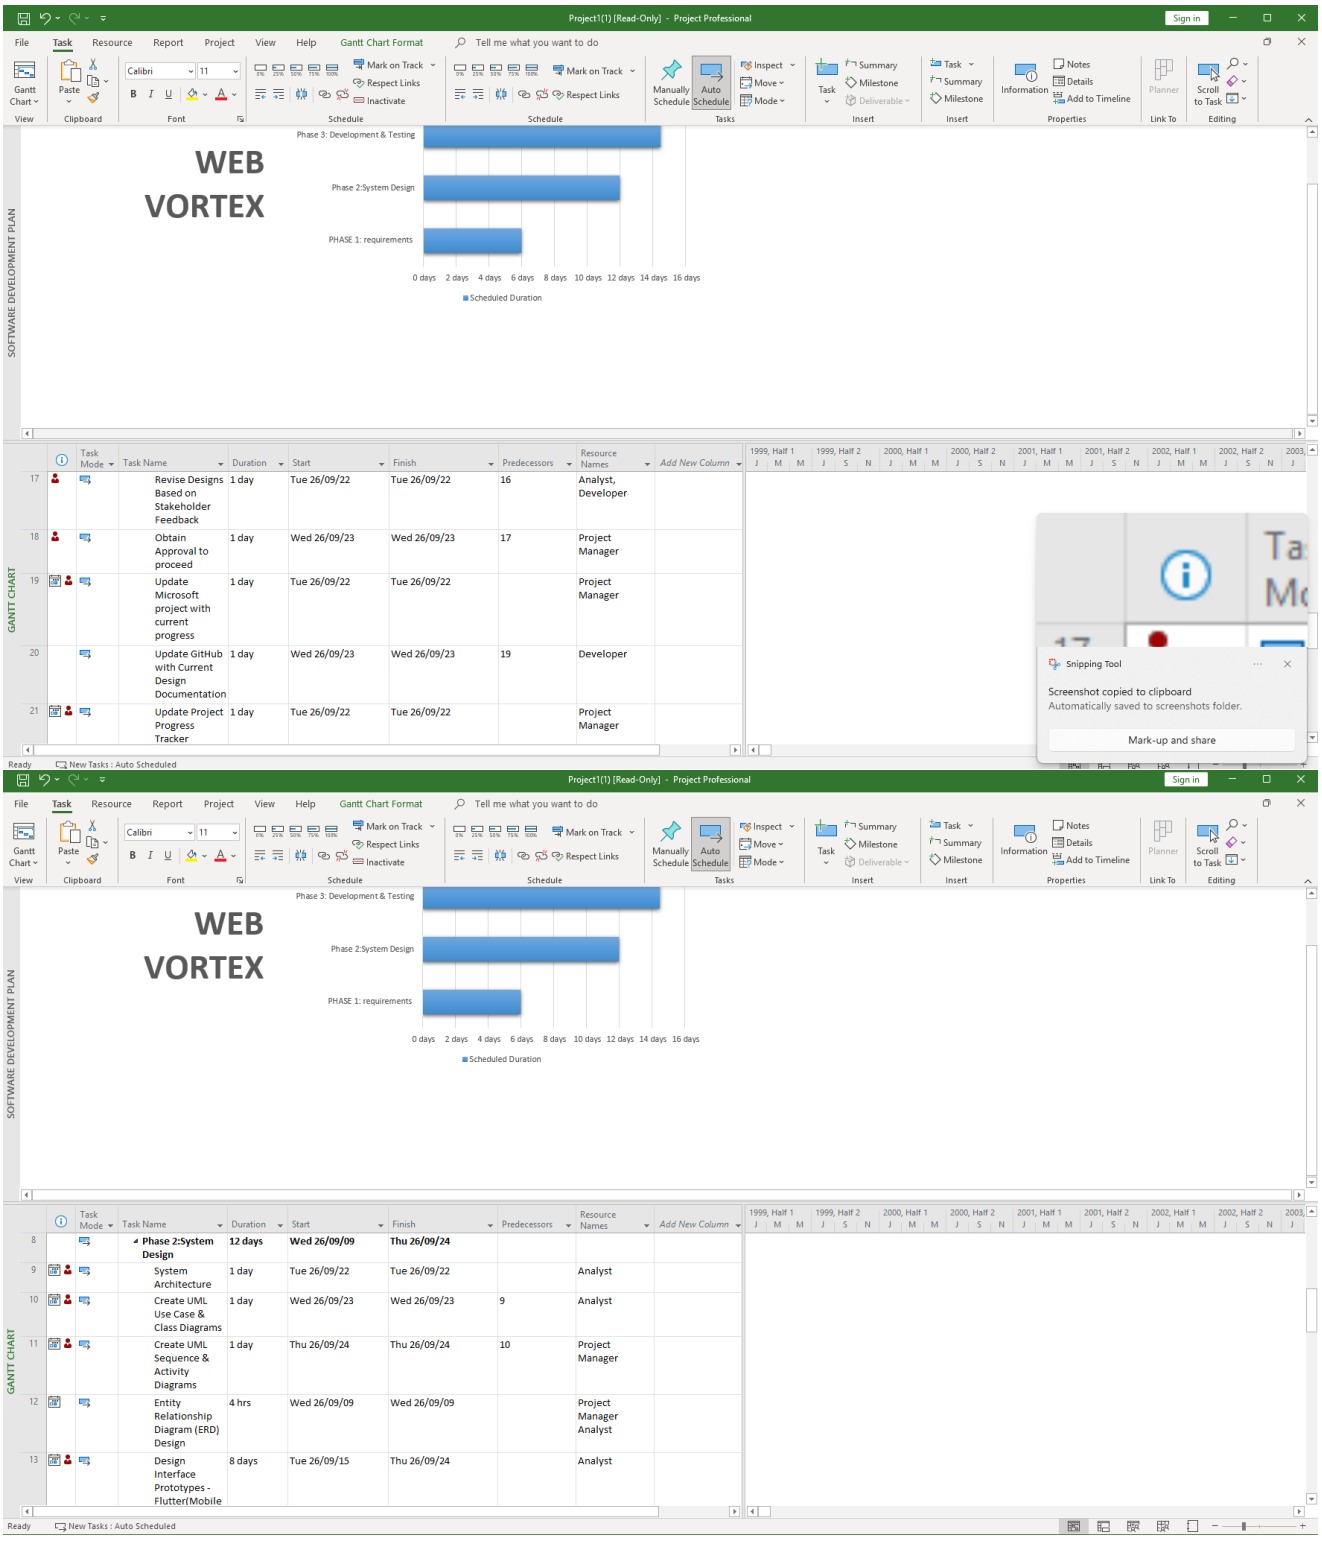
Phase Completion Checklist	
Initial or updated SRS completed	Yes
Progress report updated	Yes
Individual contributions recorded	Yes
Stakeholder engagement recorded	Yes
Challenges and actions updated	Yes
Group reflection completed	Yes
Microsoft Project updated	Yes
GitHub evidence available	Yes
Confidential peer check completed	Yes

Group Reflection

Reflection Information	Group Response
Reporting phase	Phase 2
Project title	Vehicle Service Management System (VSMS) for Mister Auto & Turbo
Most important learning from this phase	We learned how to translate the SRS into a coherent architecture, UML, ERD and interface design, and how to demonstrate traceability
What went well and why?	The stakeholder review went well because the design artefacts were checked against the SRS before approval, allowing the stakeholder to
What was difficult and why?	Keeping the architecture, use case, sequence, ERD and interface artefacts consistent across LucidChart, Draw.io and Figma was
How were tasks divided among members?	Tasks were divided around the Phase 2 design artefacts and then consolidated into one Phase 2 System Design document.
Did all members contribute fairly? Explain.	No participation concerns are documented in the supplied SRS; however, individual Phase 2 hours were not provided and should be logged in Phase 3.
How did the group handle disagreements or delays?	The group used communication, cross-checking and the Design Alignment Table, followed by stakeholder review and approval, to resolve design consistency questions.
What did the group learn from the stakeholder?	The stakeholder confirmed that the proposed roles and workflows reflected the business needs and approved the group to proceed to development.
Improvement action 1 for the next phase	Log individual contributions and hours per student throughout Phase 3.
Improvement action 2 for the next phase	Keep the GitHub repository, project schedule and implementation evidence aligned with the approved design.
Priority for the next phase	Move from design into development, integration and testing (Phase 3).

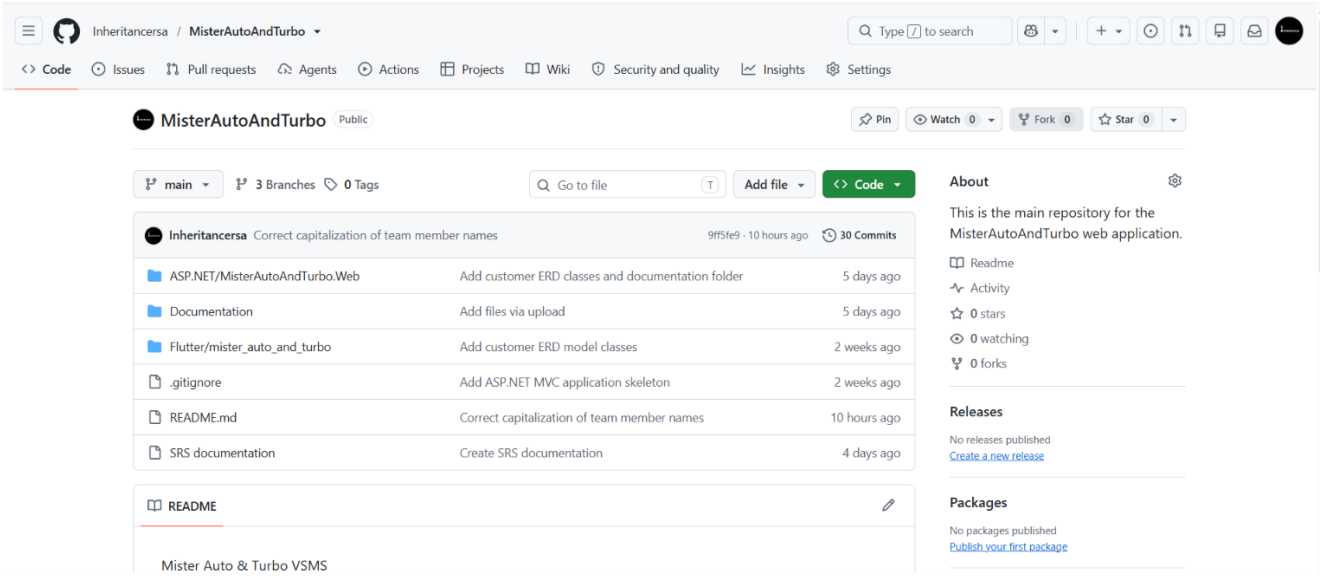
Reflection Guidance	
Length	Approximately 400–600 words in total.
Focus	Discuss the group's actual experience, not the activity instructions.
Honesty	Identifying a genuine challenge will not disadvantage the group when an improvement action is provided.
Evidence	Ensure that claims about participation agree with the contribution record, Microsoft Project and GitHub.
Research use	Student work may only be used for research after the required ethical approval and consent processes.

Microsoft Project



GitHub

https://github.com/Inheritancersa/MisterAutoAndTurbo



Manage access

Add people

Select all

Type

Find a collaborator...

Lehlokoa99
Collaborator

letsielekete45-m
Collaborator

NdivhuwoNetshituka-blip
Collaborator

Rotondwa
Rotondwa-glitch • Collaborator

PHASE 3: SYSTEM DEVELOPMENT, IMPLEMENTATION AND FINAL DEMONSTRATION

Mr Auto & Turbo Workshop Management System

Prepared by: Web Vortex | Module: ITC327W – Work-Integrated Learning | Date: 22 October 2026

1. Purpose of Phase 3

Phase 3 records the development and integration readiness of the Mr Auto & Turbo Workshop Management System. The group must review and organise the work completed, correct the existing project records where necessary, and prepare a working prototype for the final assessment. This section extends the existing Phase 1 requirements and Phase 2 architecture and design; it does not replace the approved stakeholder requirements or claim that a function is complete without verification.

What the Group Must Have Ready

The table below summarises the Phase 3 items the group must have ready for the final assessment. Status is recorded only after the group has checked the item; detailed checkpoints follow in Sections 3 to 12.

Item	What should be complete	Status
Shared Supabase Backend	Required database tables, fields, keys and relationships	Verified
Authentication and User Access	Sign-in and access permissions, where required	Verified
Flutter Mobile Application	Main approved mobile screens and functions	Verified
ASP.NET Web Application	Main approved web pages and functions	Verified
Application Integration	Both applications connected to the same Supabase project	Verified
Shared Processes	At least two important processes working across the applications	Verified
Updated SRS	Approved implementation changes recorded where necessary	Verified
Microsoft Project	Updated to reflect development progress	Verified
GitHub	Current mobile and web source code	Verified
Project Progress Tracker	Current tasks, contributions, challenges and group reflection	Verified
Final Demonstration	Working prototype ready to present to the assessment panel	Verified

2. Implementation Baseline and Architecture

The approved solution consists of a Flutter mobile application, an ASP.NET web application and a shared Supabase backend. The Flutter application supports customer-facing functions and the approved mobile functions for staff where implemented. The ASP.NET application provides role-based workshop administration and staff workflows. Supabase is the shared data backend for both applications. The implementation must use the same Supabase project and consistent database fields, relationships and values.

The Phase 2 design identifies the following user roles: Administrator/Manager, Receptionist, Mechanic and Customer. Access must follow the approved role permissions. In particular, payment processing is restricted to management, while reception functions cover customer and vehicle registration, appointments and collection; mechanics manage assigned jobs, inspections and repair-status updates.

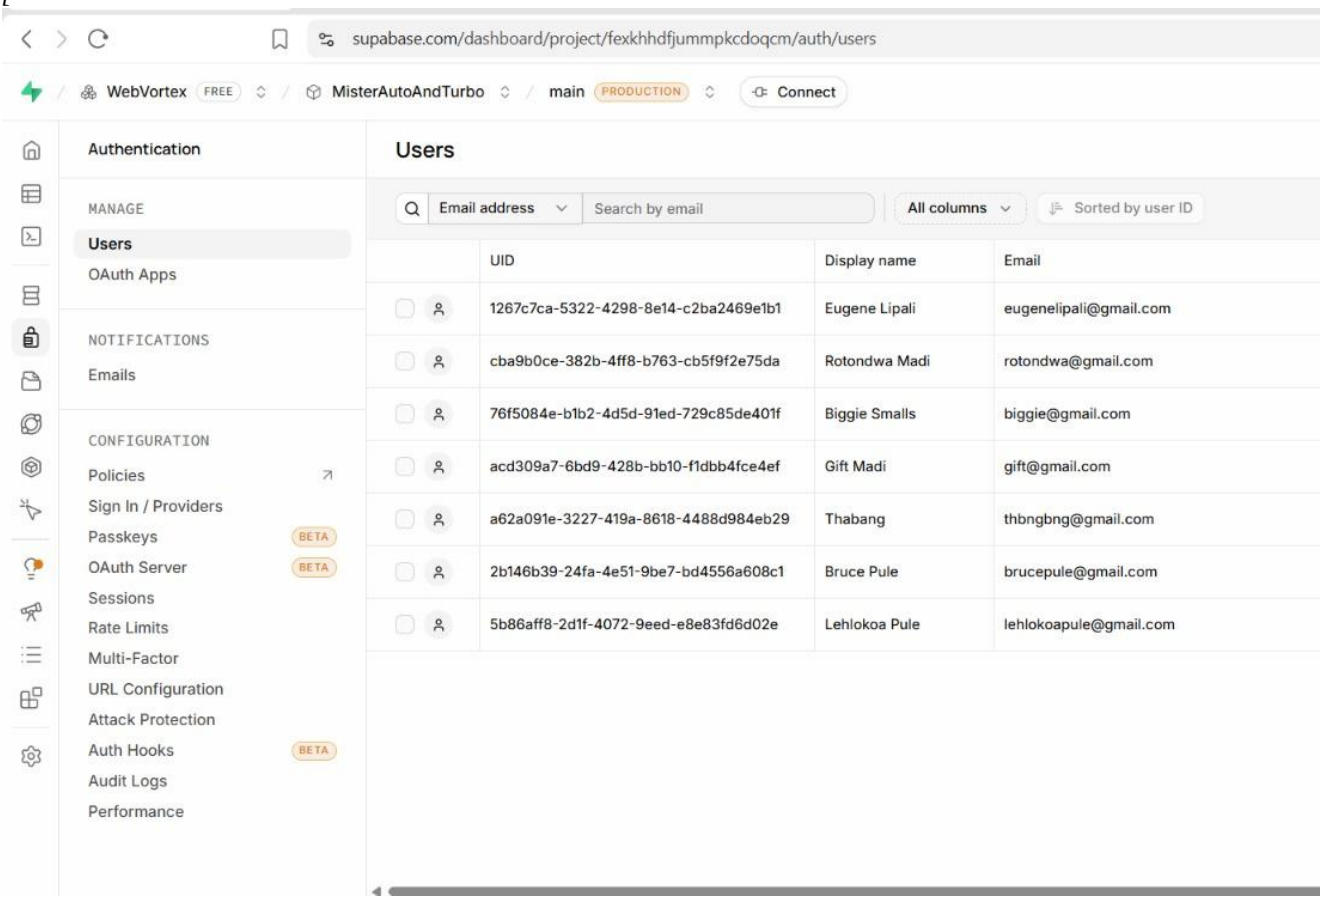
3. Shared Supabase Backend Readiness

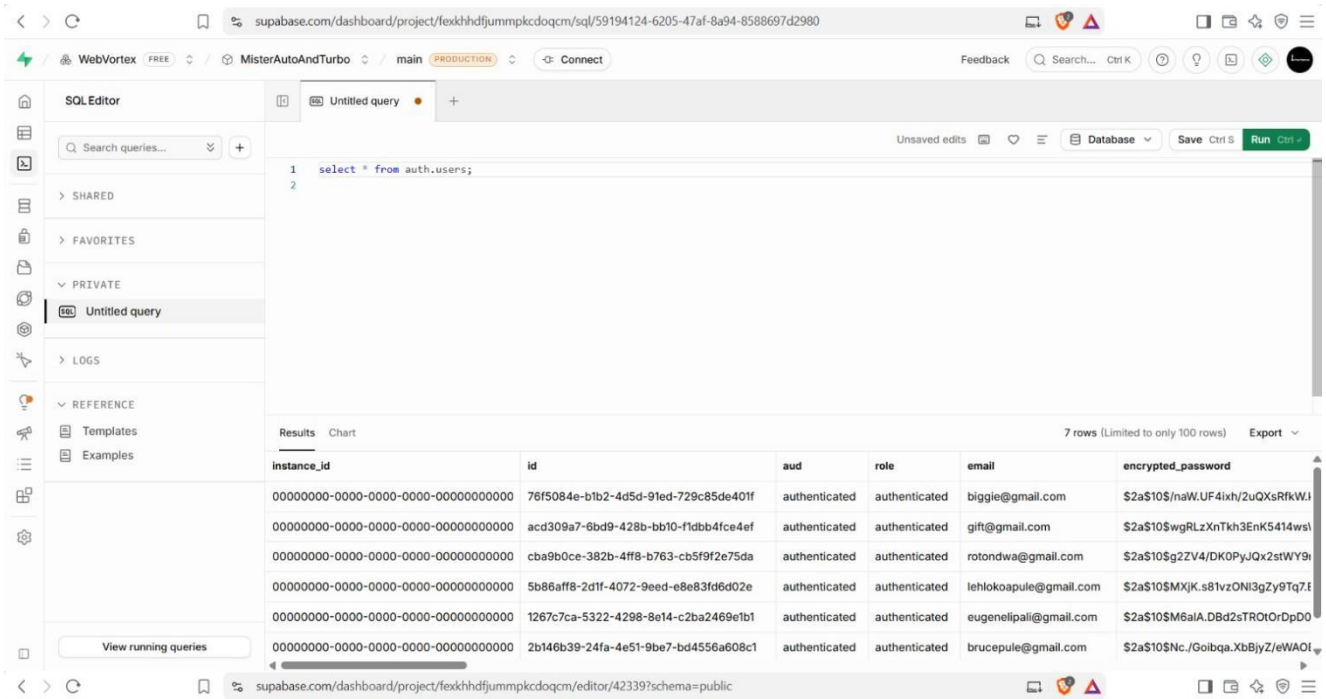
The group must inspect the live Supabase project and record the actual implementation status below.

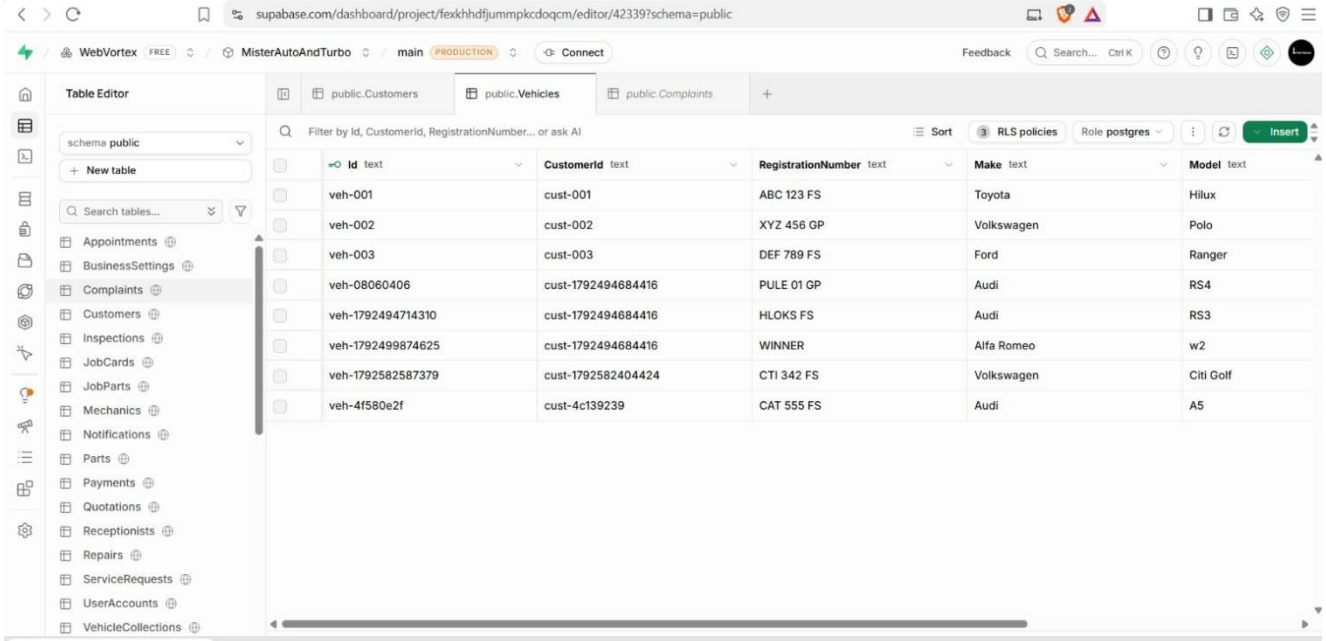
Checkpoint	Evidence to inspect	Status / notes
Required tables and fields	Confirm tables and fields match the approved ERD and application forms.	Verified
Primary and foreign keys	Confirm key constraints are configured correctly.	Verified
ERD relationships	Check Customer–Vehicle, Vehicle–Job, Job–Payment and other approved relationships.	Verified
Authentication	Confirm the configured sign-in flow works for required users; Phase 2 design specifies phone number and OTP.	Verified
Role permissions	Verify users can access only authorised records and functions.	Verified
Data operations	Demonstrate saving, retrieving and updating required records.	Verified
Shared project	Confirm Flutter and ASP.NET use the same Supabase project and compatible field names/values.	Verified

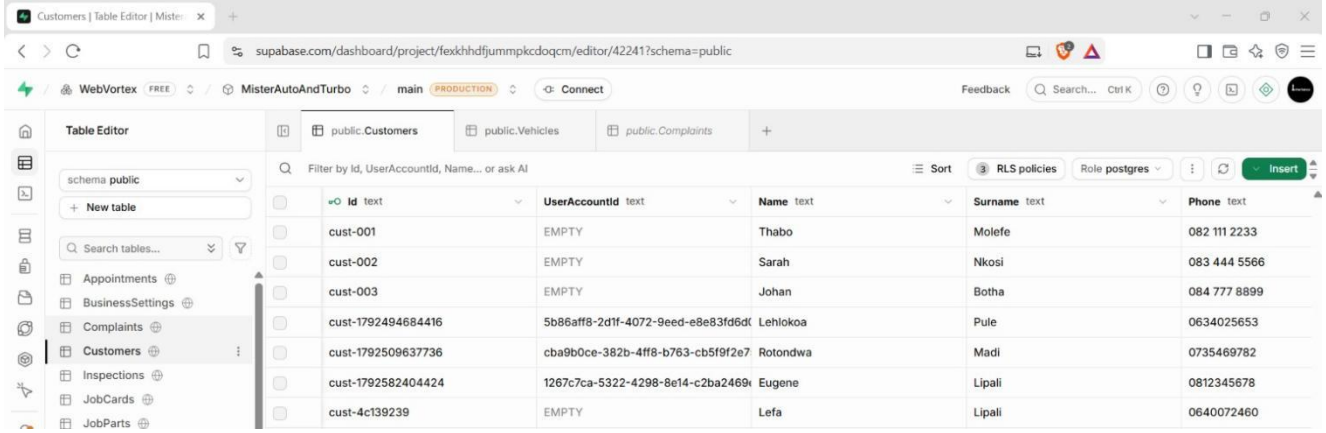
Evidence - Shared Supabase Backend

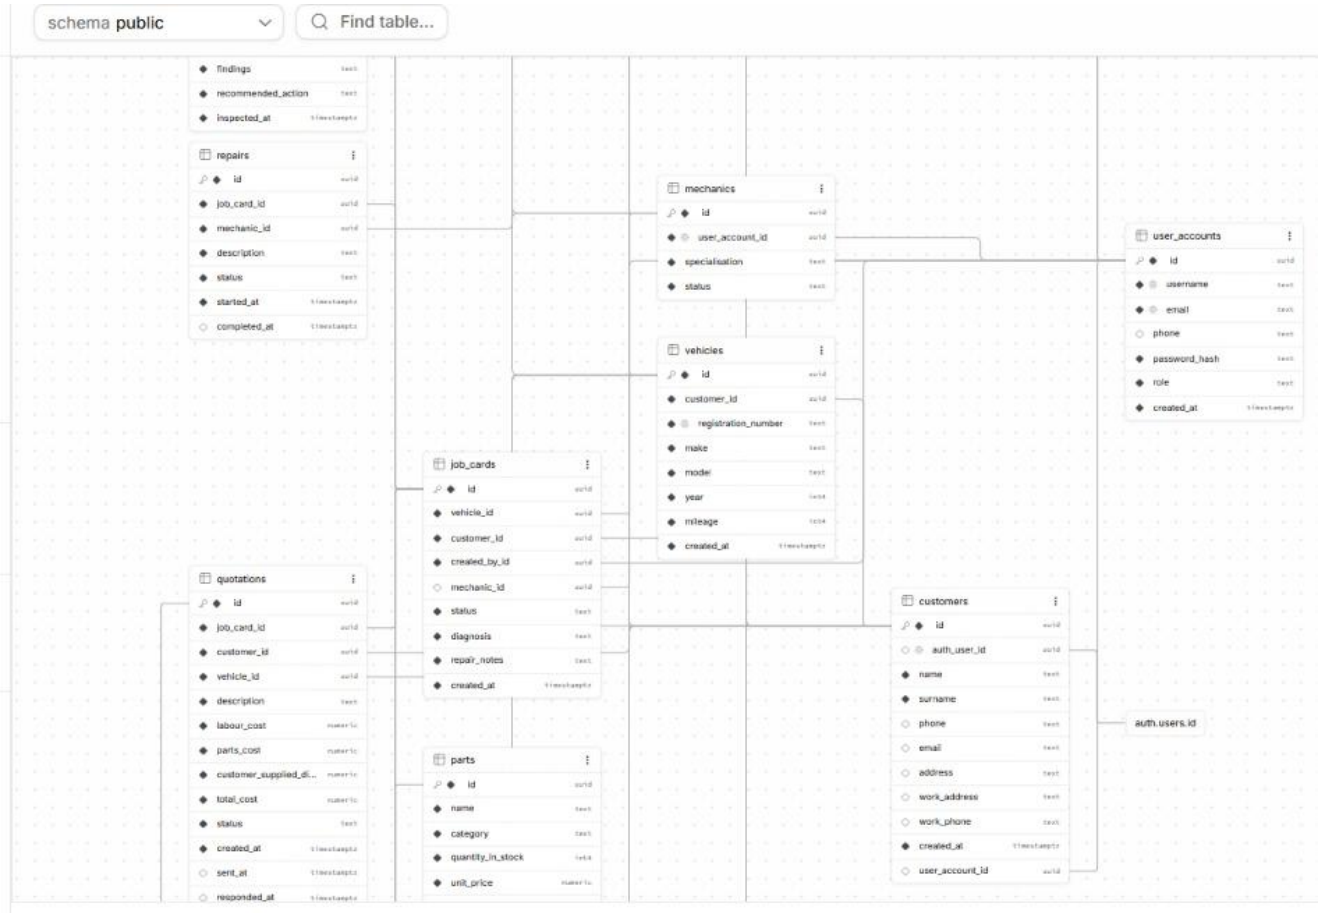
[




supabase.com/dashboard/project/fexkhhdfjummpkcdoqcm/sql/59194124-6205-47af-8a94-8588697d2980
WebVortex FREE
MisterAutoAndTurbo
main PRODUCTION
Connect
Feedback
Search... Ctrl K
SQL Editor
Untitled query
Search queries...
SHARED
FAVORITES
PRIVATE
Untitled query
LOGS
REFERENCE
Templates
Examples
View running queries
Unsaved edits
Database
Save Ctrl S
Run Ctrl ⏎
1 select * from auth.users;
2
Results
Chart
7 rows (Limited to only 100 rows)
Export
instance_id
id
aud
role
email
encrypted_password
00000000-0000-0000-0000-00000000000 76f5084e-b1b2-4d5d-91ed-729c85de401f authenticated authenticated biggie@gmail.com $2a$10$/naW.UF4ixh/2uQXsRfkW.
00000000-0000-0000-0000-00000000000 acd309a7-6bd9-428b-bb10-f1dbb4fce4ef authenticated authenticated gift@gmail.com $2a$10$wgRLzXnTkh3EnK5414ws\
00000000-0000-0000-0000-00000000000 cba9b0ce-382b-4ff8-b763-cb5f9f2e75da authenticated authenticated rotondwa@gmail.com $2a$10$g2ZV4/DK0PyJQx2stWY9
00000000-0000-0000-0000-00000000000 5b86aff8-2d1f-4072-9eed-e8e83fd6d02e authenticated authenticated lehlokoapule@gmail.com $2a$10$MXjK.s81vzONl3gZy9Tq7.
00000000-0000-0000-0000-00000000000 1267c7ca-5322-4298-8e14-c2ba2469e1b1 authenticated authenticated eugenelipali@gmail.com $2a$10$M6alA.DBd2sTROtOrDpD0
00000000-0000-0000-0000-00000000000 2b146b39-24fa-4e51-9be7-bd4556a608c1 authenticated authenticated brucepule@gmail.com $2a$10$Nc./Goibqa.XbBjyZ/eWAOI


supabase.com/dashboard/project/fexkhhdfjummpkcdoqcm/editor/42339?schema=public
WebVortex FREE
MisterAutoAndTurbo
main PRODUCTION
Connect
Feedback
Search... Ctrl K
Table Editor
public.Customers
public.Vehicles
public.Complaints
schema public
New table
Search tables...
Appointments
BusinessSettings
Complaints
Customers
Inspections
JobCards
JobParts
Mechanics
Notifications
Parts
Payments
Quotations
Receptionists
Repairs
ServiceRequests
UserAccounts
VehicleCollections
Filter by Id, CustomerId, RegistrationNumber... or ask AI
Sort
RLS policies
Role postgres
Insert
Id text
CustomerId text
RegistrationNumber text
Make text
Model text
veh-001 cust-001 ABC 123 FS Toyota Hilux
veh-002 cust-002 XYZ 456 GP Volkswagen Polo
veh-003 cust-003 DEF 789 FS Ford Ranger
veh-08060406 cust-1792494684416 PULE 01 GP Audi RS4
veh-1792494714310 cust-1792494684416 HLOKS FS Audi RS3
veh-1792499874625 cust-1792494684416 WINNER Alfa Romeo w2
veh-1792582587379 cust-1792582404424 CTI 342 FS Volkswagen Citi Golf
veh-4f580e2f cust-4c139239 CAT 555 FS Audi A5


Customers | Table Editor | Miste
supabase.com/dashboard/project/fexkhhdfjummpkcdoqcm/editor/42241?schema=public
WebVortex FREE
MisterAutoAndTurbo
main PRODUCTION
Connect
Feedback
Search... Ctrl K
Table Editor
public.Customers
public.Vehicles
public.Complaints
schema public
New table
Search tables...
Appointments
BusinessSettings
Complaints
Customers
Inspections
JobCards
JobParts
Filter by Id, UserAccountId, Name... or ask AI
Sort
RLS policies
Role postgres
Insert
Id text
UserAccountId text
Name text
Surname text
Phone text
cust-001 EMPTY Thabo Molefe 082 111 2233
cust-002 EMPTY Sarah Nkosi 083 444 5566
cust-003 EMPTY Johan Botha 084 777 8899
cust-1792494684416 5b86aff8-2d1f-4072-9eed-e8e83fd6d Lehlokoa Pule 0634025653
cust-1792509637736 cba9b0ce-382b-4ff8-b763-cb5f9f2e7 Rotondwa Madi 0735469782
cust-1792582404424 1267c7ca-5322-4298-8e14-c2ba2469 Eugene Lipali 0812345678
cust-4c139239 EMPTY Lefa Lipali 0640072460



4. Flutter Mobile Application Readiness

Review the implemented mobile application against the approved design and requirements. Mark each item only after demonstrating it.

Checkpoint	Expected evidence	Status / notes
Application launches	Application starts without a blocking error.	Verified
Approved screens	Login/OTP, vehicle status and timeline, notifications, payment/invoice view and mechanic job screens where implemented.	Verified
Navigation	Navigation between available screens works.	Verified
Forms and inputs	Required information can be entered and validation behaves appropriately.	Verified
Main mobile functions	Approved customer and/or staff functions work as designed.	Verified
Supabase connection	Application saves and retrieves records from the shared backend.	Verified
SRS alignment	Implemented functions match approved requirements; gaps are recorded below.	Verified

Evidence - Flutter Mobile Application

Proof Of Pay

Proof Of Payment Uploaded

The workshop will confirm your payment shortly.

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Hello, Teboho

Book A Service.

Choose your vehicle

Cadillac VISTIQ - ESV FS

Type of service

Diagnostic

Oil & Filter Exchange

Repair

Maintenance

Next

My Bookings

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Hello, Teboho

Active Bookings.

Maintenance

Cadillac VISTIQ · ESV FS

29 Oct 2026 at 11:00

Notes: I just need a proper service check.

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Hello, Teboho

Complaints.

Complaint Type

Select complaint type

Vehicle (optional)

None

Job (optional)

None

Complaint Description

Submit Complaint



Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Hello, Teboho

Booking Confirmed.

Maintenance

Cadillac VISTIQ

29 Oct 2026 at 11:00

Done

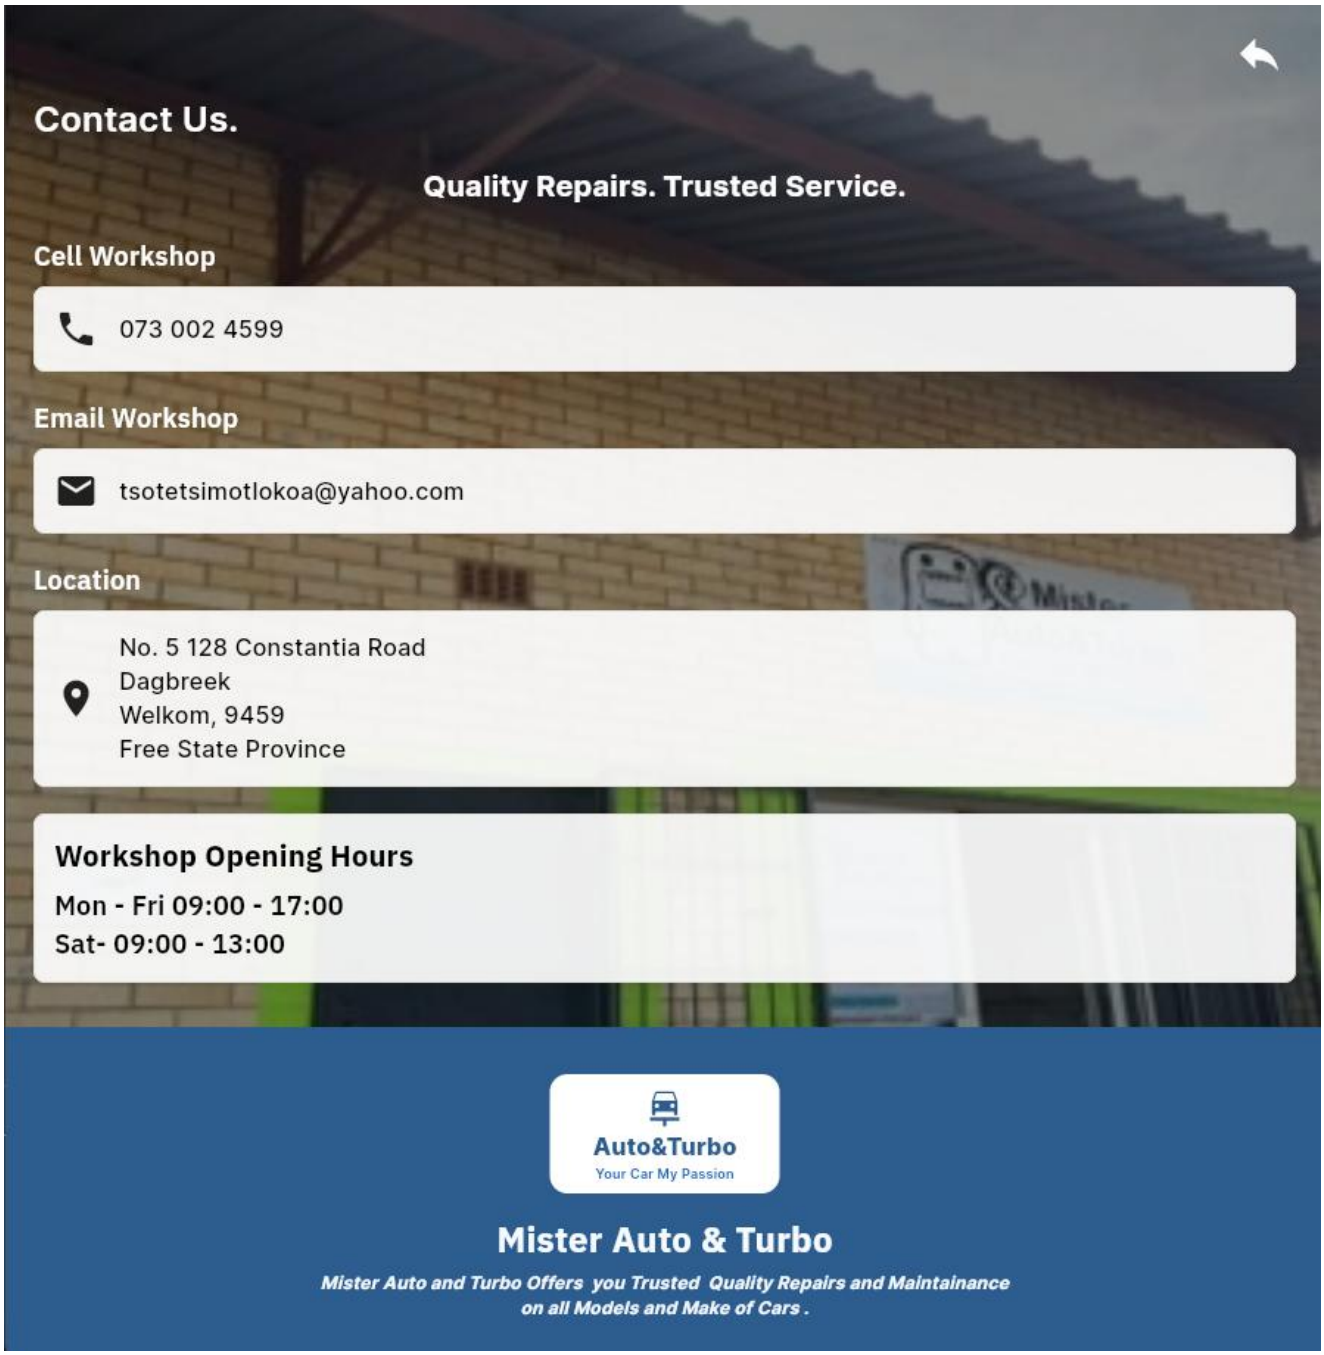
My Bookings

Auto&Turbo

Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .



Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Hello, Teboho

Edit Profile.

Full Name

Teboho Pule

Email

TebohoPule@gmail.com

Phone Number

0644025653

Address

726 Maphutsi Street

New Password (leave blank to keep)

Confirm New Password

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Hello, Teboho

Refresh | Contact Us | Log Out | Edit Profile

Your Vehicles.

No vehicles registered yet.
Register your vehicle to get started.

+ Register A Vehicle

Quick Actions...

Book A Service

Quotations

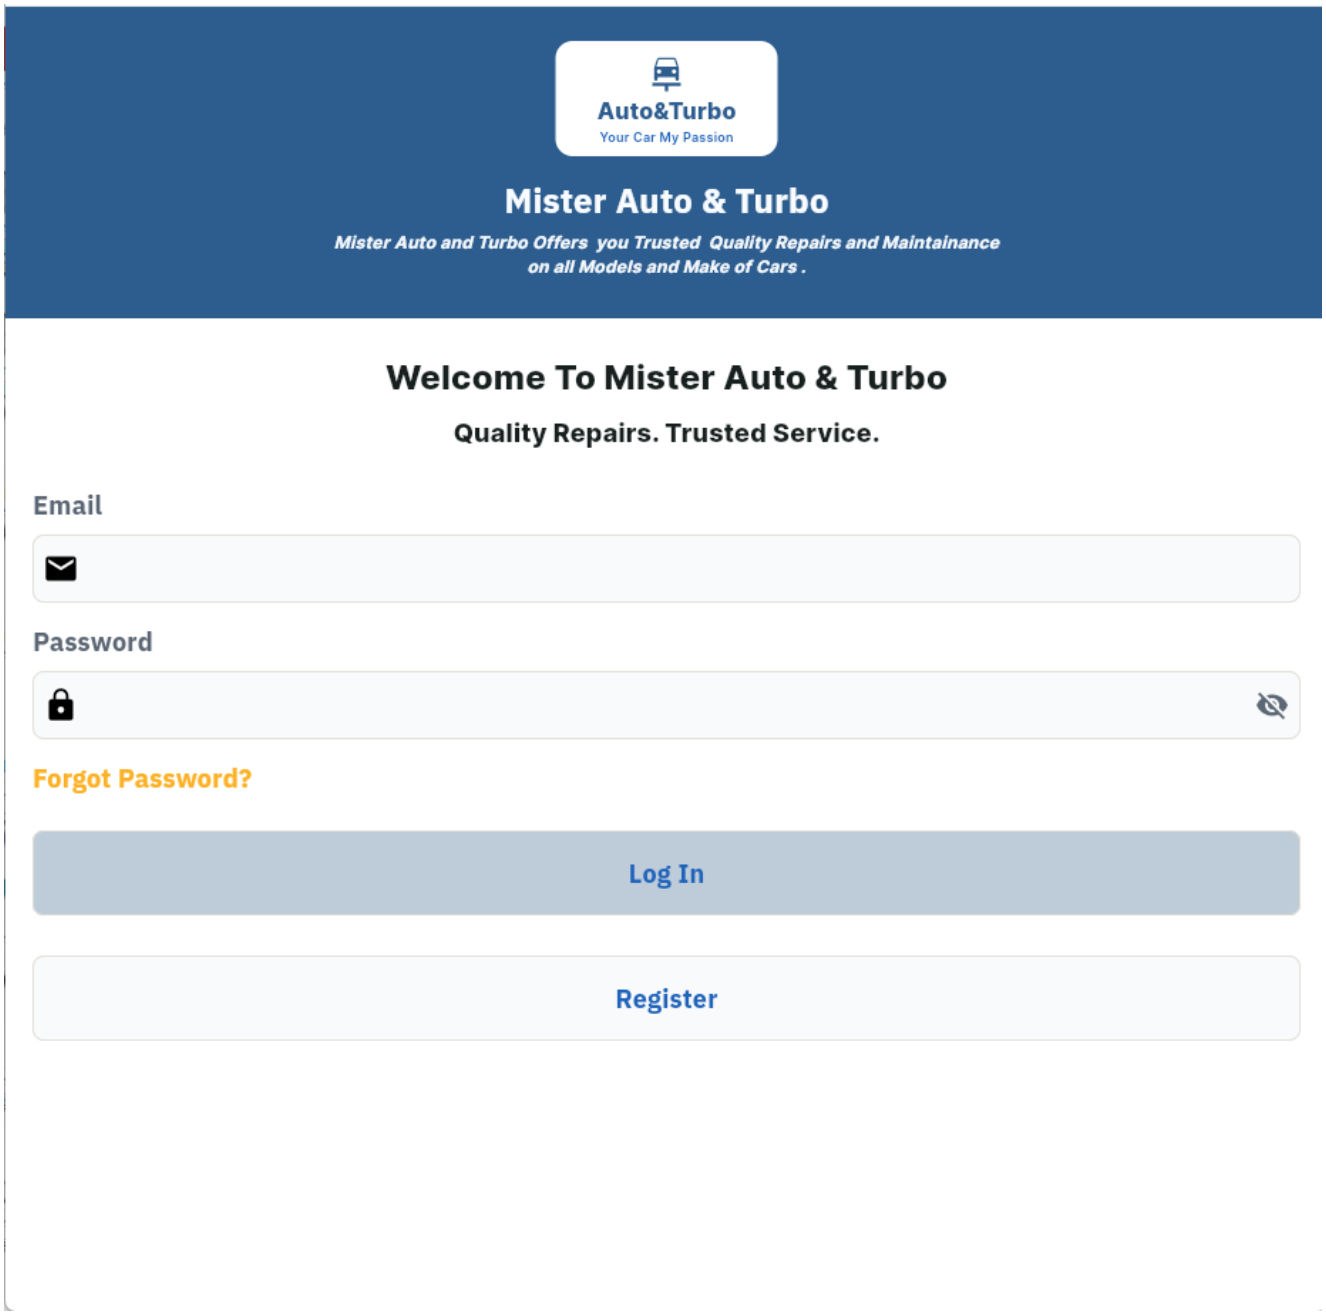
Repair History

Notifications

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .


Auto&Turbo
Your Car My Passion
Mister Auto & Turbo
Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .
Welcome To Mister Auto & Turbo
Quality Repairs. Trusted Service.
Email
Password
Forgot Password?
Log In
Register



Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Welcome To Mister Auto & Turbo

Quality Repairs. Trusted Service.

Email

TebohoPule@gmail.com

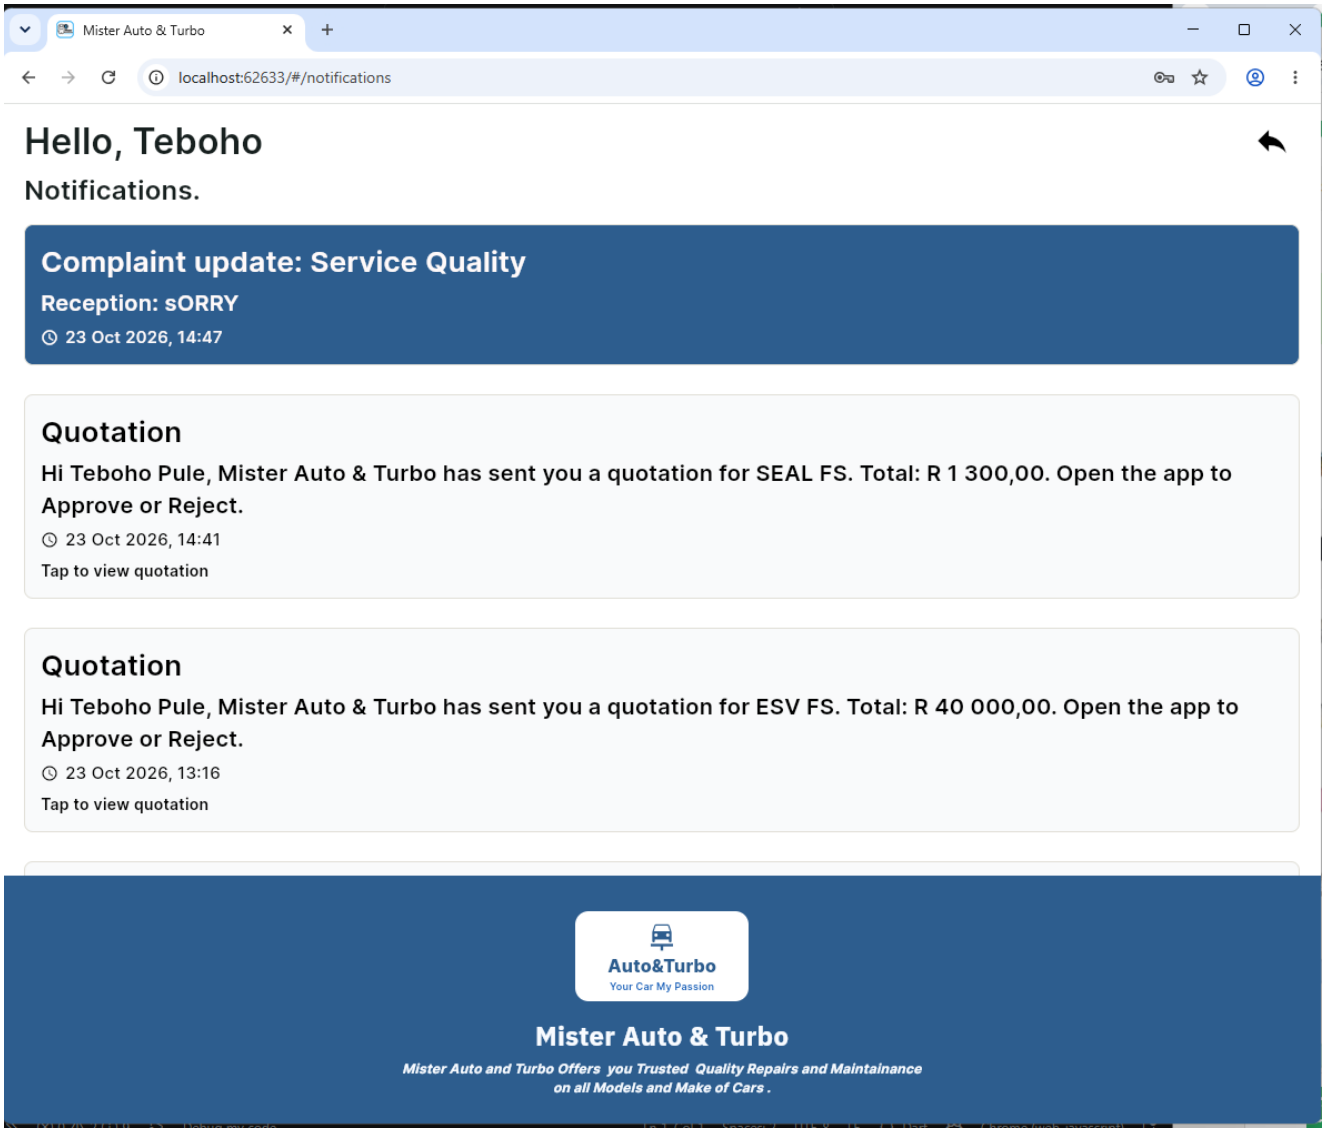
Password

Forgot Password?

Log In

Register

Account created. Please log in.


Mister Auto & Turbo
localhost:62633/#/notifications
Hello, Teboho
Notifications.
Complaint update: Service Quality
Reception: sORRY
23 Oct 2026, 14:47
Quotation
Hi Teboho Pule, Mister Auto & Turbo has sent you a quotation for SEAL FS. Total: R 1 300,00. Open the app to Approve or Reject.
23 Oct 2026, 14:41
Tap to view quotation
Quotation
Hi Teboho Pule, Mister Auto & Turbo has sent you a quotation for ESV FS. Total: R 40 000,00. Open the app to Approve or Reject.
23 Oct 2026, 13:16
Tap to view quotation
Auto&Turbo
Your Car My Passion
Mister Auto & Turbo
Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Hello, Teboho

Notifications.

Complaint Submitted

Your complaint was sent to the workshop.

23 Oct 2026, 13:04

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Hello, Teboho

Book A Service.

Choose your vehicle

Cadillac VISTIQ - ESV FS

Type of service

Diagnostic

Oil & Filter Exchange

Repair

Maintenance

Next

My Bookings

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Proof Of Pay

Vehicle
Aston Martin N6
Registration Number
NOW FS
Quotation Job Card
job-009
Customer
Lehlokoa Pule
Total Amount
R16500

Upload Payment Document

Upload your proof of payment below.

PDF, JPG or PNG • Maximum combined size: 10 MB

Tap To Upload

Choose one or multiple files

Upload Document

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Cadillac VISTIQ

Registration
ESV FS

Job Card
job-012

Total Amount
R40000

Item	Amount
Labour	R5000.
Parts	R35000.
Total	**R40000.**

Quotation Accepted

Thank you. The workshop will now start the repair.

Proof Of Payment

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Quotation

Vehicle
Cadillac VISTIQ

Registration
ESV FS

Job Card
job-012

Total Amount
R40000

Item	Amount
Labour	R5000.
Parts	R35000.
Total	**R40000.**

Accept Quotation

Reject Quotation

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Hello, Teboho

Register Your Vehicle.

MAKE

Cadillac

MODEL

VISTIQ

Registration Plate

ESV FS

Year

2024

Mileage (km)

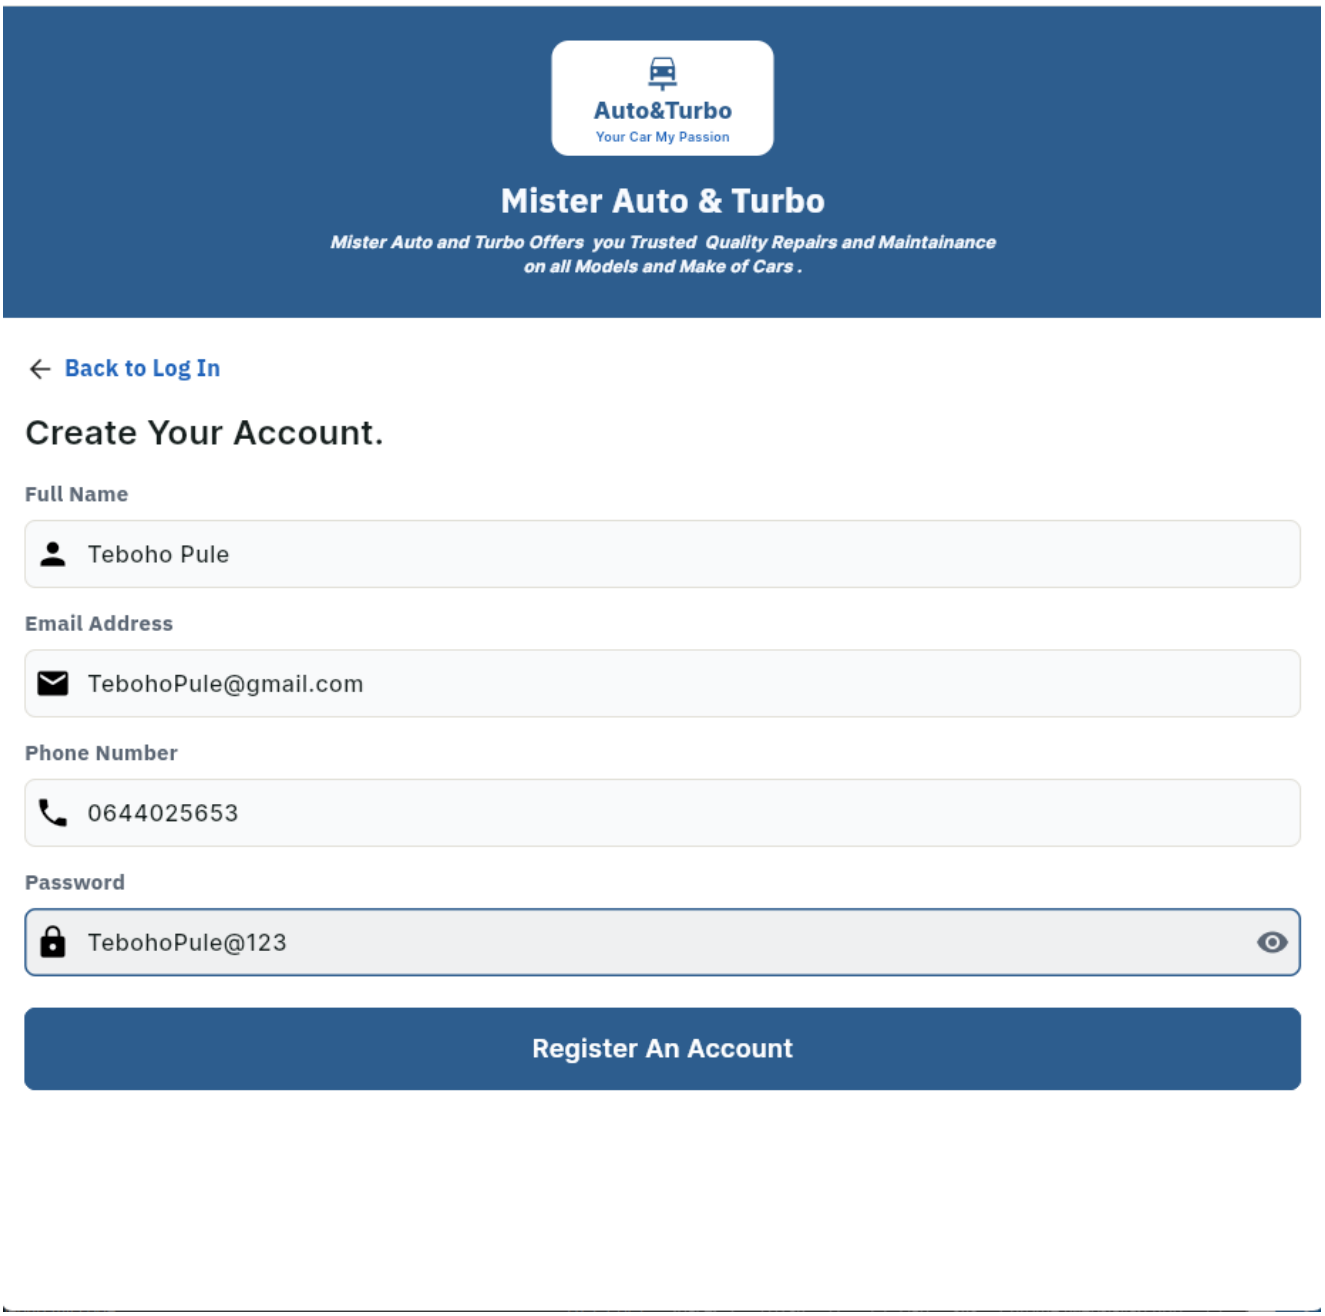
1000

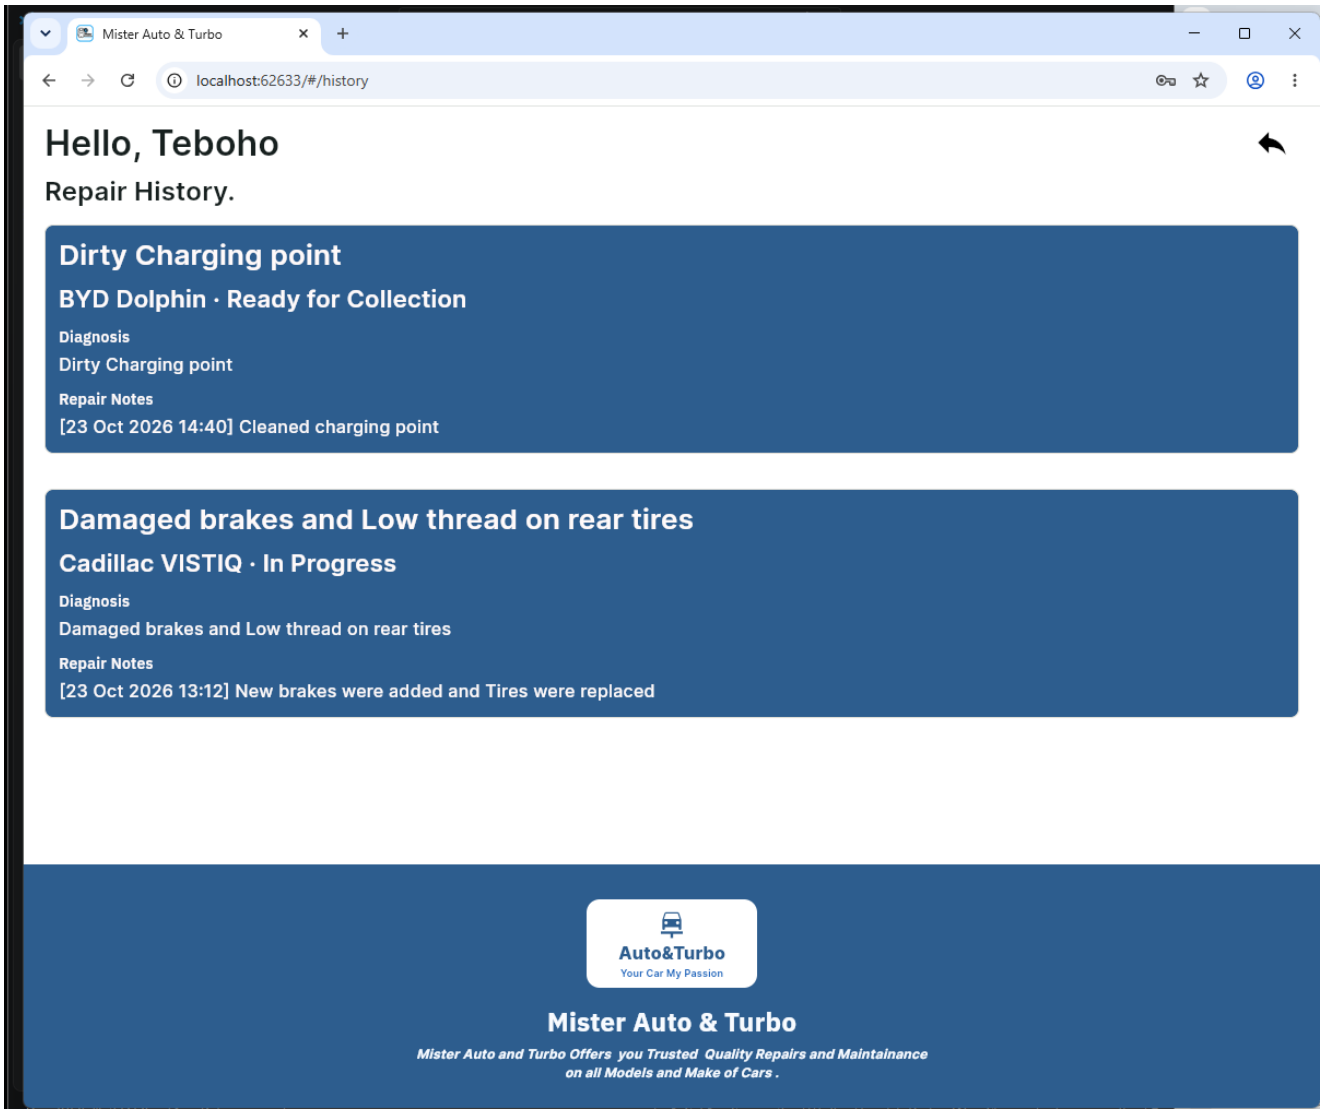
Save Vehicle Details

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .


Auto&Turbo
Your Car My Passion
Mister Auto & Turbo
Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .
Back to Log In
Create Your Account.
Full Name
Teboho Pule
Email Address
TebohoPule@gmail.com
Phone Number
0644025653
Password
TebohoPule@123
Register An Account


Mister Auto & Turbo
localhost:62633/#/history
Hello, Teboho
Repair History.
Dirty Charging point
BYD Dolphin · Ready for Collection
Diagnosis
Dirty Charging point
Repair Notes
[23 Oct 2026 14:40] Cleaned charging point
Damaged brakes and Low thread on rear tires
Cadillac VISTIQ · In Progress
Diagnosis
Damaged brakes and Low thread on rear tires
Repair Notes
[23 Oct 2026 13:12] New brakes were added and Tires were replaced
Auto&Turbo
Your Car My Passion
Mister Auto & Turbo
Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Hello, Teboho

Pick A Time.

Back

29 Oct 2026

09:00 | 10:00 | ✓ 11:00 | 12:00 | 13:00 | 14:00 | 15:00 | 16:00

Notes (optional)

I just need a proper service check.

Confirm Booking

Back

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Proof Of Pay

Vehicle
Cadillac VISTIQ
Registration Number
ESV FS
Quotation Job Card
job-012
Customer
Teboho Pule
Total Amount
R40000

Upload Payment Document

Upload your proof of payment below.

PDF, JPG or PNG • Maximum combined size: 10 MB

Tap To Upload

Choose one or multiple files

Upload Document

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

+ Register A Vehicle

Quick Actions...

Book A Service

Quotations

Repair
History

Notifications

Complaints

Upload Proof
Payment.

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .



Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

← Back to Log In

Create Your Account.

Full Name

Lehlokoa Pule

Email Address

LehlokoaPule@gmail.com

Phone Number

0634025653

Password

LehlokoaPule@123

Register An Account

An account with this email already exists. Please log in.

Quotation Job Card

job-009

Customer

Lehlokoa Pule

Total Amount

R16500

Upload Payment Document

Upload your proof of payment below.

PDF, JPG or PNG • Maximum combined size: 10 MB



Tap To Upload

Choose one or multiple files

Selected Documents (1) 142 KB / 10 MB

9.86 MB remaining



Screenshot 2026-10-22 164710.png

142 KB

+ Add More Files

Upload Document



Auto&Turbo

Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Hello, Teboho

Complaints.

Complaint Submitted

Thank you. Reception will review it and contact you.

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Hello, Teboho

Refresh | Contact Us | Log Out | Edit Profile

Your Vehicles.

Cadillac VISTIQ
ESV FS - No active repair

+ Register A Vehicle

Quick Actions...

Book A Service

Quotations

Repair History

Notifications

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance

Vehicle saved

Hello, Teboho

Current Status.

Cadillac VISTIQ

ESV FS · Inspection
Job Card ID: job-012
Mileage: 1000 km

Repair Progress.

Diagnosis

Damaged brakes and Low thread on rear tires

Repair Notes

[23 Oct 2026 13:12] New brakes were added and Tires were replaced

- ✓ Inspection
- ○ Quotation

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Damaged brakes and Low thread on rear tires

Repair Notes

[23 Oct 2026 13:12] New brakes were added and Tires were replaced

- ✅ Inspection
- ○ Quotation
- ○ In Progress
- ○ Quality Check
- ○ Ready for Collection
- ○ Collected

Refresh Status

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Hello, Teboho

Complaints.

Complaint Type

Other

Vehicle (optional)

Cadillac VISTIQ (ESV FS)

Job (optional)

None

Complaint Description

Taking a long time to respond to my booking.

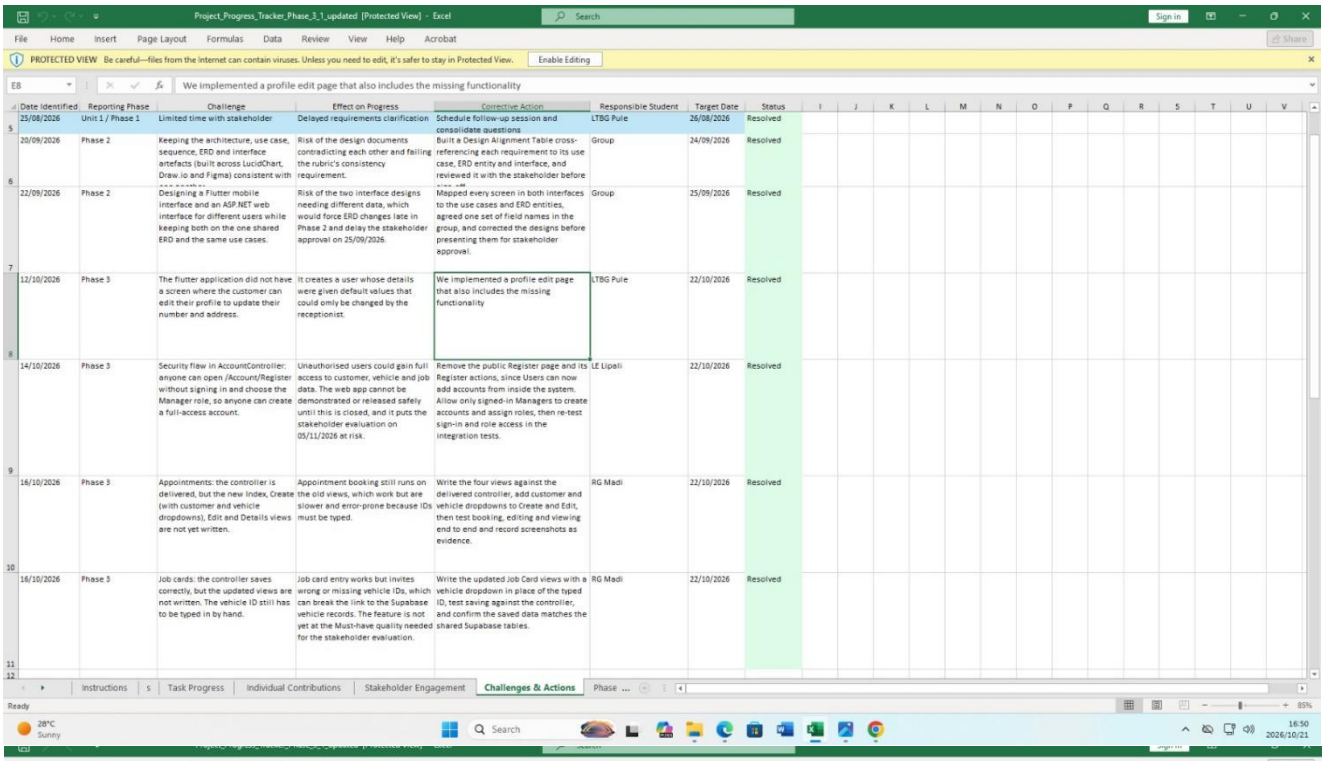
Submit Complaint

Auto&Turbo
Your Car My Passion

Mister Auto & Turbo

Mister Auto and Turbo Offers you Trusted Quality Repairs and Maintainance on all Models and Make of Cars .

Progress Tracker



Project_Progress_Tracker_Phase_3_1_updated [Protected View] - Excel

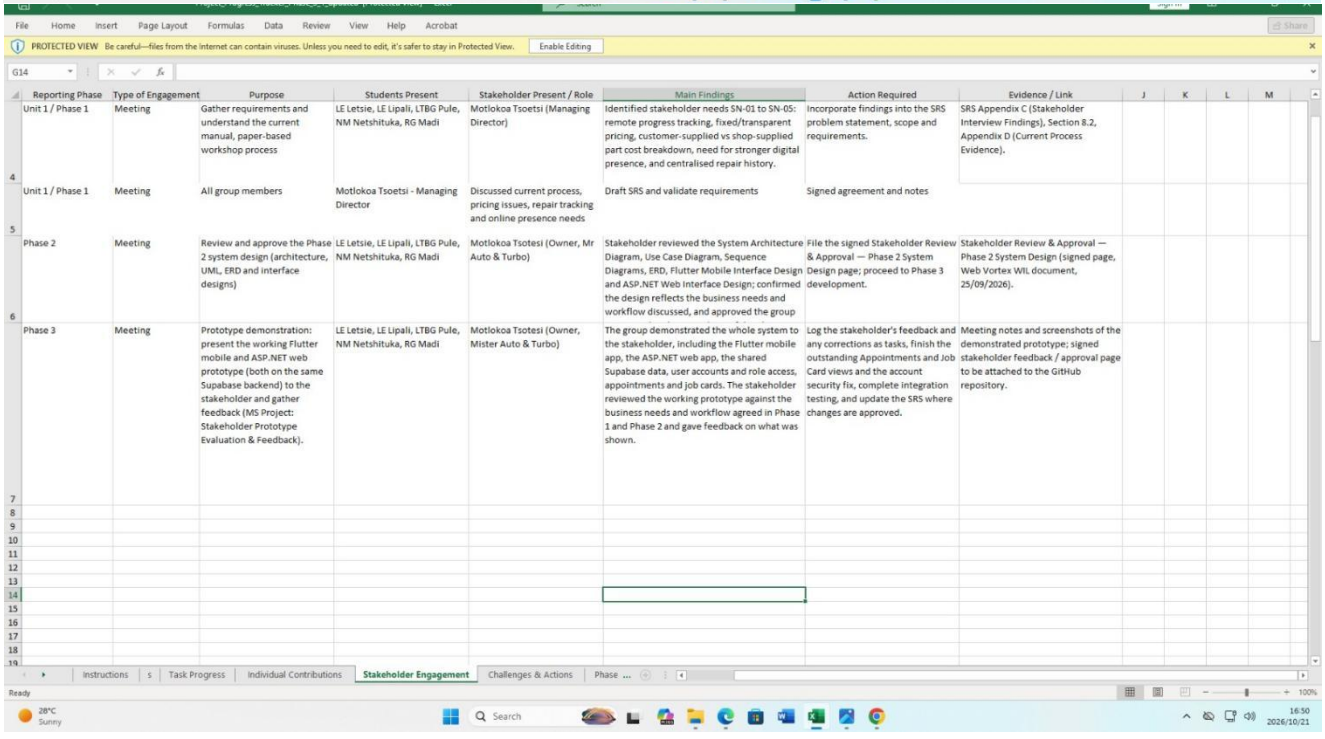
PROTECTED VIEW Be careful—files from the Internet can contain viruses. Unless you need to edit, it's safer to stay in Protected View. Enable Editing

E8: We implemented a profile edit page that also includes the missing functionality

Date Identified	Reporting Phase	Challenge	Effect on Progress	Corrective Action	Responsible Student	Target Date	Status
25/08/2026	Unit 1 / Phase 1	Limited time with stakeholder	Delayed requirements clarification	Schedule follow-up session and consolidate questions	LTBG Pule	26/08/2026	Resolved
20/09/2026	Phase 2	Keeping the architecture, use case, sequence, ERD and interface artefacts (built across LucidChart, Draw.io and Figma) consistent with	Risk of the design documents contradicting each other and failing the rubric's consistency requirement.	Built a Design Alignment Table cross-referencing each requirement to its use case, ERD entity and interface, and reviewed it with the stakeholder before	Group	24/09/2026	Resolved
22/09/2026	Phase 2	Designing a Flutter mobile interface and an ASP.NET web interface for different users while keeping both on the one shared ERD and the same use cases.	Risk of the two interface designs needing different data, which would force ERD changes late in Phase 2 and delay the stakeholder approval on 25/09/2026.	Mapped every screen in both interfaces to the use cases and ERD entities, agreed one set of field names in the group, and corrected the designs before presenting them for stakeholder approval.	Group	25/09/2026	Resolved
12/10/2026	Phase 3	The flutter application did not have a screen where the customer can edit their profile to update their number and address.	It creates a user whose details were given default values that could only be changed by the receptionist.	We implemented a profile edit page that also includes the missing functionality	LTBG Pule	22/10/2026	Resolved
14/10/2026	Phase 3	Security flaw in AccountController: anyone can open /Account/Register without signing in and choose the Manager role, so anyone can create a full-access account.	Unauthorised users could gain full access to customer, vehicle and job data. The web app cannot be demonstrated or released safely until this is closed, and it puts the stakeholder evaluation on 05/11/2026 at risk.	Remove the public Register page and its Register actions, since Users can now add accounts from inside the system. Allow only signed-in Managers to create accounts and assign roles, then re-test sign-in and role access in the integration tests.	LE Lipali	22/10/2026	Resolved
16/10/2026	Phase 3	Appointments: the controller is delivered, but the new Index, Create (with customer and vehicle dropdowns), Edit and Details views are not yet written.	Appointment booking still runs on the old views, which work but are slower and error-prone because IDs must be typed.	Write the four views against the delivered controller, add customer and vehicle dropdowns to Create and Edit, then test booking, editing and viewing end to end and record screenshots as evidence.	RG Madi	22/10/2026	Resolved
16/10/2026	Phase 3	Job cards: the controller saves correctly, but the updated views are not written. The vehicle ID still has to be typed in by hand.	Job card entry works but invites wrong or missing vehicle IDs, which can break the link to the Supabase vehicle records. The feature is not yet at the Must-have quality needed for the stakeholder evaluation.	Write the updated Job Card views with a vehicle dropdown in place of the typed ID, test saving against the controller, and confirm the saved data matches the shared Supabase tables.	RG Madi	22/10/2026	Resolved

Instructions | s | Task Progress | Individual Contributions | Stakeholder Engagement | Challenges & Actions | Phase ...

Ready



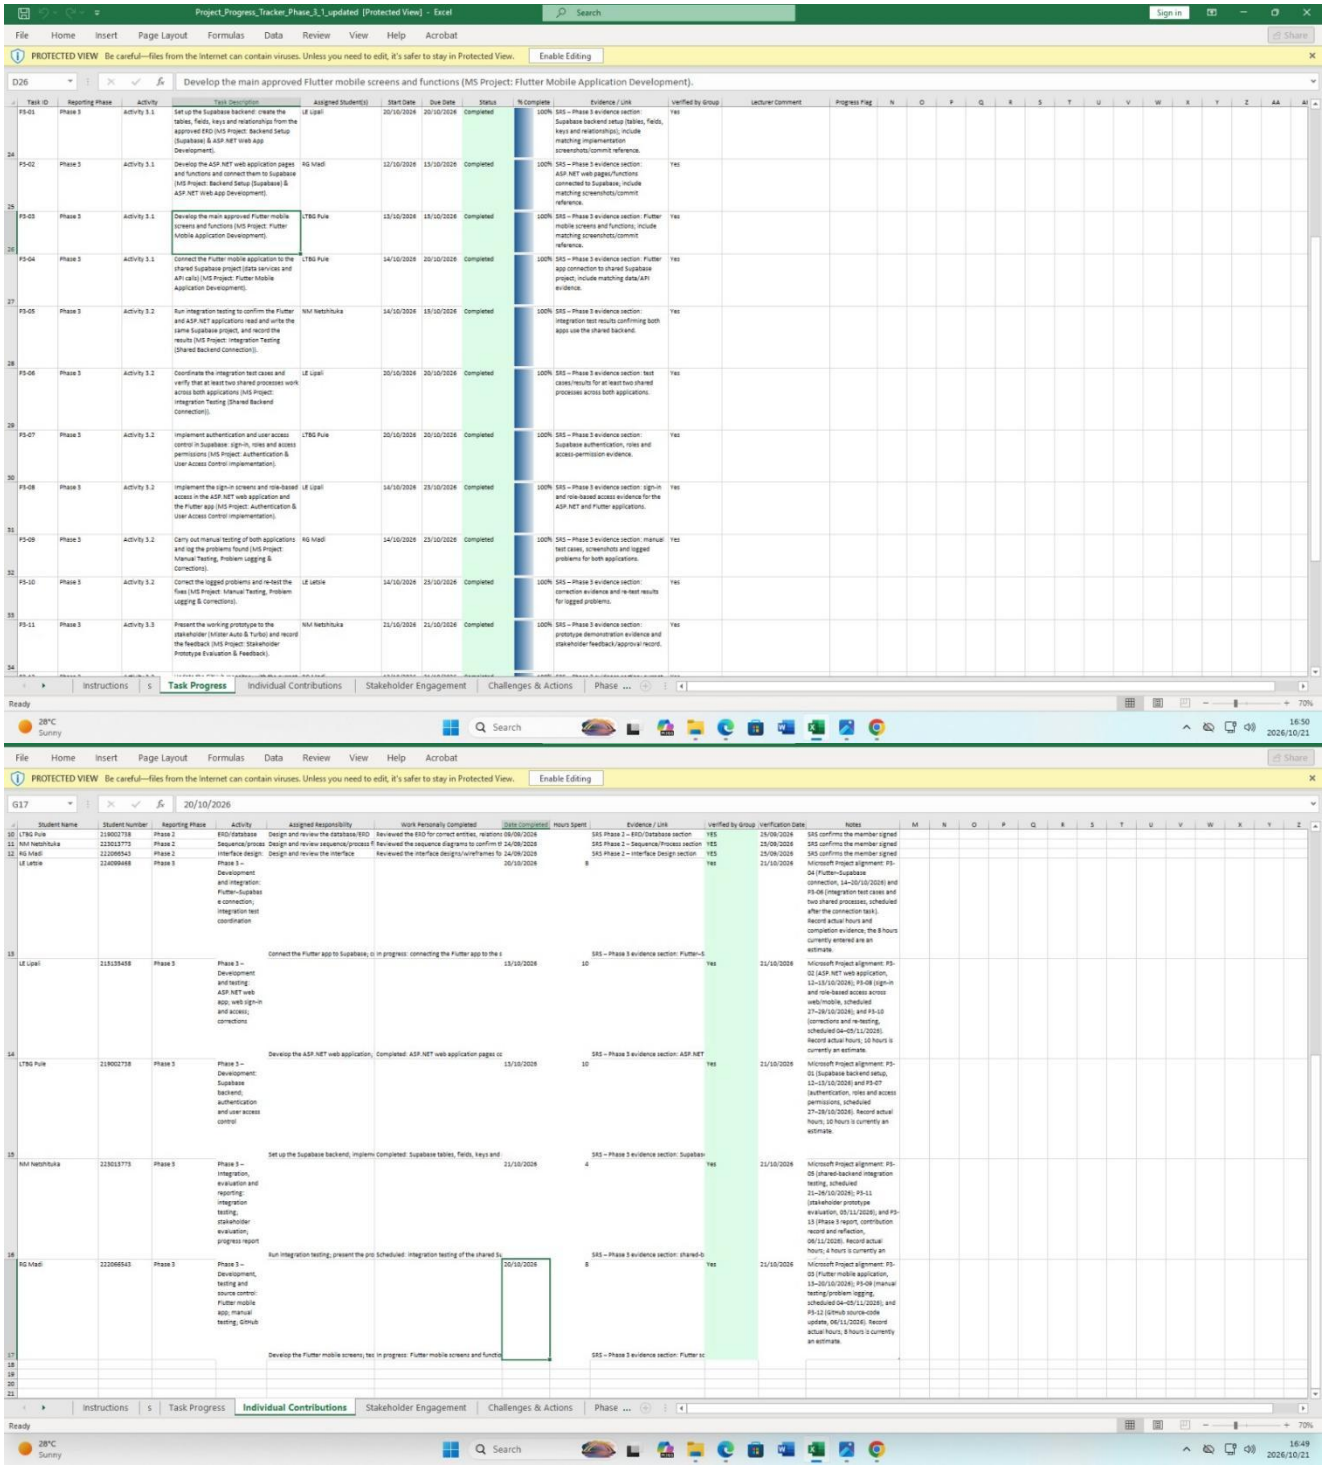
PROTECTED VIEW Be careful—files from the Internet can contain viruses. Unless you need to edit, it's safer to stay in Protected View. Enable Editing

G14:

Reporting Phase	Type of Engagement	Purpose	Students Present	Stakeholder Present / Role	Main Findings	Action Required	Evidence / Link
Unit 1 / Phase 1	Meeting	Gather requirements and understand the current manual, paper-based workshop process	LE Letsie, LE Lipali, LTBG Pule, NM Netshituka, RG Madi	Motlokoa Tsoetsi (Managing Director)	Identified stakeholder needs SN-01 to SN-05: remote progress tracking, fixed/transparent pricing, customer-supplied vs shop-supplied part cost breakdown, need for stronger digital presence, and centralised repair history.	Incorporate findings into the SRS problem statement, scope and requirements.	SRS Appendix C (Stakeholder Interview Findings), Section 8.2, Appendix D (Current Process Evidence).
Unit 1 / Phase 1	Meeting	All group members	Motlokoa Tsoetsi - Managing Director	Discussed current process, pricing issues, repair tracking and online presence needs	Draft SRS and validate requirements	Signed agreement and notes	
Phase 2	Meeting	Review and approve the Phase 2 system design (architecture, UML, ERD and interface designs)	LE Letsie, LE Lipali, LTBG Pule, NM Netshituka, RG Madi	Motlokoa Tsotesi (Owner, Mr Auto & Turbo)	Stakeholder reviewed the System Architecture Diagram, Use Case Diagram, Sequence Diagrams, ERD, Flutter Mobile Interface Design and ASP.NET Web Interface Design; confirmed the design reflects the business needs and workflow discussed, and approved the group	File the signed Stakeholder Review & Approval — Phase 2 System Design page; proceed to Phase 3 development.	Stakeholder Review & Approval — Phase 2 System Design (signed page, Web Vortex WIL document, 25/09/2026).
Phase 3	Meeting	Prototype demonstration: present the working Flutter mobile and ASP.NET web prototype (both on the same Supabase backend) to the stakeholder and gather feedback (MS Project: Stakeholder Prototype Evaluation & Feedback).	LE Letsie, LE Lipali, LTBG Pule, NM Netshituka, RG Madi	Motlokoa Tsotesi (Owner, Mister Auto & Turbo)	The group demonstrated the whole system to the stakeholder, including the Flutter mobile app, the ASP.NET web app, the shared Supabase data, user accounts and role access, appointments and job cards. The stakeholder reviewed the working prototype against the business needs and workflow agreed in Phase 1 and Phase 2 and gave feedback on what was shown.	Log the stakeholder's feedback and any corrections as tasks, finish the outstanding Appointments and Job Card views and the account security fix, complete integration testing, and update the SRS where changes are approved.	Meeting notes and screenshots of the demonstrated prototype; signed stakeholder feedback / approval page to be attached to the GitHub repository.

Instructions | s | Task Progress | Individual Contributions | Stakeholder Engagement | Challenges & Actions | Phase ...

Ready



Project_Progress_Tracker_Phase_3_1_updated [Protected View] - Excel

PROTECTED VIEW Be careful—files from the Internet can contain viruses. Unless you need to edit, it's safer to stay in Protected View. Enable Editing

D26: Develop the main approved Flutter mobile screens and functions (MS Project: Flutter Mobile Application Development).

Task ID	Reporting Phase	Activity	Task Description	Assigned Student(s)	Start Date	Due Date	Status	% Complete	Evidence / Link	Verified by Group	Lecturer Comment	Progress Flag
P3-01	Phase 3	Activity 3.1	Set up the Supabase backend: create the tables, fields, keys and relationships from the approved ERD (MS Project: Backend Setup (Supabase) & ASP.NET Web App Development).	LE Lipali	20/10/2026	20/10/2026	Completed	100%	SRS – Phase 3 evidence section: Supabase backend setup (tables, fields, keys and relationships); include matching implementation screenshots/commit reference.	Yes		
P3-02	Phase 3	Activity 3.1	Develop the ASP.NET web application pages and functions and connect them to Supabase (MS Project: Backend Setup (Supabase) & ASP.NET Web App Development).	RG Madi	12/10/2026	15/10/2026	Completed	100%	SRS – Phase 3 evidence section: ASP.NET web pages/functions connected to Supabase; include matching screenshots/commit reference.	Yes		
P3-03	Phase 3	Activity 3.1	Develop the main approved Flutter mobile screens and functions (MS Project: Flutter Mobile Application Development).	LTBG Pule	13/10/2026	15/10/2026	Completed	100%	SRS – Phase 3 evidence section: Flutter mobile screens and functions; include matching screenshots/commit reference.	Yes		
P3-04	Phase 3	Activity 3.1	Connect the Flutter mobile application to the shared Supabase project (data services and API calls) (MS Project: Flutter Mobile Application Development).	LTBG Pule	14/10/2026	20/10/2026	Completed	100%	SRS – Phase 3 evidence section: Flutter app connection to shared Supabase project, include matching data/API evidence.	Yes		
P3-05	Phase 3	Activity 3.2	Run integration testing to confirm the Flutter and ASP.NET applications read and write the same Supabase project, and record the results (MS Project: Integration Testing (Shared Backend Connection)).	NM Netshituka	14/10/2026	15/10/2026	Completed	100%	SRS – Phase 3 evidence section: integration test results confirming both apps use the shared backend.	Yes		
P3-06	Phase 3	Activity 3.2	Coordinate the integration test cases and verify that at least two shared processes work across both applications (MS Project: Integration Testing (Shared Backend Connection)).	LE Lipali	20/10/2026	20/10/2026	Completed	100%	SRS – Phase 3 evidence section: test cases/results for at least two shared processes across both applications.	Yes		
P3-07	Phase 3	Activity 3.2	Implement authentication and user access control in Supabase: sign-in, roles and access permissions (MS Project: Authentication & User Access Control implementation).	LTBG Pule	20/10/2026	20/10/2026	Completed	100%	SRS – Phase 3 evidence section: Supabase authentication, roles and access-permission evidence.	Yes		
P3-08	Phase 3	Activity 3.2	Implement the sign-in screens and role-based access in the ASP.NET web application and the Flutter app (MS Project: Authentication & User Access Control implementation).	LE Lipali	14/10/2026	25/10/2026	Completed	100%	SRS – Phase 3 evidence section: sign-in and role-based access evidence for the ASP.NET and Flutter applications.	Yes		
P3-09	Phase 3	Activity 3.2	Carry out manual testing of both applications and log the problems found (MS Project: Manual Testing, Problem Logging & Corrections).	RG Madi	14/10/2026	25/10/2026	Completed	100%	SRS – Phase 3 evidence section: manual test cases, screenshots and logged problems for both applications.	Yes		
P3-10	Phase 3	Activity 3.2	Correct the logged problems and re-test the fixes (MS Project: Manual Testing, Problem Logging & Corrections).	LE Letsie	14/10/2026	25/10/2026	Completed	100%	SRS – Phase 3 evidence section: correction evidence and re-test results for logged problems.	Yes		
P3-11	Phase 3	Activity 3.3	Present the working prototype to the stakeholder (Mister Auto & Turbo) and record the feedback (MS Project: Stakeholder Prototype Evaluation & Feedback).	NM Netshituka	21/10/2026	21/10/2026	Completed	100%	SRS – Phase 3 evidence section: prototype demonstration evidence and stakeholder feedback/approval record.	Yes		

Instructions | s | Task Progress | Individual Contributions | Stakeholder Engagement | Challenges & Actions | Phase ...

Ready

28°C Sunny

Search

16:50 2026/10/21

PROTECTED VIEW Be careful—files from the Internet can contain viruses. Unless you need to edit, it's safer to stay in Protected View. Enable Editing

G17: 20/10/2026

Student Name	Student Number	Reporting Phase	Activity	Assigned Responsibility	Work Personally Completed	Date Completed	Hours Spent	Evidence / Link	Verified by Group	Verification Date	Notes
LTBG Pule	219002758	Phase 2	ERD/database	Design and review the database/ERD	Reviewed the ERD for correct entities, relations	08/08/2026		SRS Phase 2 – ERD/Database section	YES	25/08/2026	SRS confirms the member signed
NM Netshituka	223013775	Phase 2	Sequence/proces	Design and review sequence/process fl	Reviewed the sequence diagrams to confirm th	24/08/2026		SRS Phase 2 – Sequence/Process section	YES	25/08/2026	SRS confirms the member signed
RG Madi	222066543	Phase 2	Interface design	Design and review the interface	Reviewed the interface designs/wireframes to	24/08/2026		SRS Phase 2 – Interface Design section	YES	25/08/2026	SRS confirms the member signed
LE Letsie	224099468	Phase 3	Phase 3 – Development and integration: Flutter–Supabase connection; integration test coordination			20/10/2026	8		Yes	21/10/2026	Microsoft Project alignment: P3-04 (Flutter–Supabase connection, 14–20/10/2026) and P3-06 (integration test cases and two shared processes, scheduled after the connection task). Record actual hours and completion evidence; the 8 hours currently entered are an estimate.
			Connect the Flutter app to Supabase; c	In progress: connecting the Flutter app to the s		15/10/2026	10	SRS – Phase 3 evidence section: Flutter–S			
LE Lipali	215135458	Phase 3	Phase 3 – Development and testing: ASP.NET web app; web sign-in and access; corrections						Yes	21/10/2026	Microsoft Project alignment: P3-02 (ASP.NET web application, 12–15/10/2026); P3-08 (sign-in and role-based access across web/mobile, scheduled 27–28/10/2026); and P3-10 (corrections and re-testing, scheduled 04–05/11/2026). Record actual hours; 10 hours is currently an estimate.
			Develop the ASP.NET web application,	Completed: ASP.NET web application pages cc		15/10/2026	10	SRS – Phase 3 evidence section: ASP.NET			
LTBG Pule	219002758	Phase 3	Phase 3 – Development: Supabase backend; authentication and user access control						Yes	21/10/2026	Microsoft Project alignment: P3-01 (Supabase backend setup, 12–15/10/2026) and P3-07 (authentication, roles and access permissions, scheduled 27–28/10/2026). Record actual hours; 10 hours is currently an estimate.
			Set up the Supabase backend, implem	Completed: Supabase tables, fields, keys and		21/10/2026	4	SRS – Phase 3 evidence section: Supabas			
NM Netshituka	223013775	Phase 3	Phase 3 – Integration, evaluation and reporting: integration testing; stakeholder evaluation; progress report						Yes	21/10/2026	Microsoft Project alignment: P3-05 (shared-backend integration testing, scheduled 21–26/10/2026); P3-11 (stakeholder prototype evaluation, 05/11/2026); and P3-13 (Phase 3 report, contribution record and reflection, 06/11/2026). Record actual hours; 4 hours is currently an estimate.
			Run integration testing; present the pro	Scheduled: integration testing of the shared Su		20/10/2026	8	SRS – Phase 3 evidence section: shared-b			
RG Madi	222066543	Phase 3	Phase 3 – Development, testing and source control: Flutter mobile app; manual testing; Github						Yes	21/10/2026	Microsoft Project alignment: P3-03 (Flutter mobile application, 13–20/10/2026); P3-09 (manual testing/problem logging, scheduled 04–05/11/2026); and P3-12 (Github source-code update, 06/11/2026). Record actual hours; 8 hours is currently an estimate.
			Develop the Flutter mobile screens; tes	In progress: Flutter mobile screens and functio				SRS – Phase 3 evidence section: Flutter sc			

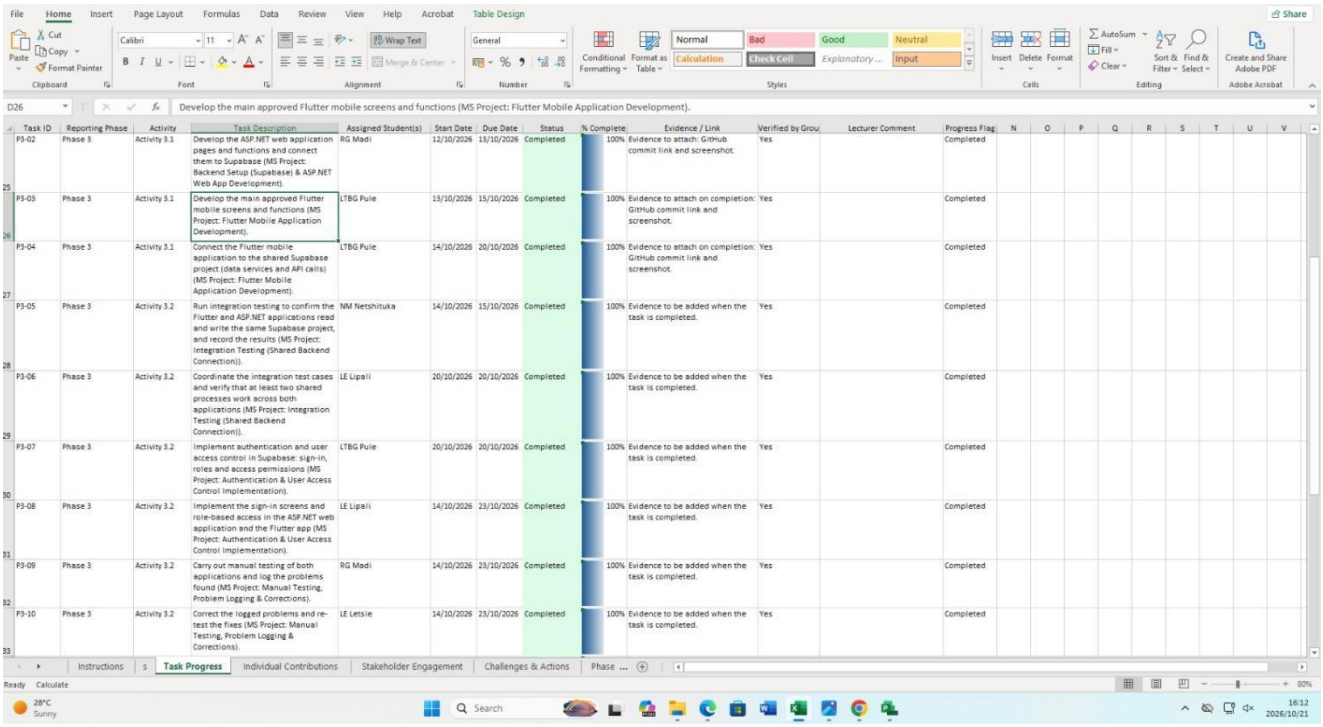
Instructions | s | Task Progress | Individual Contributions | Stakeholder Engagement | Challenges & Actions | Phase ...

Ready

28°C Sunny

Search

16:49 2026/10/21



Task ID	Reporting Phase	Activity	Task Description	Assigned Student(s)	Start Date	Due Date	Status	% Complete	Evidence / Link	Verified by Grou	Lecturer Comment	Progress Flag
P3-02	Phase 3	Activity 3.1	Develop the ASP.NET web application pages and functions and connect them to Supabase (MS Project: Backend Setup (Supabase) & ASP.NET Web App Development).	RG Madi	12/10/2026	13/10/2026	Completed	100%	Evidence to attach: GitHub commit link and screenshot.	Yes		Completed
P3-03	Phase 3	Activity 3.1	Develop the main approved Flutter mobile screens and functions (MS Project: Flutter Mobile Application Development).	LTBG Pule	13/10/2026	15/10/2026	Completed	100%	Evidence to attach on completion: GitHub commit link and screenshot.	Yes		Completed
P3-04	Phase 3	Activity 3.1	Connect the Flutter mobile application to the shared Supabase project (data services and API calls) (MS Project: Flutter Mobile Application Development).	LTBG Pule	14/10/2026	20/10/2026	Completed	100%	Evidence to attach on completion: GitHub commit link and screenshot.	Yes		Completed
P3-05	Phase 3	Activity 3.2	Run integration testing to confirm the Flutter and ASP.NET applications read and write the same Supabase project, and record the results (MS Project: Integration Testing (Shared Backend Connection)).	NM Netshituka	14/10/2026	15/10/2026	Completed	100%	Evidence to be added when the task is completed.	Yes		Completed
P3-06	Phase 3	Activity 3.2	Coordinate the integration test cases and verify that at least two shared processes work across both applications (MS Project: Integration Testing (Shared Backend Connection)).	LE Lipali	20/10/2026	20/10/2026	Completed	100%	Evidence to be added when the task is completed.	Yes		Completed
P3-07	Phase 3	Activity 3.2	Implement authentication and user access control in Supabase: sign-in, roles and access permissions (MS Project: Authentication & User Access Control Implementation).	LTBG Pule	20/10/2026	20/10/2026	Completed	100%	Evidence to be added when the task is completed.	Yes		Completed
P3-08	Phase 3	Activity 3.2	Implement the sign-in screens and role-based access in the ASP.NET web application and the Flutter app (MS Project: Authentication & User Access Control Implementation).	LE Lipali	14/10/2026	23/10/2026	Completed	100%	Evidence to be added when the task is completed.	Yes		Completed
P3-09	Phase 3	Activity 3.2	Carry out manual testing of both applications and log the problems found (MS Project: Manual Testing, Problem Logging & Corrections).	RG Madi	14/10/2026	23/10/2026	Completed	100%	Evidence to be added when the task is completed.	Yes		Completed
P3-10	Phase 3	Activity 3.2	Correct the logged problems and re-test the fixes (MS Project: Manual Testing, Problem Logging & Corrections).	LE Letsie	14/10/2026	23/10/2026	Completed	100%	Evidence to be added when the task is completed.	Yes		Completed

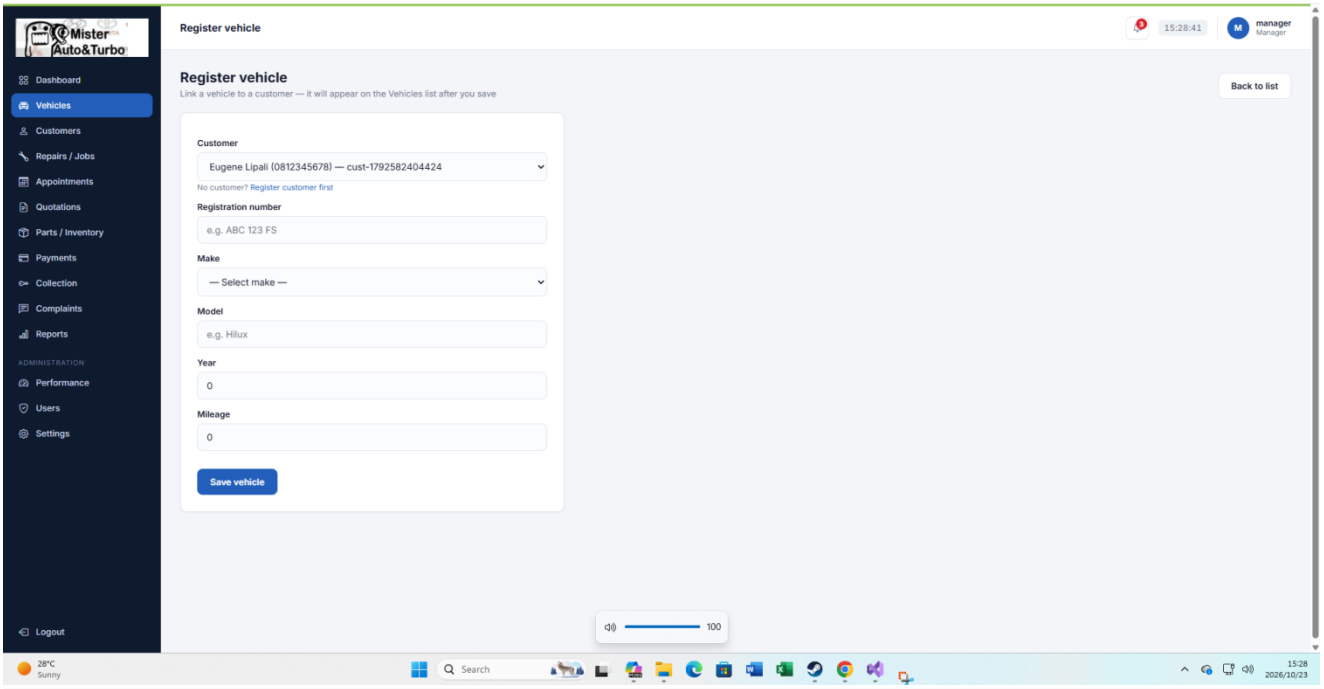
5. ASP.NET Web Application Readiness

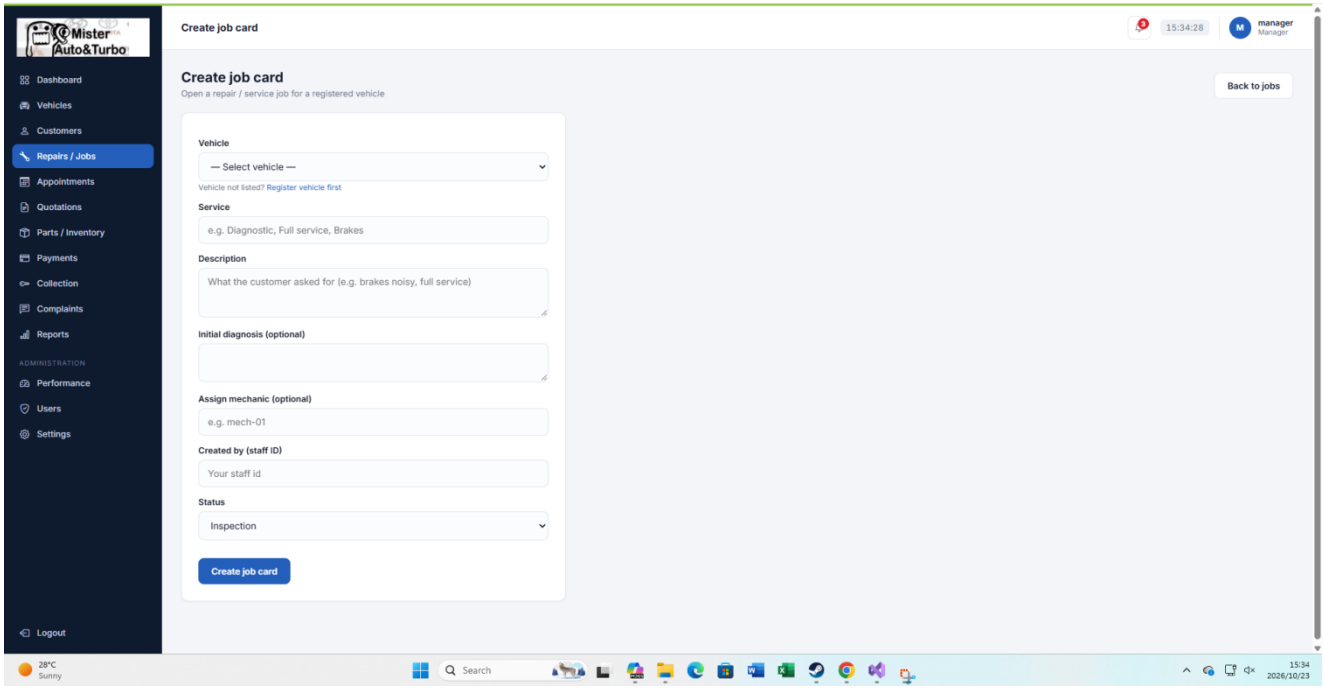
Checkpoint	Expected evidence	Status / notes
Application launches	Web application starts and required pages load.	Verified
Approved pages	Dashboard, customers, vehicles, appointments, jobs/job cards, parts, payments, collection, complaints, users and reports as applicable to the implementation.	Verified
Navigation	Navigation between available pages works.	Verified
Forms and inputs	Required information can be entered and validation behaves appropriately.	Verified
Role-based functions	Manager, Receptionist and Mechanic permissions match the approved design.	Verified
Supabase connection	Web application retrieves and updates data in the shared backend.	Verified
SRS alignment	Implemented functions match approved requirements; gaps are recorded below.	Verified

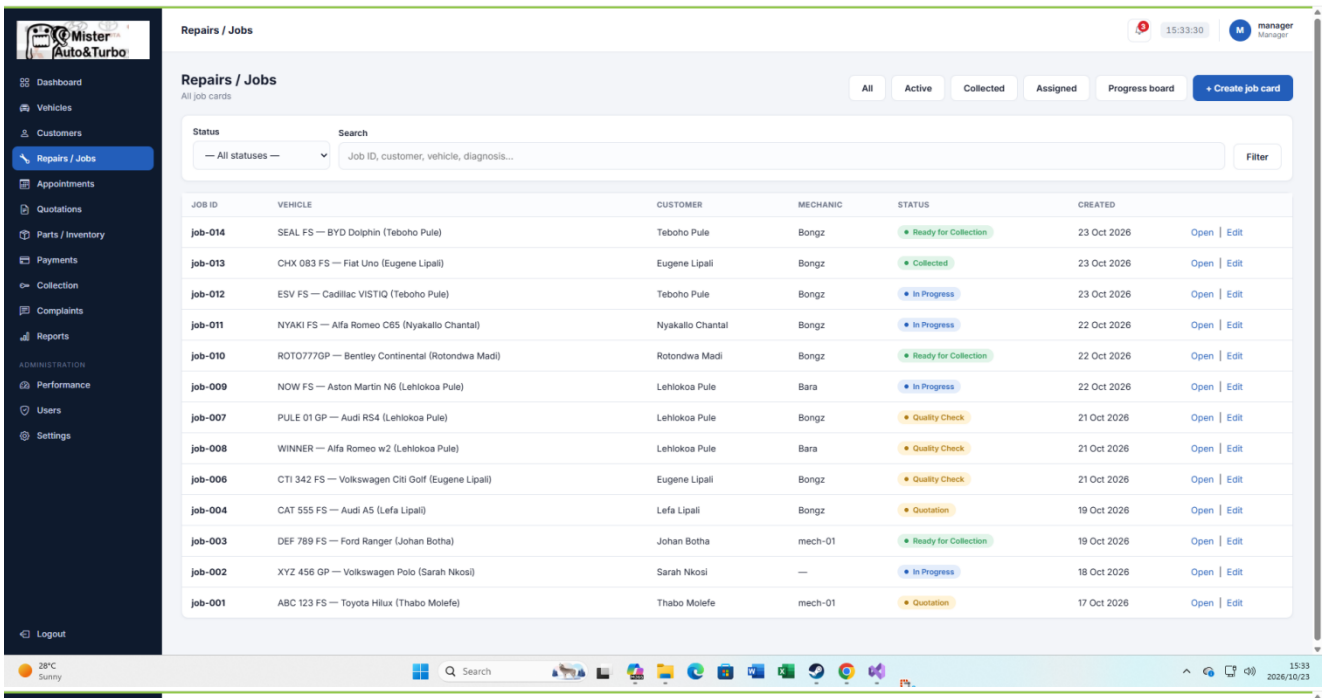
Evidence - ASP.NET Web Application

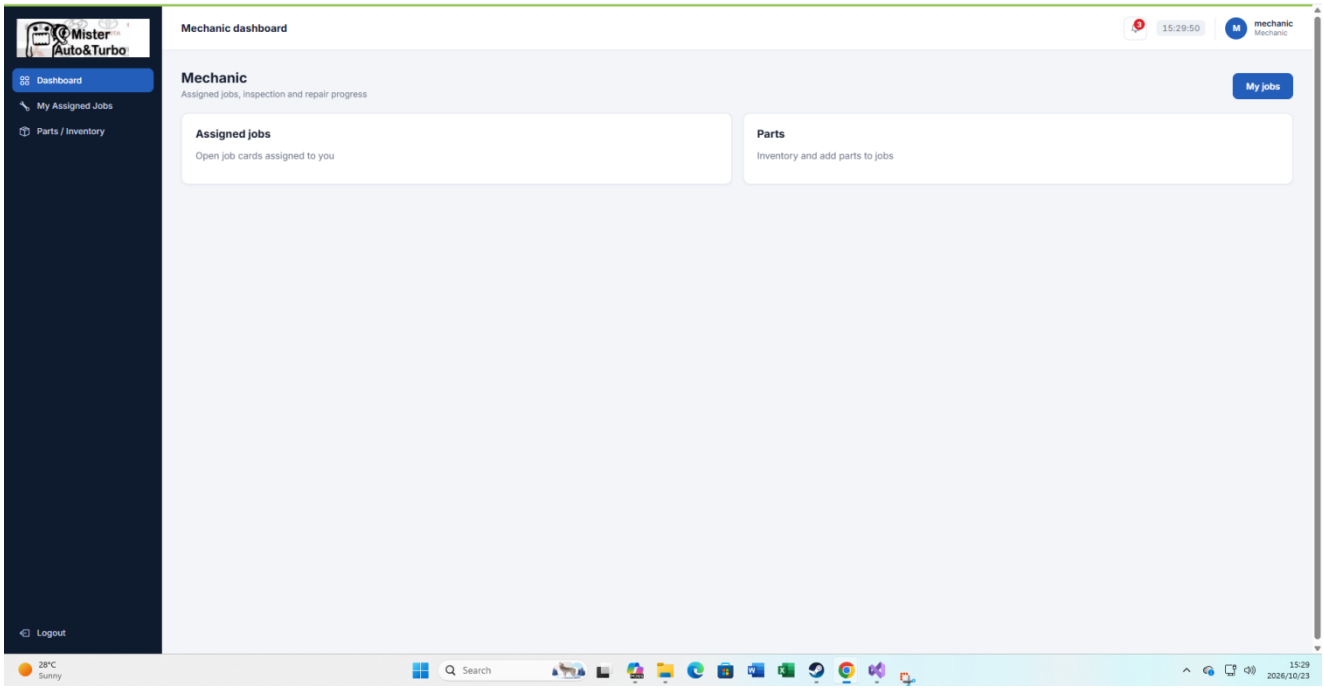
Appointment pages

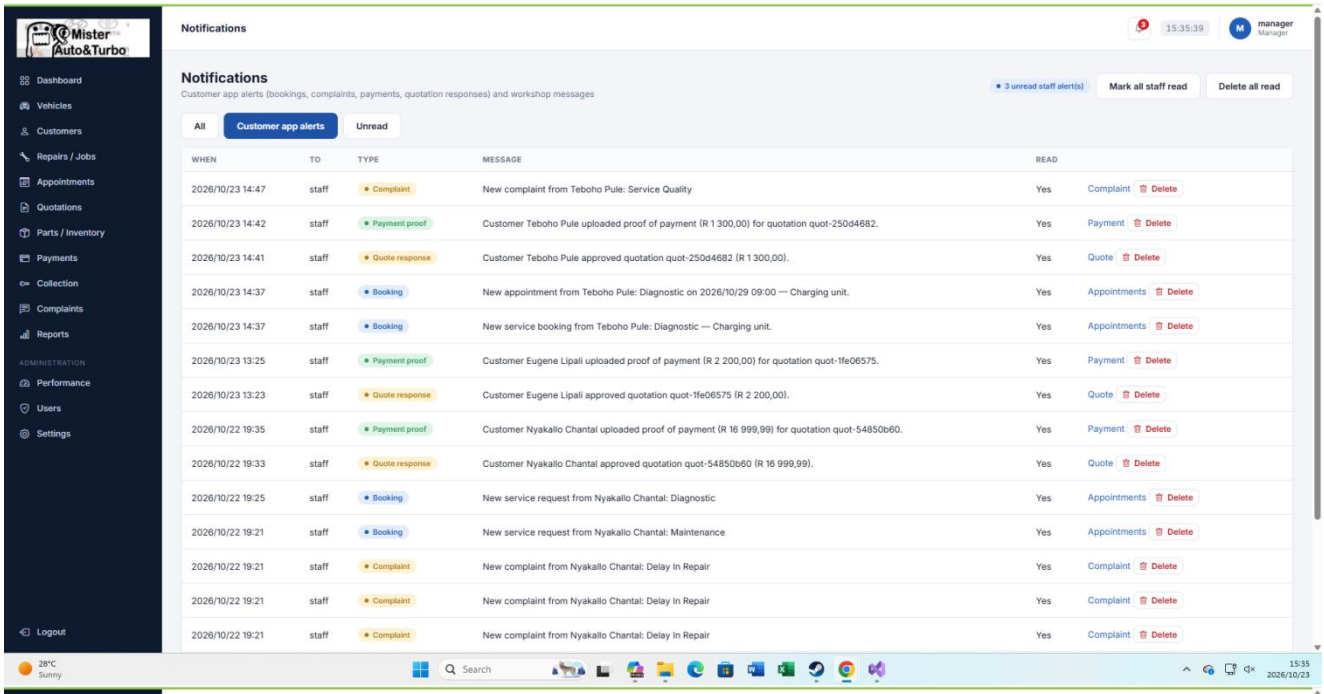
Dashboard details

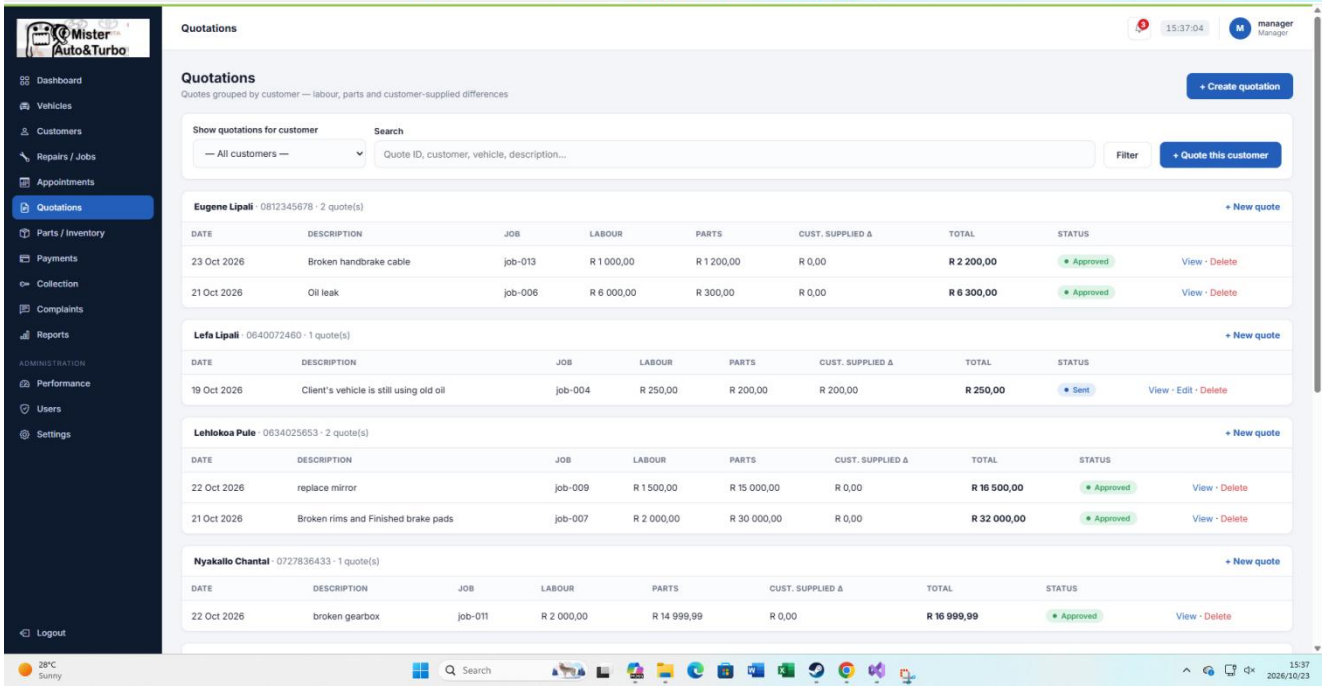

Mister Auto&Turbo
Register vehicle
15:28:41
manager
Manager
Dashboard
Vehicles
Customers
Repairs / Jobs
Appointments
Quotations
Parts / Inventory
Payments
Collection
Complaints
Reports
ADMINISTRATION
Performance
Users
Settings
Logout
Register vehicle
Link a vehicle to a customer — it will appear on the Vehicles list after you save
Back to list
Customer
Eugene Lipali (0812345678) — cust-1792582404424
No customer? Register customer first
Registration number
e.g. ABC 123 FS
Make
— Select make —
Model
e.g. Hilux
Year
0
Mileage
0
Save vehicle
100
28°C
Sunny
Search
15:28
2026/10/23

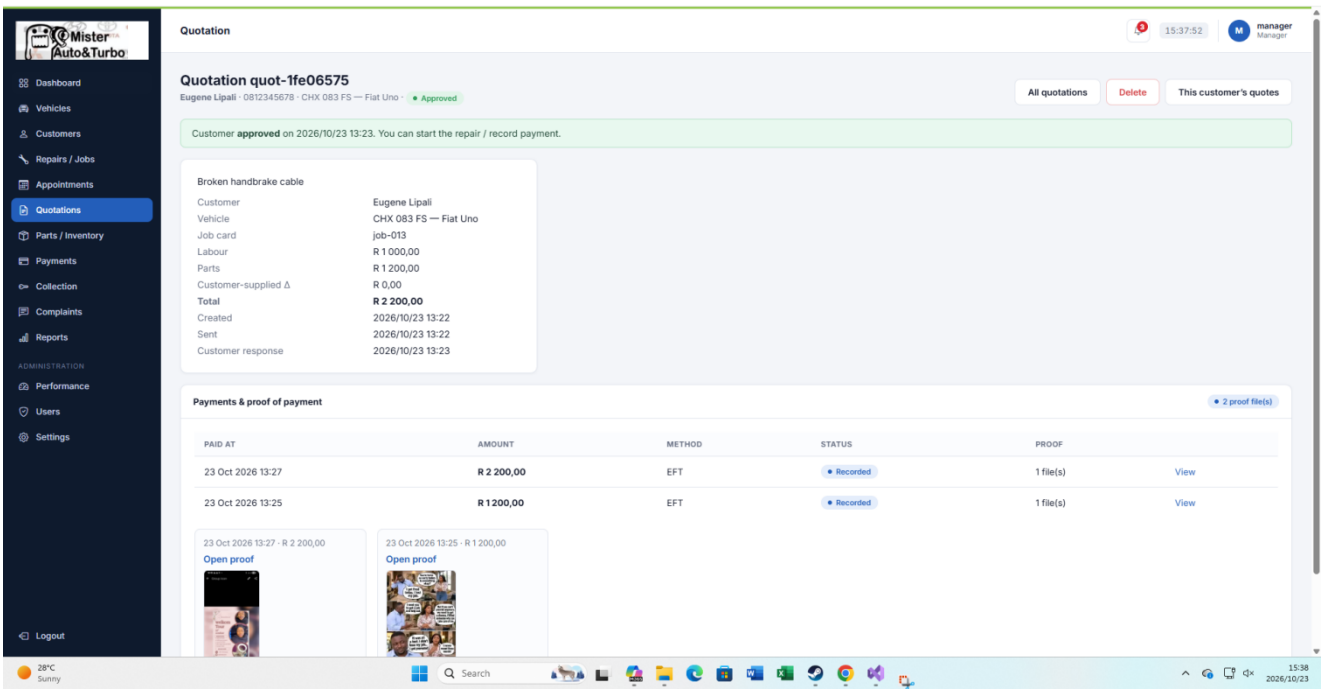

Mister Auto&Turbo
Create job card
15:34:28
manager
Manager
Dashboard
Vehicles
Customers
Repairs / Jobs
Appointments
Quotations
Parts / Inventory
Payments
Collection
Complaints
Reports
ADMINISTRATION
Performance
Users
Settings
Logout
Create job card
Open a repair / service job for a registered vehicle
Back to jobs
Vehicle
— Select vehicle —
Vehicle not listed? Register vehicle first
Service
e.g. Diagnostic, Full service, Brakes
Description
What the customer asked for (e.g. brakes noisy, full service)
Initial diagnosis (optional)
Assign mechanic (optional)
e.g. mech-01
Created by (staff ID)
Your staff id
Status
Inspection
Create job card
28°C
Sunny
Search
15:34
2026/10/23


Mister Auto&Turbo
Repairs / Jobs
15:33:30
manager
Manager
Dashboard
Vehicles
Customers
Repairs / Jobs
Appointments
Quotations
Parts / Inventory
Payments
Collection
Complaints
Reports
ADMINISTRATION
Performance
Users
Settings
Logout
Repairs / Jobs
All job cards
All
Active
Collected
Assigned
Progress board
+ Create job card
Status
— All statuses —
Search
Job ID, customer, vehicle, diagnosis...
Filter
JOB ID
VEHICLE
CUSTOMER
MECHANIC
STATUS
CREATED
job-014 SEAL FS — BYD Dolphin (Teboho Pule) Teboho Pule Bongz Ready for Collection 23 Oct 2026 Open | Edit
job-013 CHX 083 FS — Fiat Uno (Eugene Lipali) Eugene Lipali Bongz Collected 23 Oct 2026 Open | Edit
job-012 ESV FS — Cadillac VISTIQ (Teboho Pule) Teboho Pule Bongz In Progress 23 Oct 2026 Open | Edit
job-011 NYAKI FS — Alfa Romeo C65 (Nyakallo Chantal) Nyakallo Chantal Bongz In Progress 22 Oct 2026 Open | Edit
job-010 ROTO777GP — Bentley Continental (Rotondwa Madi) Rotondwa Madi Bongz Ready for Collection 22 Oct 2026 Open | Edit
job-009 NOW FS — Aston Martin N6 (Lehlokoa Pule) Lehlokoa Pule Bara In Progress 22 Oct 2026 Open | Edit
job-007 PULE 01 GP — Audi RS4 (Lehlokoa Pule) Lehlokoa Pule Bongz Quality Check 21 Oct 2026 Open | Edit
job-008 WINNER — Alfa Romeo w2 (Lehlokoa Pule) Lehlokoa Pule Bara Quality Check 21 Oct 2026 Open | Edit
job-006 CTI 342 FS — Volkswagen Citi Golf (Eugene Lipali) Eugene Lipali Bongz Quality Check 21 Oct 2026 Open | Edit
job-004 CAT 555 FS — Audi A5 (Lefa Lipali) Lefa Lipali Bongz Quotation 19 Oct 2026 Open | Edit
job-003 DEF 789 FS — Ford Ranger (Johan Botha) Johan Botha mech-01 Ready for Collection 19 Oct 2026 Open | Edit
job-002 XYZ 456 GP — Volkswagen Polo (Sarah Nkosi) Sarah Nkosi — In Progress 18 Oct 2026 Open | Edit
job-001 ABC 123 FS — Toyota Hilux (Thabo Molefe) Thabo Molefe mech-01 Quotation 17 Oct 2026 Open | Edit
28°C
Sunny
Search
15:33
2026/10/23


Mister Auto&Turbo
Mechanic dashboard
15:29:50
mechanic
Mechanic
Dashboard
My Assigned Jobs
Parts / Inventory
Logout
Mechanic
Assigned jobs, inspection and repair progress
My jobs
Assigned jobs
Open job cards assigned to you
Parts
Inventory and add parts to jobs
28°C
Sunny
Search
15:29
2026/10/23


Mister Auto&Turbo
Notifications
15:35:39
manager
Manager
Dashboard
Vehicles
Customers
Repairs / Jobs
Appointments
Quotations
Parts / Inventory
Payments
Collection
Complaints
Reports
ADMINISTRATION
Performance
Users
Settings
Logout
Notifications
Customer app alerts (bookings, complaints, payments, quotation responses) and workshop messages
3 unread staff alert(s)
Mark all staff read
Delete all read
All
Customer app alerts
Unread
WHEN TO TYPE MESSAGE READ
2026/10/23 14:47 staff Complaint New complaint from Teboho Pule: Service Quality Yes Complaint Delete
2026/10/23 14:42 staff Payment proof Customer Teboho Pule uploaded proof of payment (R 1 300,00) for quotation quot-250d4682. Yes Payment Delete
2026/10/23 14:41 staff Quote response Customer Teboho Pule approved quotation quot-250d4682 (R 1 300,00). Yes Quote Delete
2026/10/23 14:37 staff Booking New appointment from Teboho Pule: Diagnostic on 2026/10/29 09:00 — Charging unit. Yes Appointments Delete
2026/10/23 14:37 staff Booking New service booking from Teboho Pule: Diagnostic — Charging unit. Yes Appointments Delete
2026/10/23 13:25 staff Payment proof Customer Eugene Lipali uploaded proof of payment (R 2 200,00) for quotation quot-1fe06575. Yes Payment Delete
2026/10/23 13:23 staff Quote response Customer Eugene Lipali approved quotation quot-1fe06575 (R 2 200,00). Yes Quote Delete
2026/10/22 19:35 staff Payment proof Customer Nyakallo Chantal uploaded proof of payment (R 16 999,99) for quotation quot-54850b60. Yes Payment Delete
2026/10/22 19:33 staff Quote response Customer Nyakallo Chantal approved quotation quot-54850b60 (R 16 999,99). Yes Quote Delete
2026/10/22 19:25 staff Booking New service request from Nyakallo Chantal: Diagnostic Yes Appointments Delete
2026/10/22 19:21 staff Booking New service request from Nyakallo Chantal: Maintenance Yes Appointments Delete
2026/10/22 19:21 staff Complaint New complaint from Nyakallo Chantal: Delay In Repair Yes Complaint Delete
2026/10/22 19:21 staff Complaint New complaint from Nyakallo Chantal: Delay In Repair Yes Complaint Delete
2026/10/22 19:21 staff Complaint New complaint from Nyakallo Chantal: Delay In Repair Yes Complaint Delete
28°C
Sunny
Search
15:35
2026/10/23


Mister Auto&Turbo
Quotations
15:37:04
manager
Manager
Dashboard
Vehicles
Customers
Repairs / Jobs
Appointments
Quotations
Parts / Inventory
Payments
Collection
Complaints
Reports
ADMINISTRATION
Performance
Users
Settings
Logout
Quotations
Quotes grouped by customer — labour, parts and customer-supplied differences
+ Create quotation
Show quotations for customer
— All customers —
Search
Quote ID, customer, vehicle, description...
Filter
+ Quote this customer
Eugene Lipali · 0812345678 · 2 quote(s)
+ New quote
DATE DESCRIPTION JOB LABOUR PARTS CUST. SUPPLIED Δ TOTAL STATUS
23 Oct 2026 Broken handbrake cable job-013 R 1 000,00 R 1 200,00 R 0,00 R 2 200,00 Approved View · Delete
21 Oct 2026 Oil leak job-006 R 6 000,00 R 300,00 R 0,00 R 6 300,00 Approved View · Delete
Lefa Lipali · 0640072460 · 1 quote(s)
+ New quote
DATE DESCRIPTION JOB LABOUR PARTS CUST. SUPPLIED Δ TOTAL STATUS
19 Oct 2026 Client's vehicle is still using old oil job-004 R 250,00 R 200,00 R 200,00 R 250,00 Sent View · Edit · Delete
Lehlokoa Pule · 0634025653 · 2 quote(s)
+ New quote
DATE DESCRIPTION JOB LABOUR PARTS CUST. SUPPLIED Δ TOTAL STATUS
22 Oct 2026 replace mirror job-009 R 1 500,00 R 15 000,00 R 0,00 R 16 500,00 Approved View · Delete
21 Oct 2026 Broken rims and Finished brake pads job-007 R 2 000,00 R 30 000,00 R 0,00 R 32 000,00 Approved View · Delete
Nyakallo Chantal · 0727836433 · 1 quote(s)
+ New quote
DATE DESCRIPTION JOB LABOUR PARTS CUST. SUPPLIED Δ TOTAL STATUS
22 Oct 2026 broken gearbox job-011 R 2 000,00 R 14 999,99 R 0,00 R 16 999,99 Approved View · Delete
28°C
Sunny
Search
15:37
2026/10/23



SCREENSHOTS for the ASP.NET are all attached in the hyperlink below.

Images

6. Cross-Application Integration

At least two important shared processes must be demonstrated end to end. The processes below are based on the approved Mr Auto & Turbo workflow. They are proposed demonstration scenarios, not statements that integration has already been proven.

Shared process	Flutter action	ASP.NET action	Working? / evidence
Process 1: Repair-status tracking	Customer opens vehicle status/timeline and views the latest status.	Mechanic updates the job status (for example, In Progress, Quality Check or Ready for Collection).	Verified
Process 2: Job and vehicle record visibility	Customer views the relevant vehicle/service information where authorised.	Receptionist registers/checks in a vehicle and authorised staff create or update its job card.	Verified

Optional process: Notifications	Customer or mechanic views a relevant notification if this feature is implemented.	Staff action or job-status change triggers the configured notification process.	Verified

For each selected process, demonstrate that data entered or changed in one application is saved to Supabase and can be retrieved by the other application where required. Check consistent fields and values, refresh/retrieval behaviour, and role permissions. Record any manual refresh, delay or other limitation honestly.

7. Alignment with Approved Requirements

The following requirements are drawn from the existing SRS. Use the status column to record demonstrated implementation results. Do not mark a function as working unless the group has verified it.

Approved requirement	Application	Implementation evidence to demonstrate	Status
FR-01 Customer registration	ASP.NET / Flutter as implemented	Create or register a customer account/record using the implemented workflow.	Verified
FR-02 Vehicle registration	ASP.NET	Register a vehicle against the correct customer.	Verified
FR-03 Digital job cards	ASP.NET	Create and retrieve a job card with reported issue and inspection notes.	Verified
FR-04 Diagnosis and quotation generation	ASP.NET	Record diagnosis and generate/view a quotation where implemented.	Verified
FR-05 Customer quotation approval workflow	Flutter / ASP.NET	Show approval request and record/view the approval decision where implemented.	Verified
FR-06 Repair status tracking	Flutter / ASP.NET	Update job status on the staff side and retrieve it on the customer side.	Verified
FR-07 Payment recording	ASP.NET	Authorised management user records and retrieves a payment.	Verified
FR-08 Ready-for-collection notifications	Flutter / configured notification service	Demonstrate notification delivery if implemented; otherwise record the gap.	Verified
FR-09 Itemised quotations	Flutter / ASP.NET as implemented	Show labour and parts costs separately.	Verified
FR-10 Customer-supplied part comparison	ASP.NET / customer view as implemented	Show the applicable price difference for customer-supplied versus business-supplied parts.	Verified
Role-based access	ASP.NET and Flutter as applicable	Verify the user role restricts access to permitted pages, records and actions.	Verified
Shared Supabase backend	Flutter + ASP.NET	Verify both applications read/write the same Supabase project and consistent records.	Verified

Evidence - Approved Requirements (The contract between WebVortex and MR Auto&Turbo)

MR AUTO & TURBO

Stakeholder Review & Approval - Phase 3 System Developed

This page confirms that the stakeholder listed below has reviewed the Phase 2 system design for the Mr Auto & Turbo Workshop Management System, prepared as part of the ITC327W Work-Integrated Learning module (Central University of Technology, Free State).

Project

Mr Auto & Turbo Workshop Management System - a Flutter mobile application and ASP.NET web application, sharing a Supabase backend, designed to manage customers, vehicles, repair jobs, appointments, parts, payments, and complaints for the workshop.

Artefacts Reviewed

Artefact	Reviewed
System Architecture Diagram	☑Yes ☐ No
Use Case Diagram	☑Yes ☐ No
Sequence Diagrams	☑ Yes ☐ No
Entity Relationship Diagram (ERD)	☑ Yes ☐ No
Flutter Mobile Interface Design	☑Yes ☐ No
ASP.NET Web Application	☑Yes ☐ No
Flutter Mobile Application	☑Yes ☐ No
Explained Shared Supabase Backend	☑Yes ☐ No
Reviewed changes requested by Mr Motlokoa	☑Yes ☐ No
Demonstrated to make it understandable for staff	☑Yes ☐ No
ASP.NET Web Interface Design	☑ Yes ☐ No

Stakeholder Statement

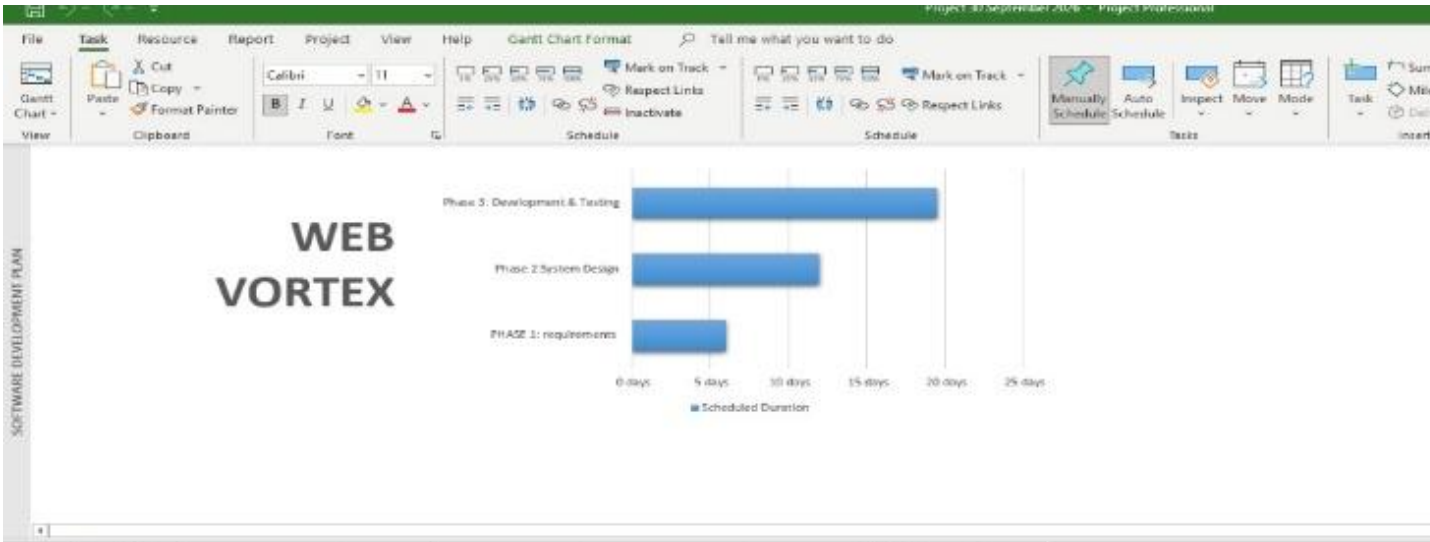
I, the undersigned, confirm that I have reviewed the system design listed above, prepared by the project group for Mr Auto & Turbo. I confirm that the design reflects the business needs and workflow discussed with the group, and I approve the group to proceed to the next phase of development on this basis.

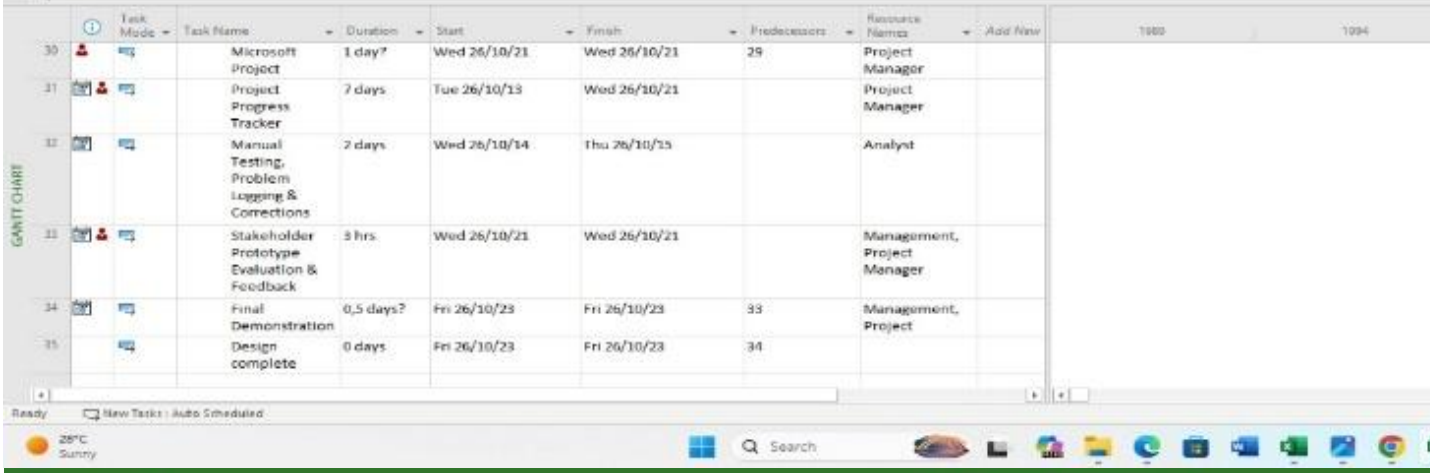
I understand that this design may be refined during development, and that any significant change to scope will be discussed with me before implementation.

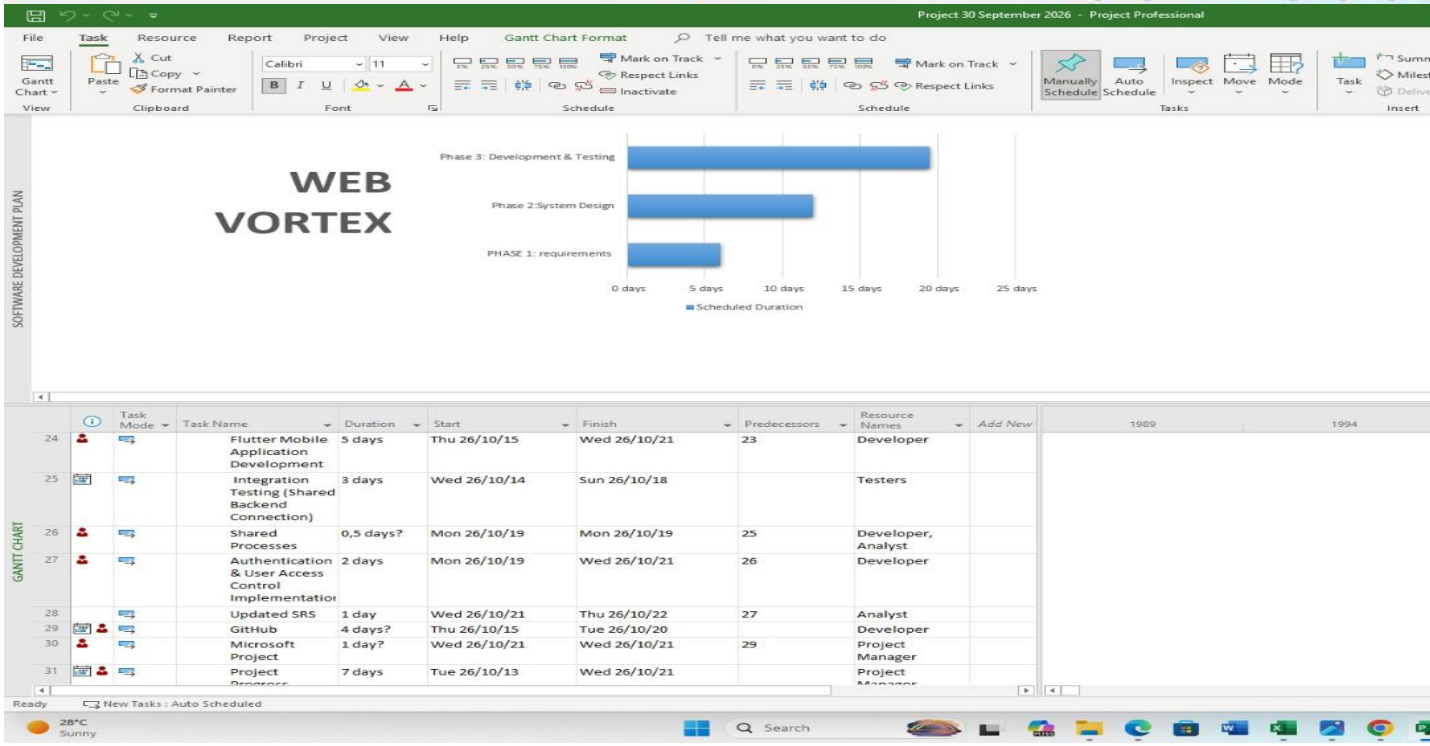
Signatures

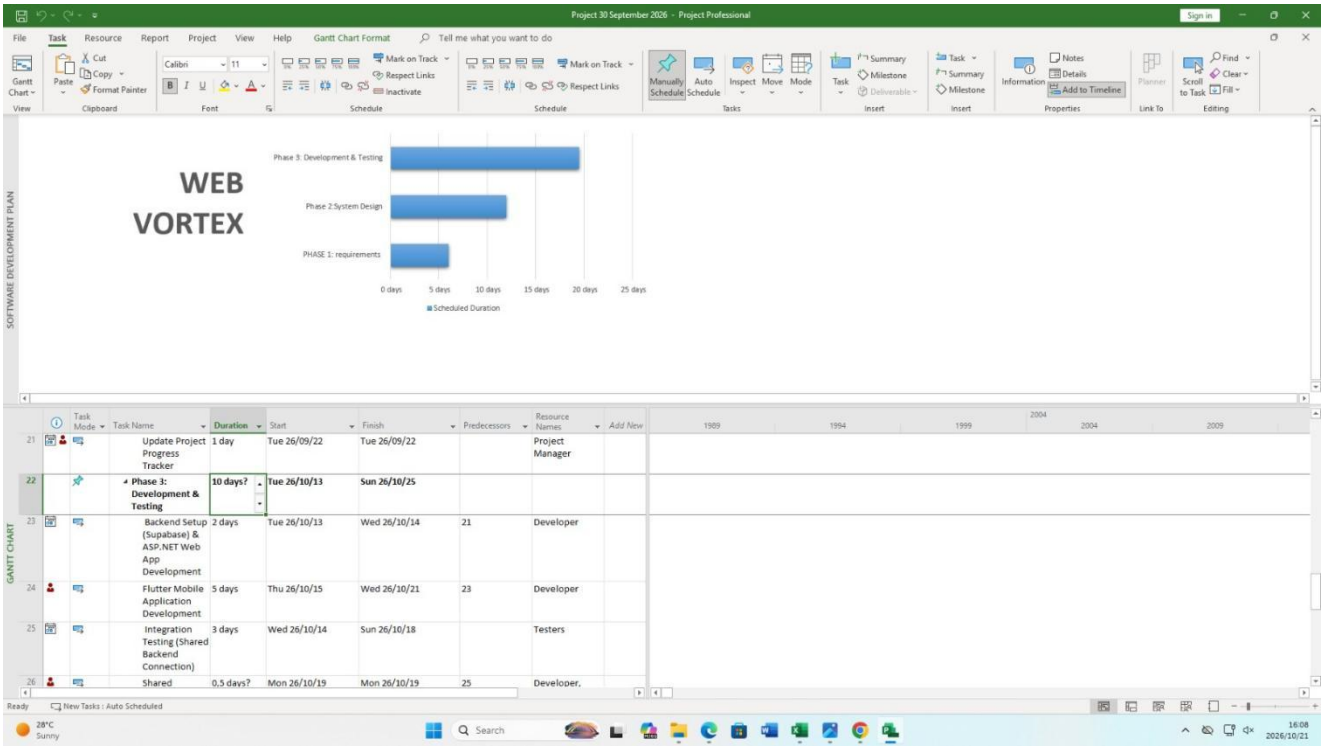
	Name	Signature/Student no.	Date
Stakeholder	Motlokoa Tsotesi (Owner, Mr Auto & Turbo)	T Motlokoa	21/10/2026

THE Microsoft Project is attached in the next page.


File
Task
Resource
Report
Project
View
Help
Gantt Chart Format
Tell me what you want to do
Gantt Chart
Paste
Cut
Copy
Format Painter
Calibri
11
Mark on Track
Respect Links
Inactivate
Manually Schedule
Auto Schedule
Inspect
Move
Mode
Task
WEB VORTEX
Phase 3: Development & Testing
Phase 2:System Design
PHASE 1: requirements
0 days
5 days
10 days
15 days
20 days
25 days
Scheduled Duration
SOFTWARE DEVELOPMENT PLAN


GANTT CHART
Task Mode
Task Name
Duration
Start
Finish
Predecessors
Resource Names
Add New
1989
1994
30 Microsoft Project 1 day? Wed 26/10/21 Wed 26/10/21 29 Project Manager
31 Project Progress Tracker 7 days Tue 26/10/13 Wed 26/10/21 Project Manager
32 Manual Testing, Problem Logging & Corrections 2 days Wed 26/10/14 Thu 26/10/15 Analyst
33 Stakeholder Prototype Evaluation & Feedback 3 hrs Wed 26/10/21 Wed 26/10/21 Management, Project Manager
34 Final Demonstration 0,5 days? Fri 26/10/23 Fri 26/10/23 33 Management, Project
35 Design complete 0 days Fri 26/10/23 Fri 26/10/23 34
Ready
New Tasks : Auto Scheduled
28°C
Sunny
Search


Project 30 September 2026 - Project Professional
File
Task
Resource
Report
Project
View
Help
Gantt Chart Format
Tell me what you want to do
WEB VORTEX
Phase 3: Development & Testing
Phase 2:System Design
PHASE 1: requirements
0 days
5 days
10 days
15 days
20 days
25 days
Scheduled Duration
SOFTWARE DEVELOPMENT PLAN
GANTT CHART
Task Mode
Task Name
Duration
Start
Finish
Predecessors
Resource Names
Add New
1989
1994
24 Flutter Mobile Application Development 5 days Thu 26/10/15 Wed 26/10/21 23 Developer
25 Integration Testing (Shared Backend Connection) 3 days Wed 26/10/14 Sun 26/10/18 Testers
26 Shared Processes 0,5 days? Mon 26/10/19 Mon 26/10/19 25 Developer, Analyst
27 Authentication & User Access Control Implementatio 2 days Mon 26/10/19 Wed 26/10/21 26 Developer
28 Updated SRS 1 day Wed 26/10/21 Thu 26/10/22 27 Analyst
29 GitHub 4 days? Thu 26/10/15 Tue 26/10/20 Developer
30 Microsoft Project 1 day? Wed 26/10/21 Wed 26/10/21 29 Project Manager
31 Project 7 days Tue 26/10/13 Wed 26/10/21 Project
Ready
New Tasks : Auto Scheduled
28°C
Sunny
Search



8. Outstanding Development Problems and Actions

Record only issues that the group actually identifies during its review. Assign an owner and a realistic status. If no issue remains after verification, write “None identified during final review” rather than leaving the section ambiguous.

Problem / outstanding task	Action required	Responsible member	Status
None identified during final review	No corrective action required.	N/A	N/A

9. Approved Changes and Known Limitations

Any approved changes to requirements, design, database structure, user permissions or workflow must be recorded here and reflected in the relevant parts of the existing SRS, diagrams and project records. Do not treat a development shortcut or unfinished feature as an approved requirement change.

Change / limitation	Reason and stakeholder/approval reference	Affected requirement/design	Action or current status
No approved changes recorded	Implementation follows the approved SRS and Phase 3 development	N/A	No action required
No known limitations identified during final review	N/A	N/A	N/A

10. Final Demonstration Plan

Before the assessment, prepare the following demonstration sequence using suitable dummy data.

- Launch the Flutter mobile application and demonstrate its main approved screens and functions.
- Launch the ASP.NET web application and demonstrate its main approved pages and functions.
- Show the shared Supabase project and demonstrate required records being saved, retrieved or updated.
- Demonstrate at least two cross-application processes, including repair-status tracking where implemented.
- Demonstrate role-appropriate access and explain any permissions that restrict users.
- Explain the current implementation state, outstanding work and known limitations honestly.
- Ensure development tools, network access, test accounts and dummy data are ready before the allocated presentation time.
- Capture suitable screenshots or short recordings of key functions and integrated processes as supporting evidence.

11. Project Records to Update

Project record	Required update / evidence	Status
Software Requirements Specification (SRS)	Phase 3 readiness, verified implementation state, approved changes and known limitations.	Verified
Microsoft Project	Update task progress and dependencies; retain the original editable .mpp file.	Verified
GitHub repository	Ensure the latest source code is committed, including the mobile/ and web/ folders as applicable.	Verified
Project Progress Tracker	Update Task Progress, Individual Contributions, Challenges and Actions, Phase Summary and Group Reflection.	Verified
Supporting evidence	Screenshots/short recordings of working functions and at least two integrated processes.	Verified

11. Final Assessment Readiness Checklist

- ☑ Shared Supabase backend implemented and checked against the approved ERD.
- ☑ Authentication and role permissions checked where required.
- ☑ Main Flutter screens and functions demonstrated.
- ☑ Main ASP.NET pages and functions demonstrated.
- ☑ Both applications use the same Supabase project.
- ☑ At least two important shared processes demonstrated across the applications.
- ☑ Implemented functions checked against the approved SRS.
- ☑ Outstanding tasks and limitations recorded and assigned.
- ☑ Approved implementation changes recorded in the SRS.
- ☑ Microsoft Project reflects current development progress and the editable file is retained.
- ☑ GitHub contains the latest mobile and web source code.

- [x] Project Progress Tracker is current and complete.
- [x] Group is prepared to present and explain the working prototype.

12. Phase 3 Completion Statement

The group should complete this statement after reviewing the evidence: “We have reviewed the current implementation of the Mr Auto & Turbo Workshop Management System against the approved SRS and Phase 2 design. The working functions, cross-application integration evidence, outstanding tasks and known limitations are recorded in this Phase 3 section. Our final demonstration will reflect the actual state of the prototype.”

Group names LE Letsie | LE Lipali | LTBG Pule | NM Netshituka | RG Madi

Date reviewed: _____21/10/2026_____
